PRINCE2®

PRINCE2® Project Management Foundation

PeopleCert

Official Training Materials

General information



Copyright © 2025 PeopleCert International Limited.

Introductions

Getting to know you


- Name
- Reason for attending
- Job role
- Course Objectives



Copyright © 2025 PeopleCert International Limited.

Official Book

Do not forget to use the **Official Book** for more detailed information on the modules presented.

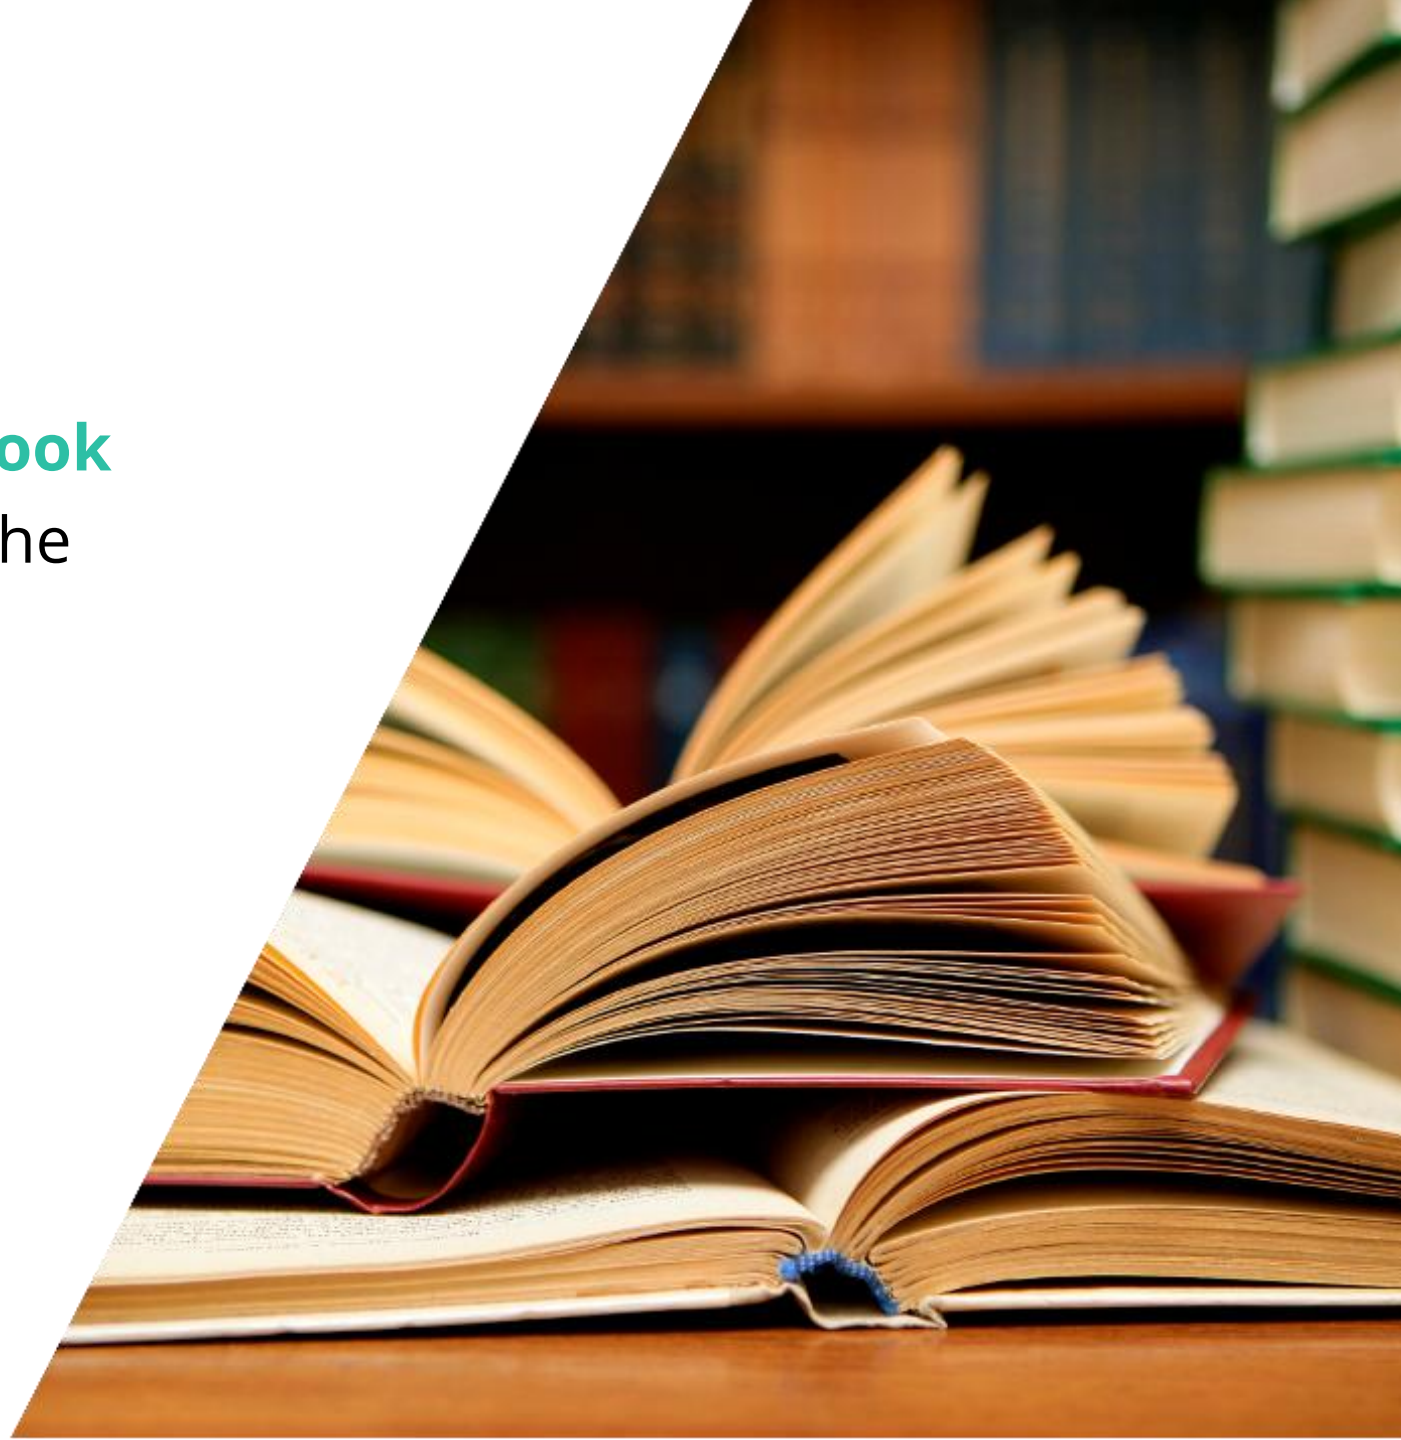


Copyright © 2025 PeopleCert International Limited.

Exam information

The PRINCE2® Project Management Foundation exam specifications are:

- closed book
- 60 minutes
- 60 questions
- 60% pass mark (36/60)
- multiple choice.

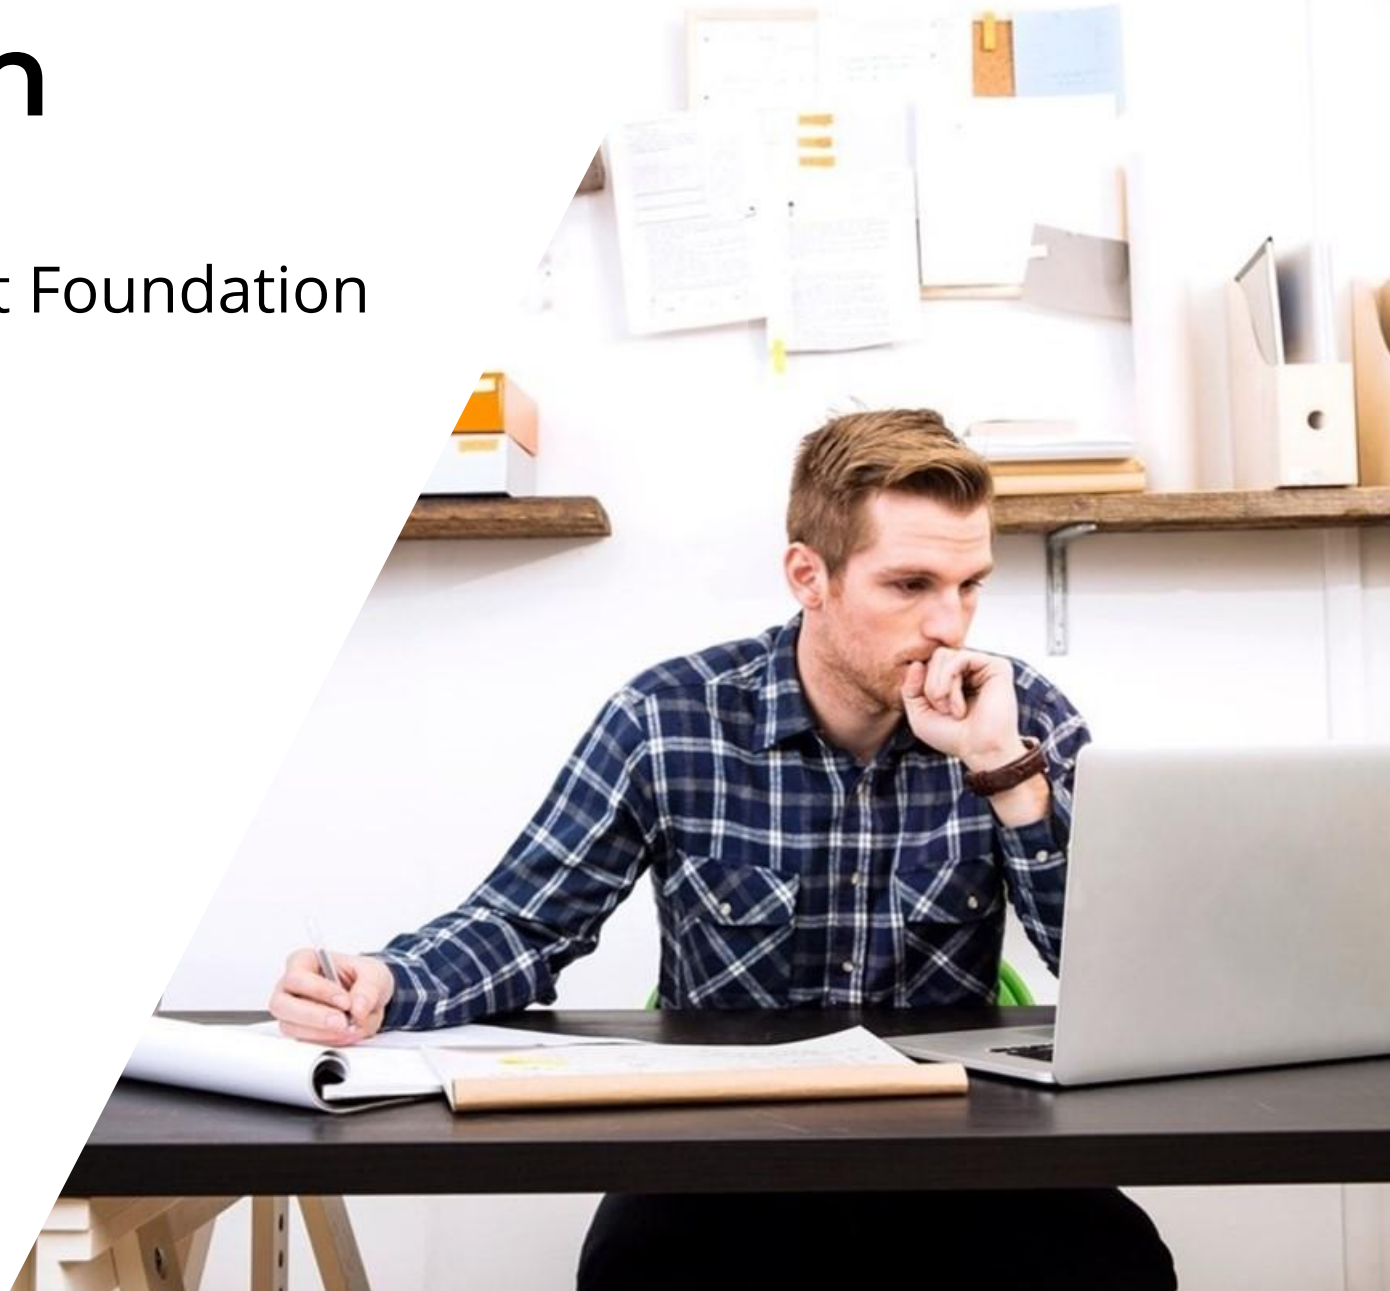

Copyright © 2025 PeopleCert International Limited.

Course modules

- Overview of PRINCE2® Project Management
- People
- Organization
- Starting up and initiating a project
- Business case
- Plans
- Quality
- Risk
- Controlling a stage and managing product delivery
- Managing a stage boundary
- Issues
- Progress
- Closing a project
- Directing a project
- Course review



Copyright © 2025 PeopleCert International Limited.

10 minutes




Introduction

Activity

What makes a good project? (1/2)

10 minutes

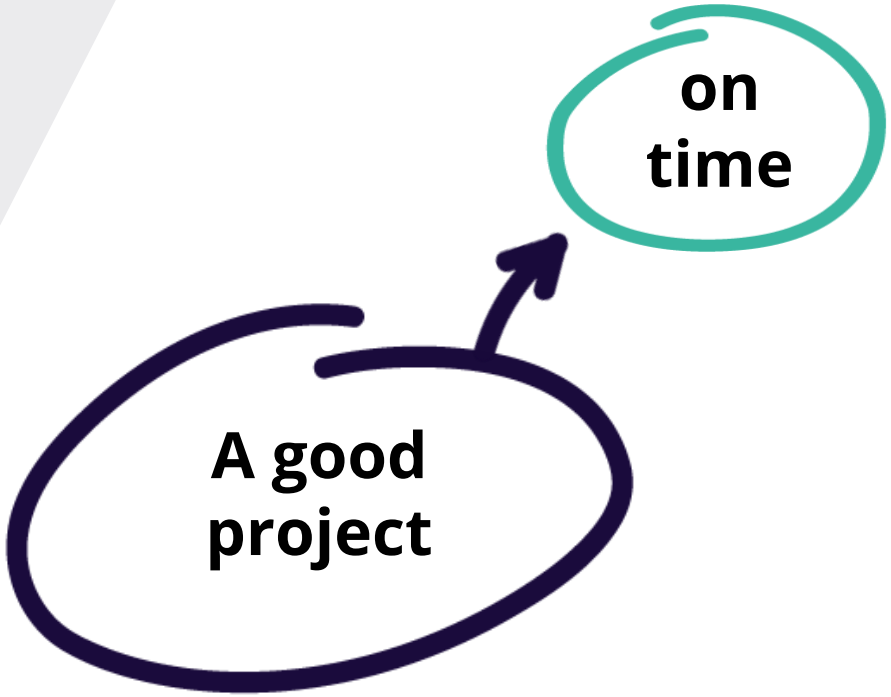



Use your Learner Workbook to note down your ideas.

Copyright © 2025 PeopleCert International Limited.

What makes a good project? (2/2)





Copyright © 2025 PeopleCert International Limited.

Module 1

Overview of PRINCE2® Project Management

Characteristics of a project

cross-functional

change

PROJECT

uncertainty

unique

temporary



Copyright © 2025 PeopleCert International Limited.

What is a project?

A **temporary organization** that is created for the **purpose of delivering** one or more **business products** according to an agreed **business case**.



Copyright © 2025 PeopleCert International Limited.

Topics not included in PRINCE2 Project Management

specialist aspects

detailed techniques



Copyright © 2025 PeopleCert International Limited.

The five integrated elements

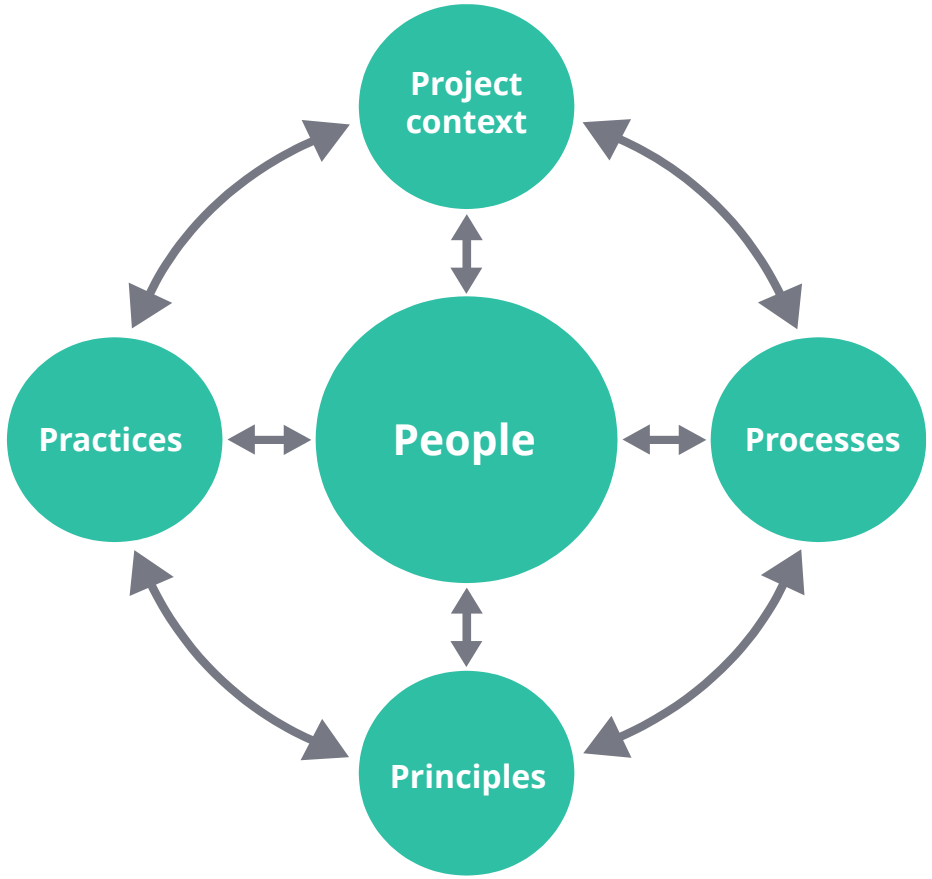


Figure 1.1 The five integrated elements of PRINCE2 Project Management

Copyright © 2025 PeopleCert International Limited.

Features and benefits of PRINCE2 Project Management


- Universal
- Common language and concepts
- Increased organizational maturity
- Proven
- Flexible
- Outcome-focused
- Part of an integrated suite of methods



Copyright © 2025 PeopleCert International Limited.


Project management

The application of methods, tools, techniques, and competencies

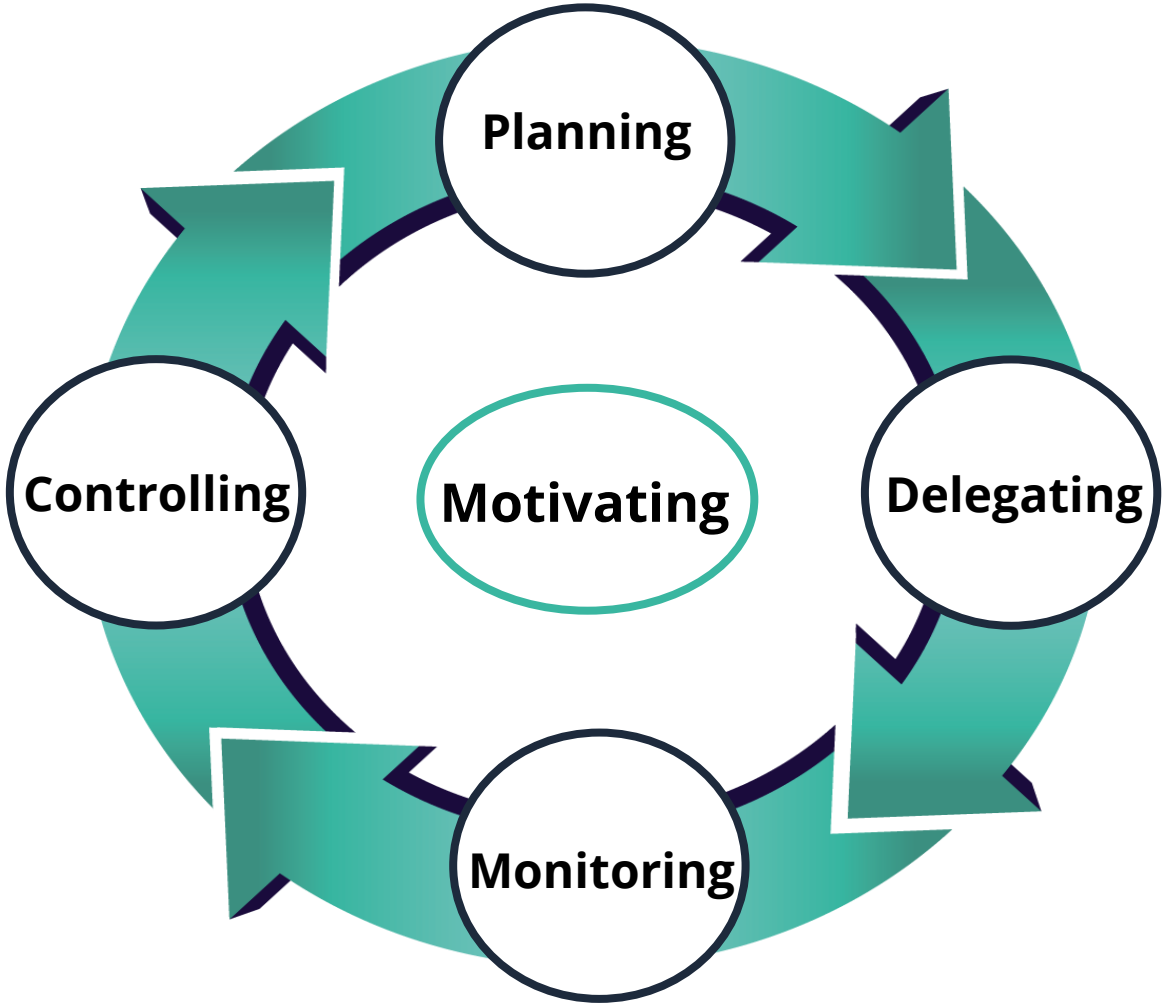

Copyright © 2025 PeopleCert International Limited.

Aspects of project performance

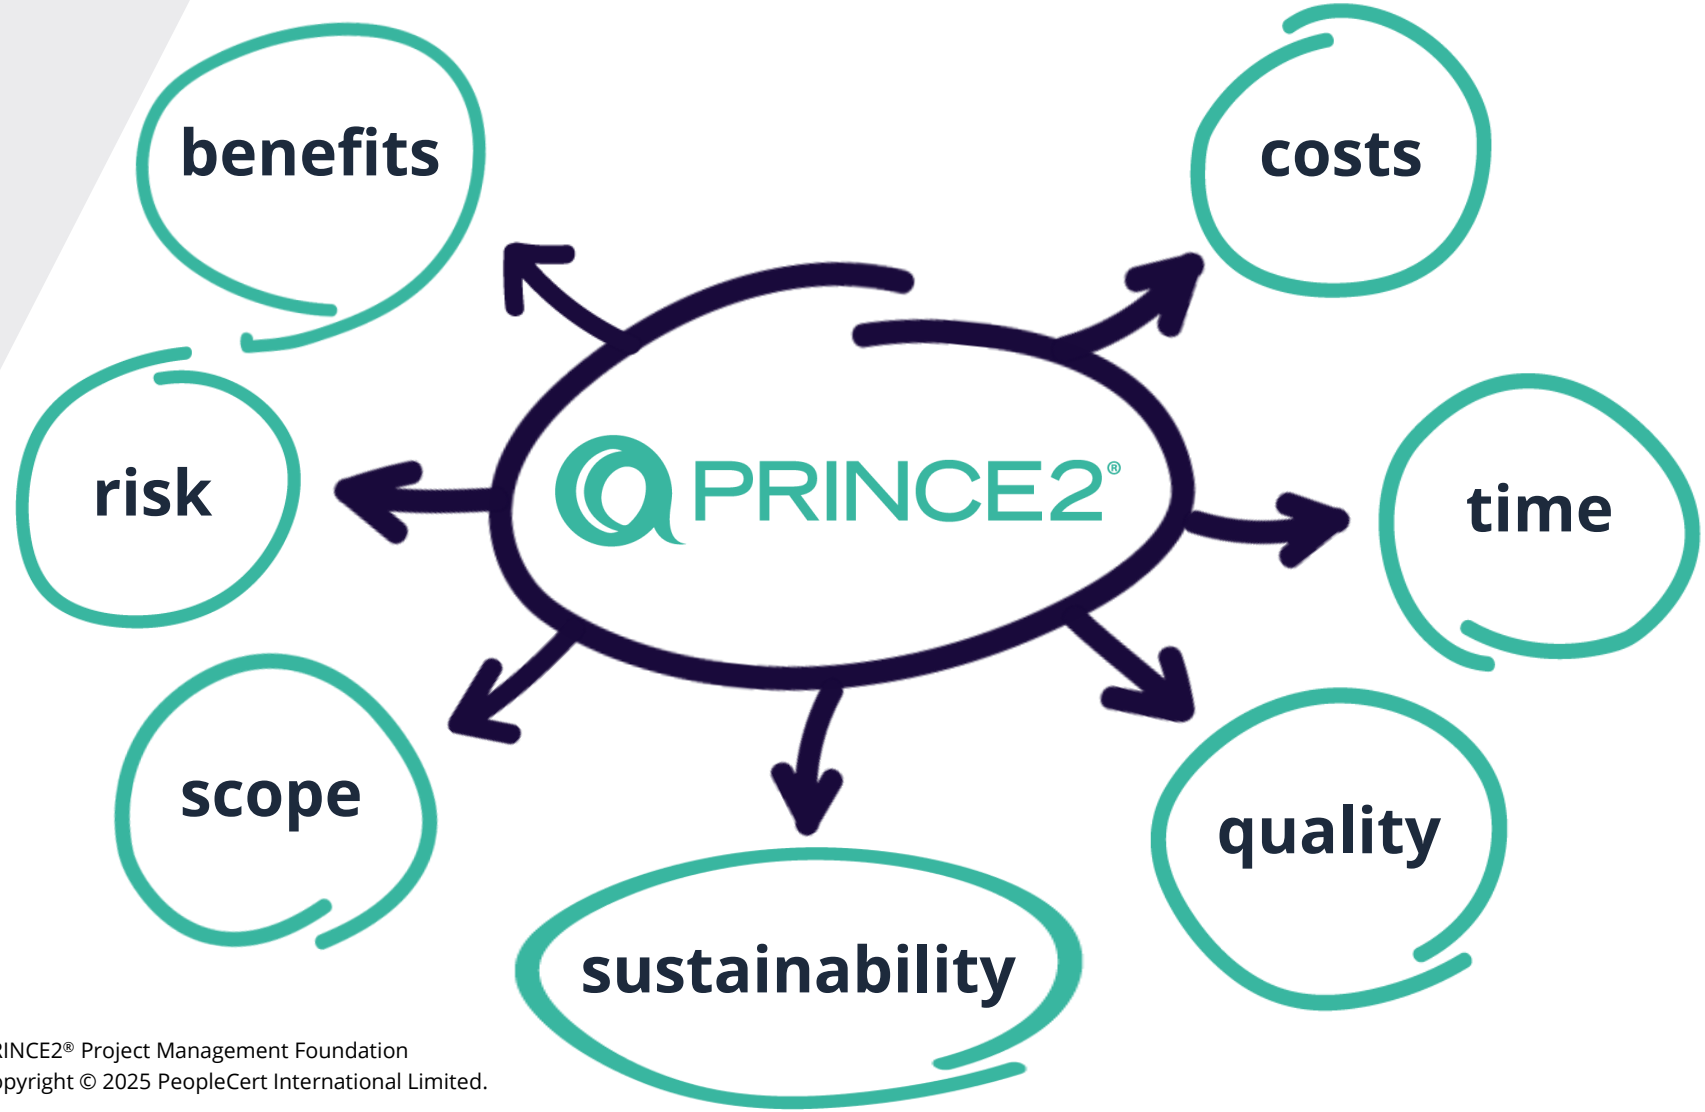

Copyright © 2025 PeopleCert International Limited.

Exploring the five integrated elements

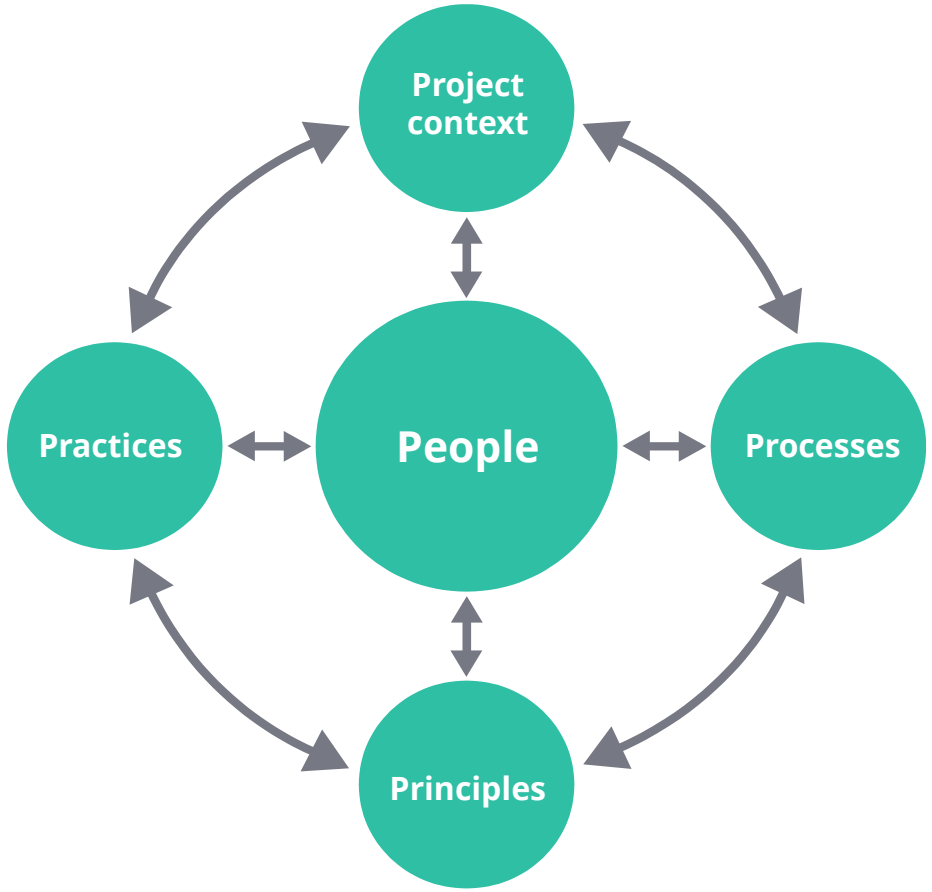


Figure 1.1 The five integrated elements of PRINCE2 Project Management

Copyright © 2025 PeopleCert International Limited.

Project context

Organizational context

Delivery method

Scale

Commercial context

Sustainability



Copyright © 2025 PeopleCert International Limited.

Users, suppliers, and business

PRINCE2 Project Management projects must have:



A **user** who will **specify** the **desired outputs.**



A **supplier** who will provide the **resources** and **expertise** to **deliver the products.**



The **business** provides the **project mandate** and **structure** for project governance.



Copyright © 2025 PeopleCert International Limited.

Organizational context

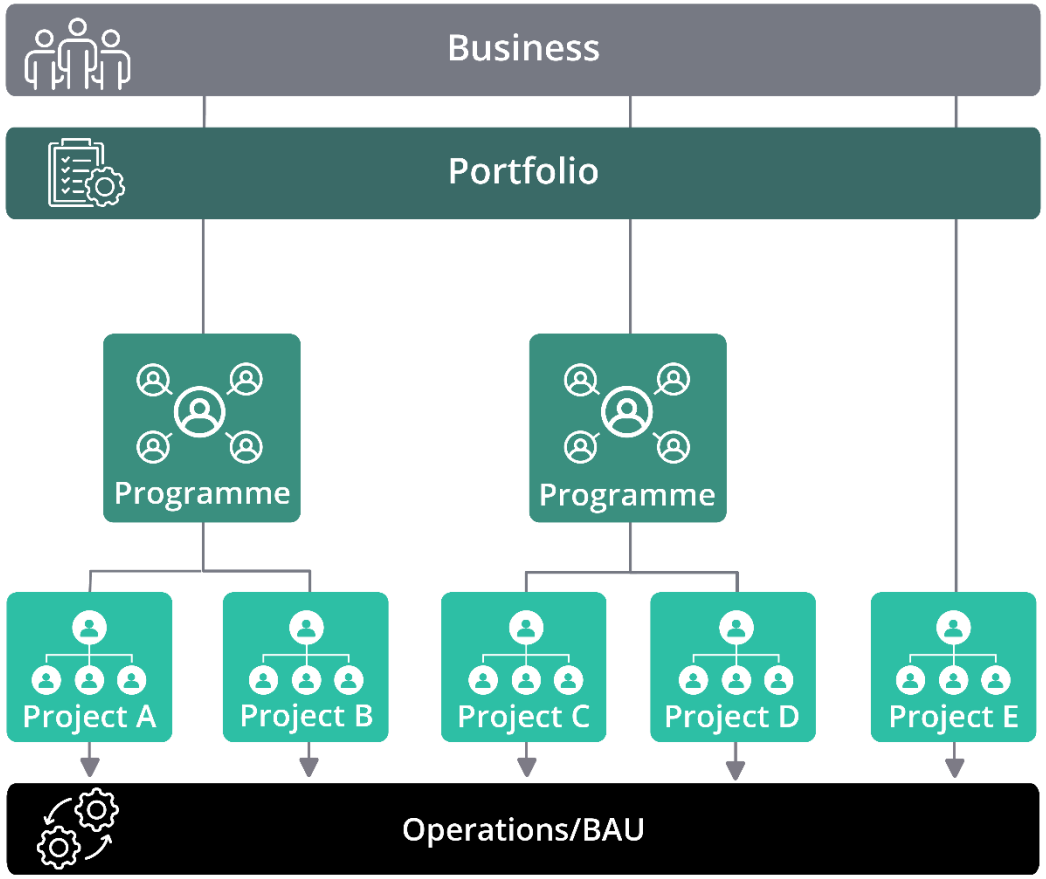


Figure 1.2 Projects within organizational context




Copyright © 2025 PeopleCert International Limited.


Delivery methods



Linear-sequential approach: steps occur in sequence and the product is available during or at the end of the project.




Iterative-incremental approach: steps occur iteratively throughout the project. Also referred to as the agile approach.



Hybrid approach: different elements of the project use either of the two approaches.

Copyright © 2025 PeopleCert International Limited.

People in PRINCE2 Project Management

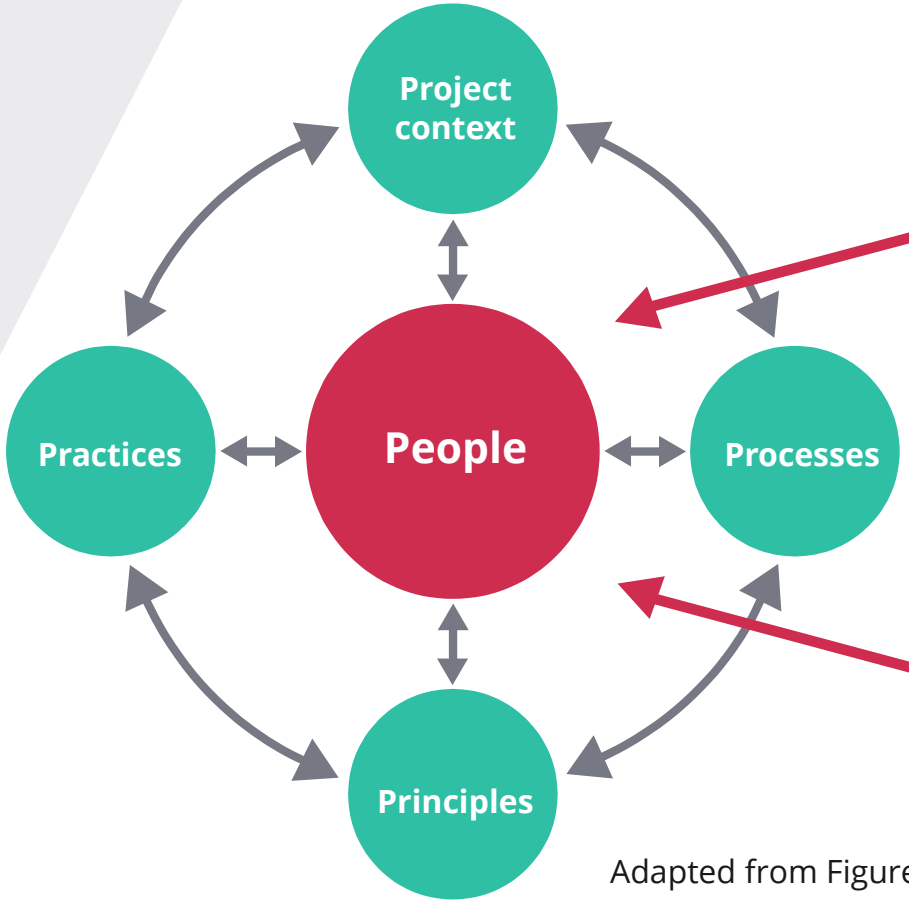

Those working on the project





Those affected by the project

Adapted from Figure 1.1 The five integrated elements of PRINCE2 Project Management

Copyright © 2025 PeopleCert International Limited.

PRINCE2 Project Management principles

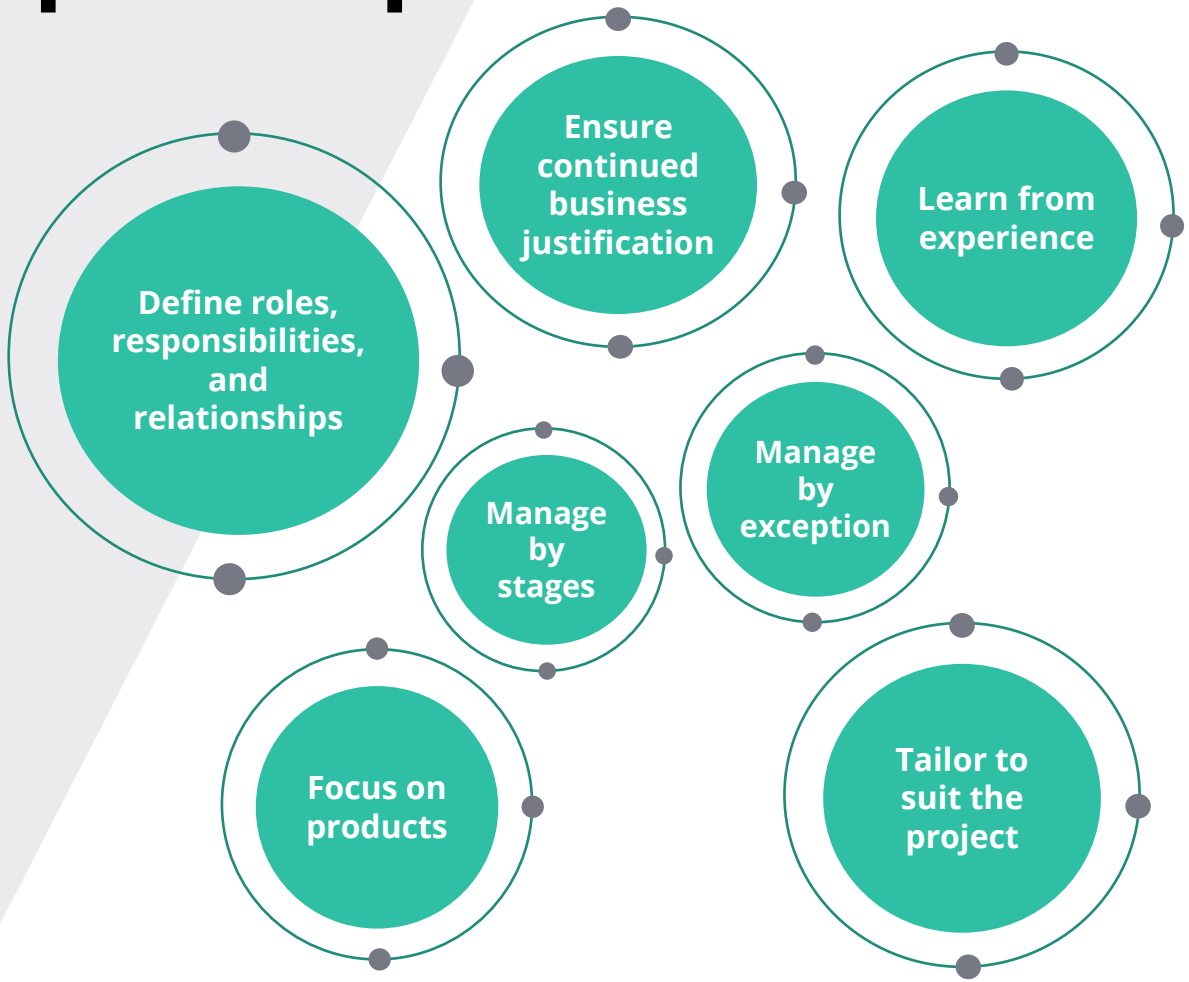


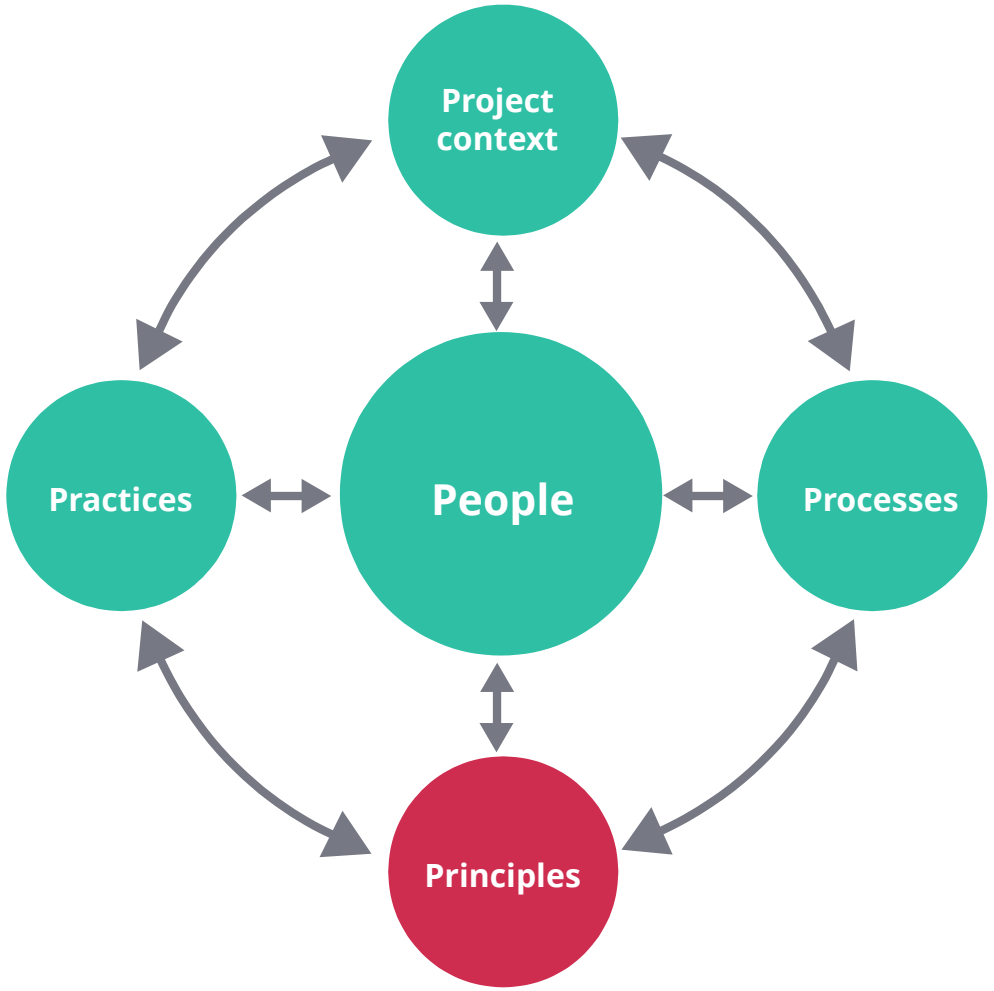


Adapted from Figure 1.1 The five integrated elements of PRINCE2 Project Management

Copyright © 2025 PeopleCert International Limited.

PRINCE2 Project Management practices

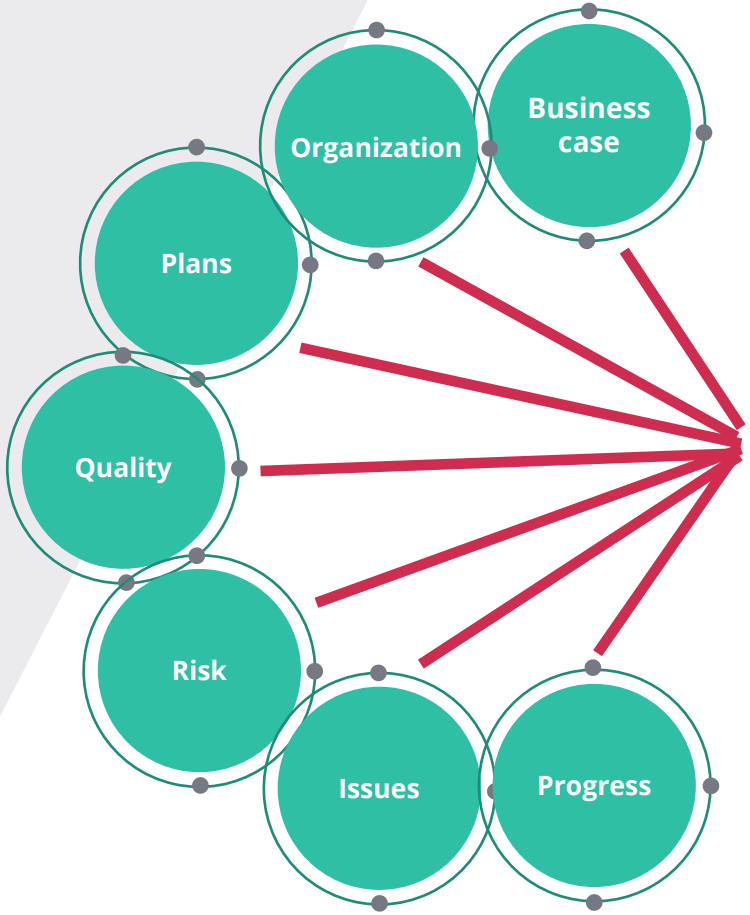

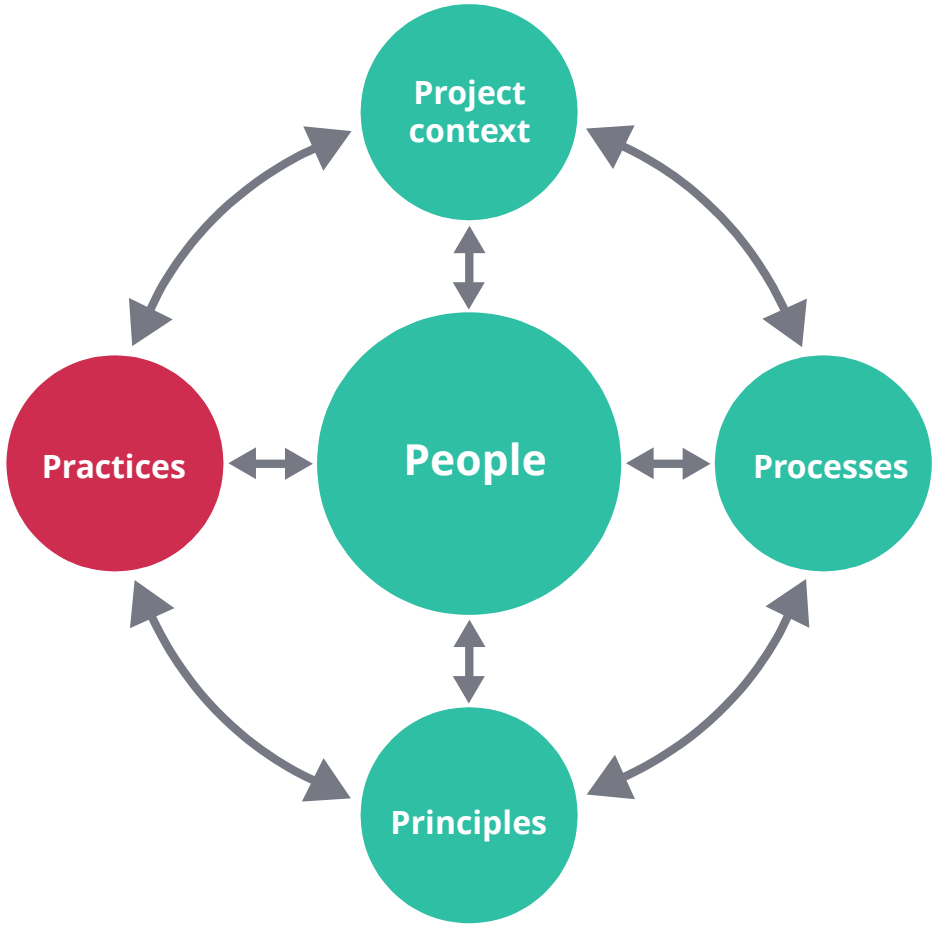


Adapted from Figure 1.1 The five integrated elements of PRINCE2 Project Management

Copyright © 2025 PeopleCert International Limited.

PRINCE2 Project Management processes

A **process-based approach** for project management

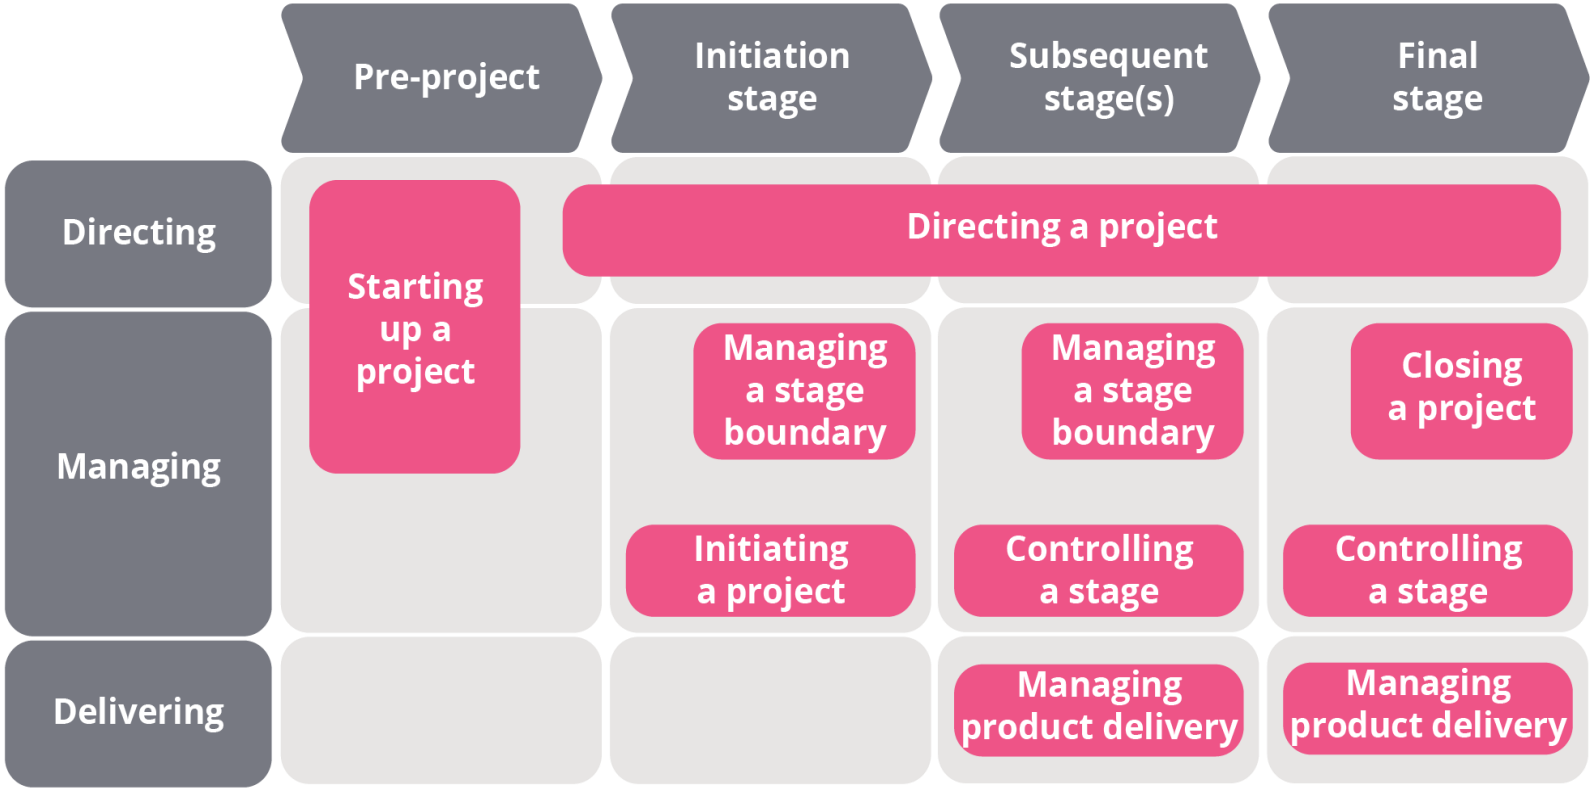

Note

- Starting up a project is used by both the directing and managing levels.
- There should be at least two stages, the first of which is the initiation stage.
- Managing a stage boundary is first used at the end of the initiation stage and repeated at the end of each subsequent stage except the final stage. It is also used to prepare exception plans, which can be done at any time including in the final stage.

Copyright © 2025 PeopleCert International Limited.

Figure 12.1 The PRINCE2 Project Management processes

Process diagrams

Managing a stage boundary

This is a PRINCE2 Project Management process. Each process contains a number of activities.


Assess previous lessons

This is an activity within a PRINCE2 Project Management process. Each activity contains a number of actions.

Project initiation request

This is an event or decision that triggers a PRINCE2 Project Management process. The direction of the arrow indicates which process is being triggered. Where the arrow goes to the business layer, it serves to notify the business of an update or request. Double triggers indicate that there are alternative triggers for a process.

Figure 12.3 Key to process diagrams

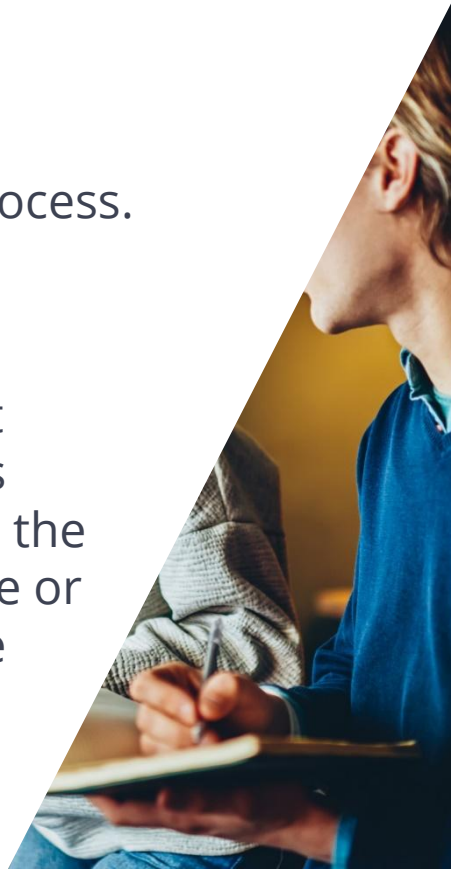

Copyright © 2025 PeopleCert International Limited.

The PRINCE2 Project Management journey

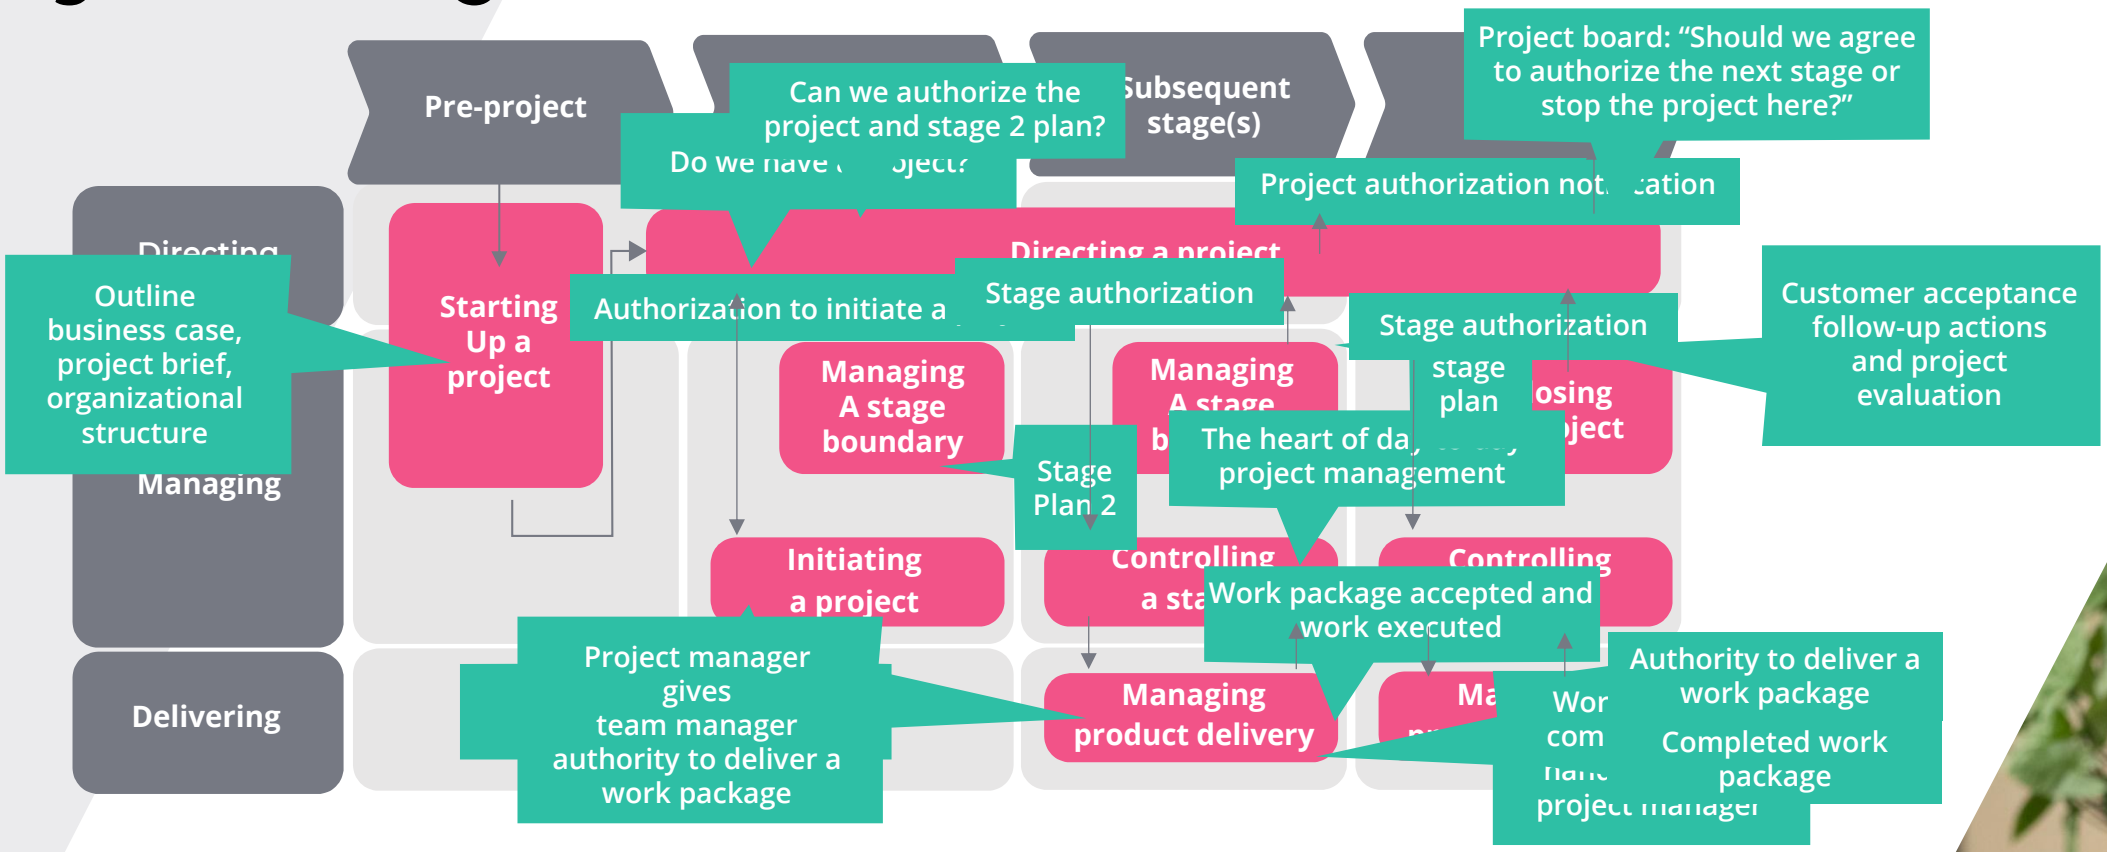


Figure 12.1 The PRINCE2 Project Management processes

Copyright © 2025 PeopleCert International Limited.

Tailoring a project

The purpose of tailoring is to ensure that:

- the project management method used is appropriate to the project
- project controls are appropriate to the project's scale, complexity, importance, team capability, and level of risk.



Copyright © 2025 PeopleCert International Limited.

Applying and tailoring PRINCE2 Project Management

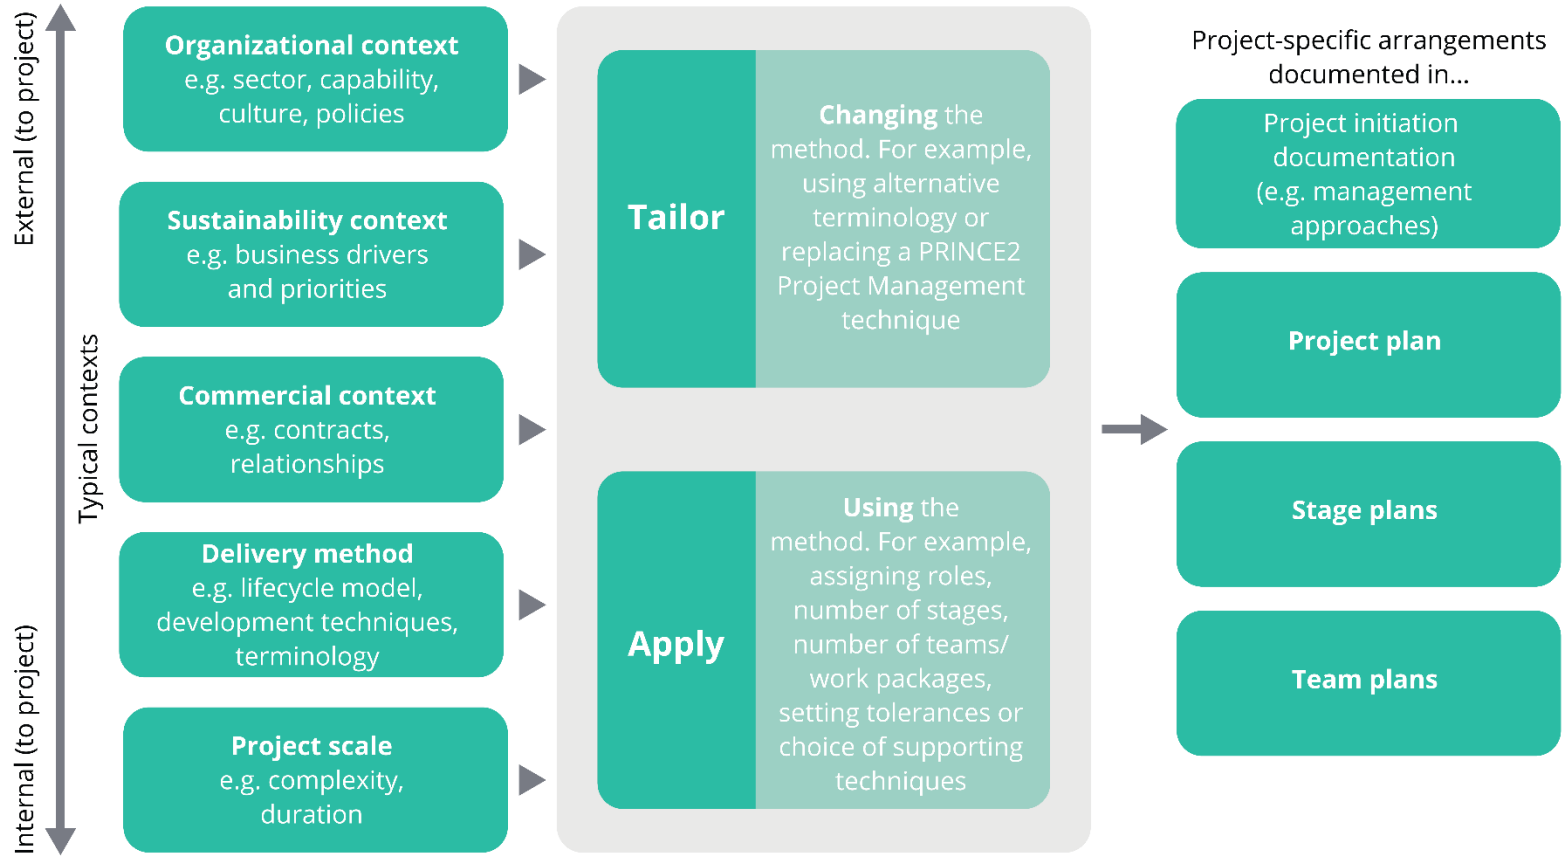


Figure 2.1 How to apply and tailor PRINCE2 Project Management to a project

Copyright © 2025 PeopleCert International Limited.

Tailoring example

Simple two-stage project



- project mandate sent by email
- simple PID
- one log for risks, issues, lessons
- verbal highlight and checkpoint reports
- no stage plans, work packages, team plans, end of stage reports or issue reports.

Copyright © 2025 PeopleCert International Limited.

Module 2

People

The ‘people’ context

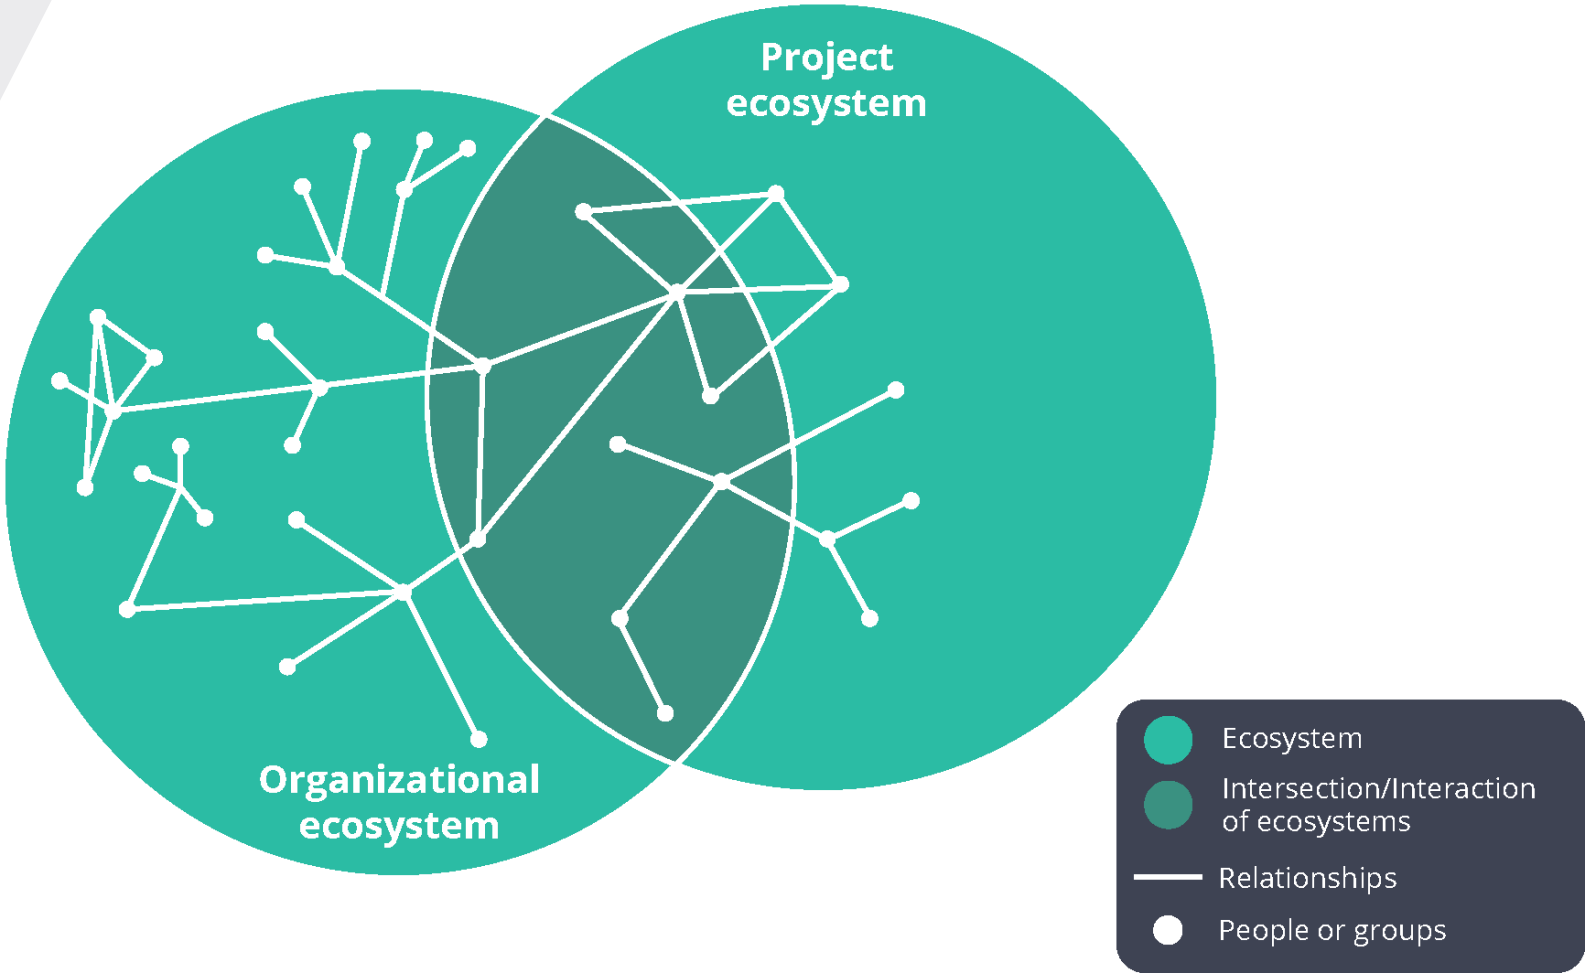


Figure 3.1 Organizational and project ecosystems

Copyright © 2025 PeopleCert International Limited.

People are central



Figure 3.3 People central to the method

Copyright © 2025 PeopleCert International Limited.

Leading successful change



Copyright © 2025 PeopleCert International Limited.

Change management approach

To establish the **target organizational state** required for the project to meet its objectives together with the **means** by which the business will **shift from the current state** and through any interim states.



Copyright © 2025 PeopleCert International Limited.

What is a stakeholder?

Any **individual, group** or **organization** that **can affect, be affected by,** or **perceive** itself to be affected by, the **project.**



Copyright © 2025 PeopleCert International Limited.

Stakeholders


Which of these could be a stakeholder?



- Senior executives ✓
- The end user ✓
- The supplier ✓

Copyright © 2025 PeopleCert International Limited.

Possible stakeholders

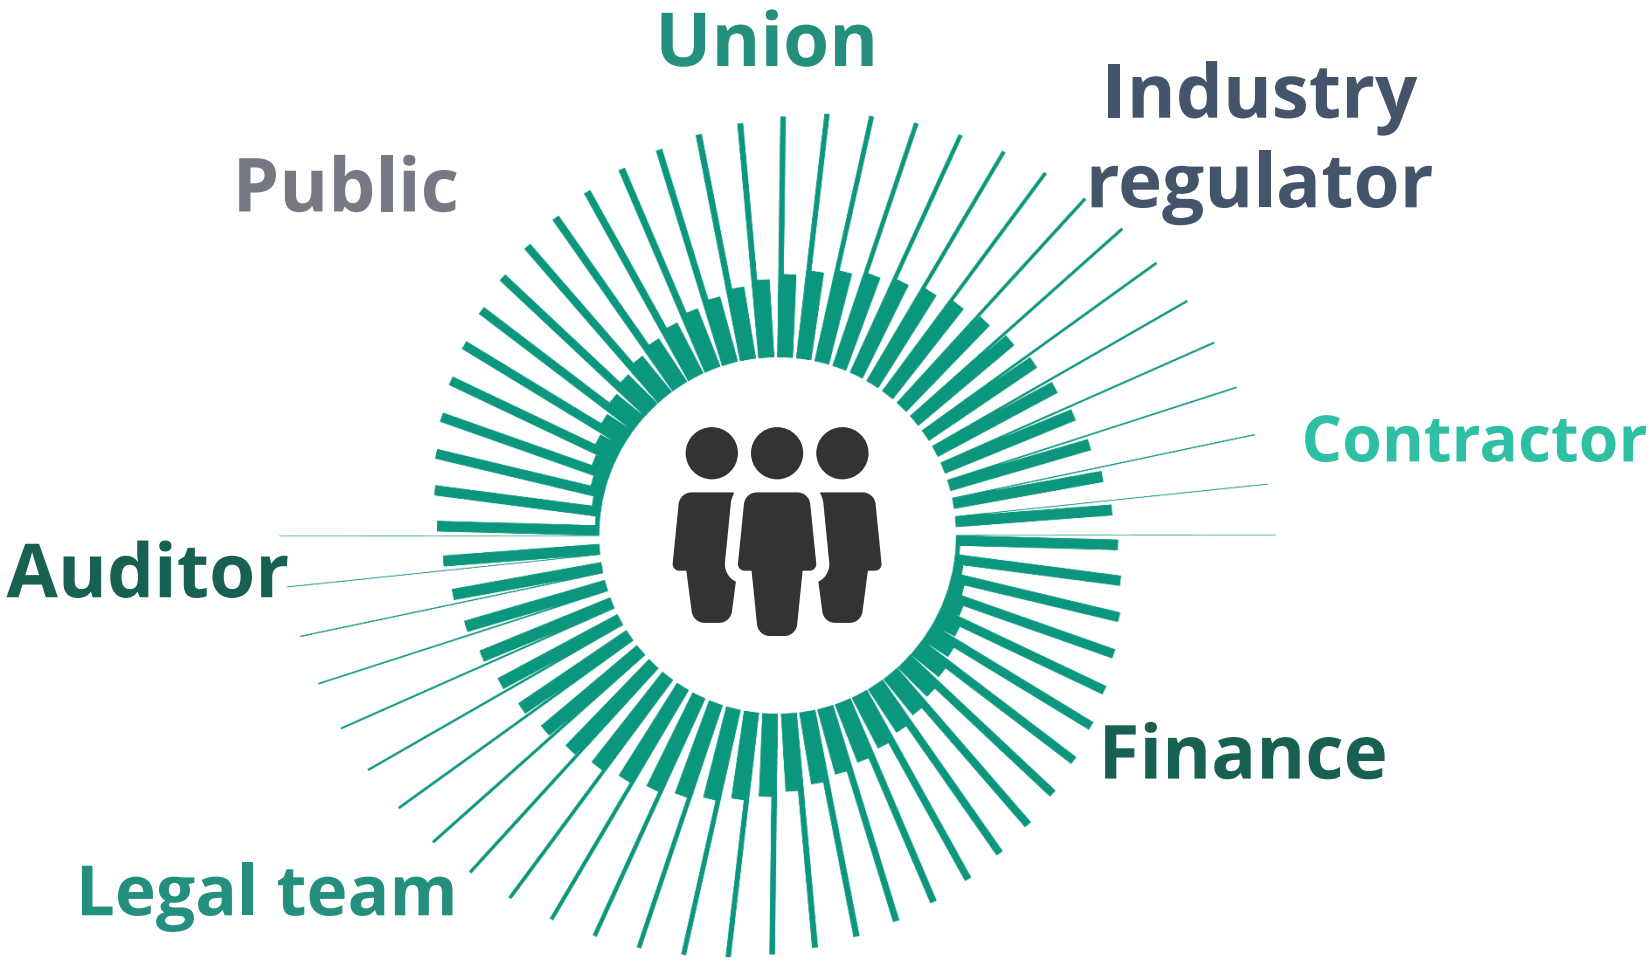

Copyright © 2025 PeopleCert International Limited.

Stakeholder buy-in

Stakeholders may...

support or oppose the project

gain or lose as a result of project delivery

see the project as a threat or enhancement to their position

become active supporters or blockers of the project and its progress.




Copyright © 2025 PeopleCert International Limited.

Project culture

Culture is the set of shared attitudes, values, goals, and ways of working that characterize a group of people.

A project culture may be **distinct** from the business but **aligned** with the wider ecosystem.


Shared understanding must be developed with **key influencers** to establish **ways of working,** align behaviours and set the culture.

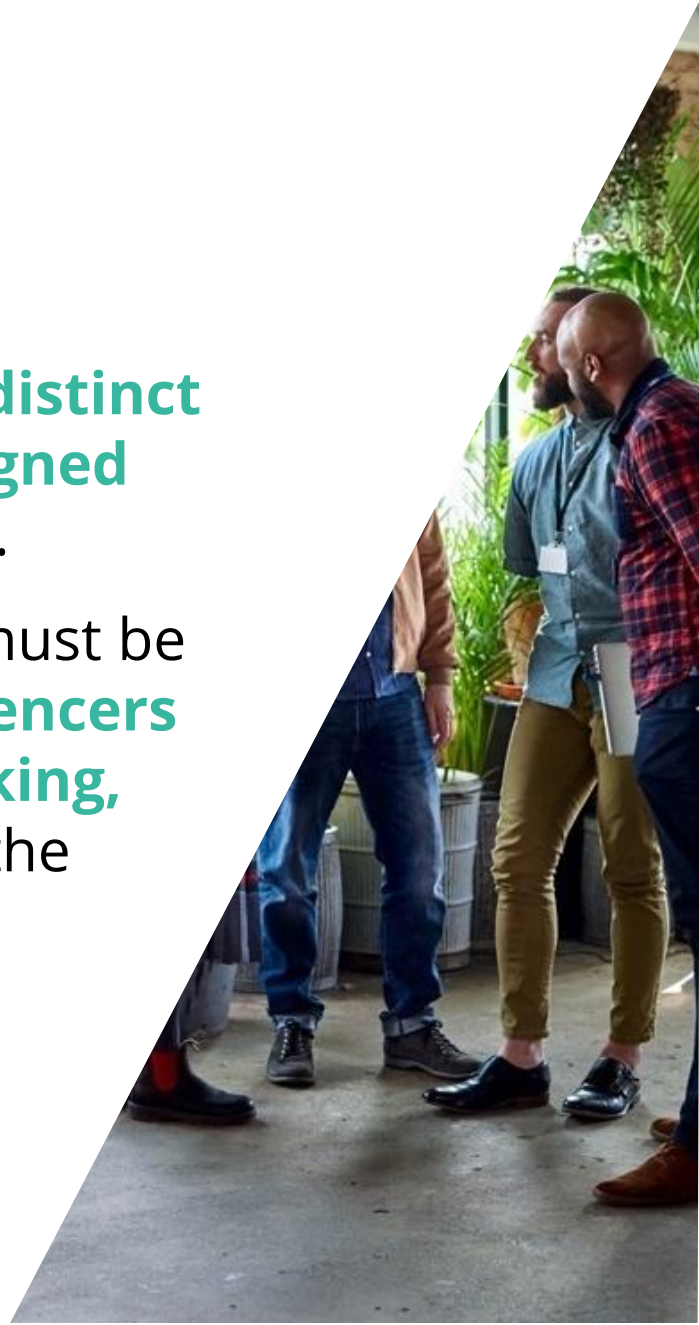

Copyright © 2025 PeopleCert International Limited.

Leading successful teams (1/2)

What are the challenges in leading a project team?

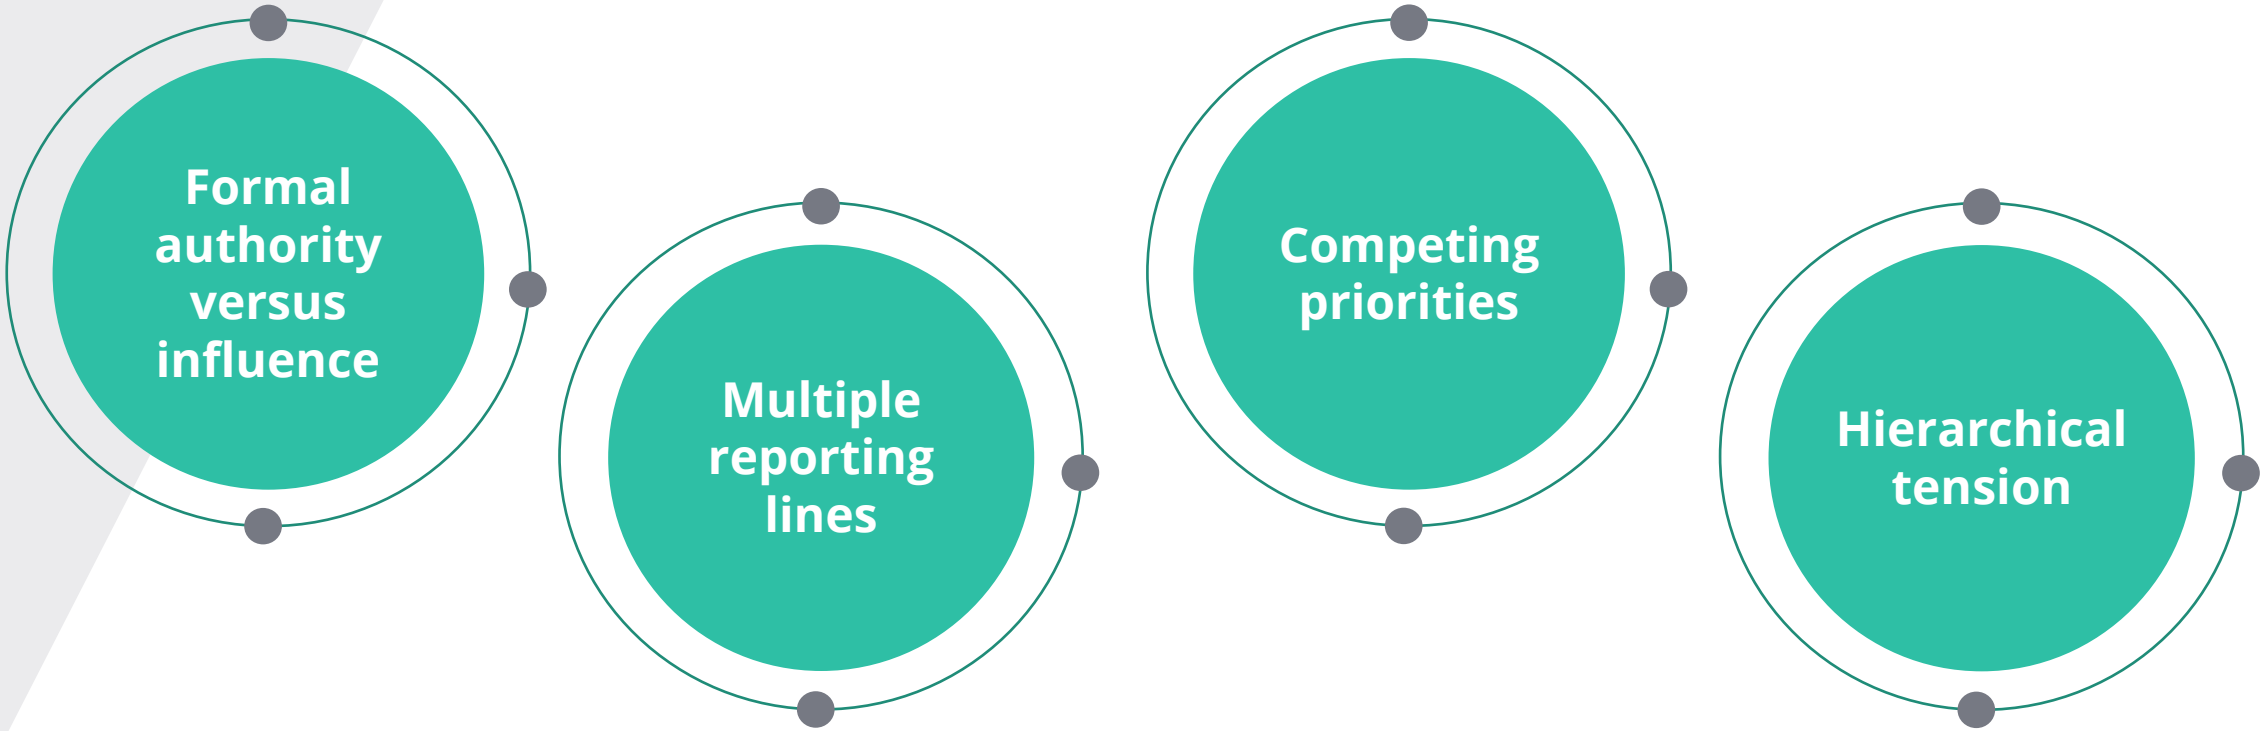

Copyright © 2025 PeopleCert International Limited.

Leadership versus management



Activity	Leadership	Management
Developing a common understanding of the project objectives and ways of working	✓	
Explaining how a specific task needs to be executed		✓
Following up on completion of an activity		✓
Gathering project team members to agree ways of working	✓	
Eliciting feedback to confirm alignment and commitment	✓	

Copyright © 2025 PeopleCert International Limited.

Leading successful teams (2/2)



Leadership

Motivating people to achieve a project's objectives.



Collaboration

People from across the project ecosystem working together to achieve the project's objectives.



Co-creation

A specific form of collaboration involving users and key influencers in the design of products and agreed ways of working to ensure they are adopted by the project and organizational ecosystems.



Management

Instructing the execution of tasks in line with agreed ways of working.

Copyright © 2025 PeopleCert International Limited.

Building the team

Competencies and capability

Understand, identify and mitigate gaps.

PRINCE2 Project Management support

Five key management products support building effective teams.



Different perspectives

Exercises to build self-awareness, trust and ways of working.

Culture

Acceptance, respect and psychological safety.


Roles and responsibilities

Reflect capability, authority, and availability and consider key relationships.

Copyright © 2025 PeopleCert International Limited.

Bringing the team together

How do you build social cohesion, particularly when teams are virtual?

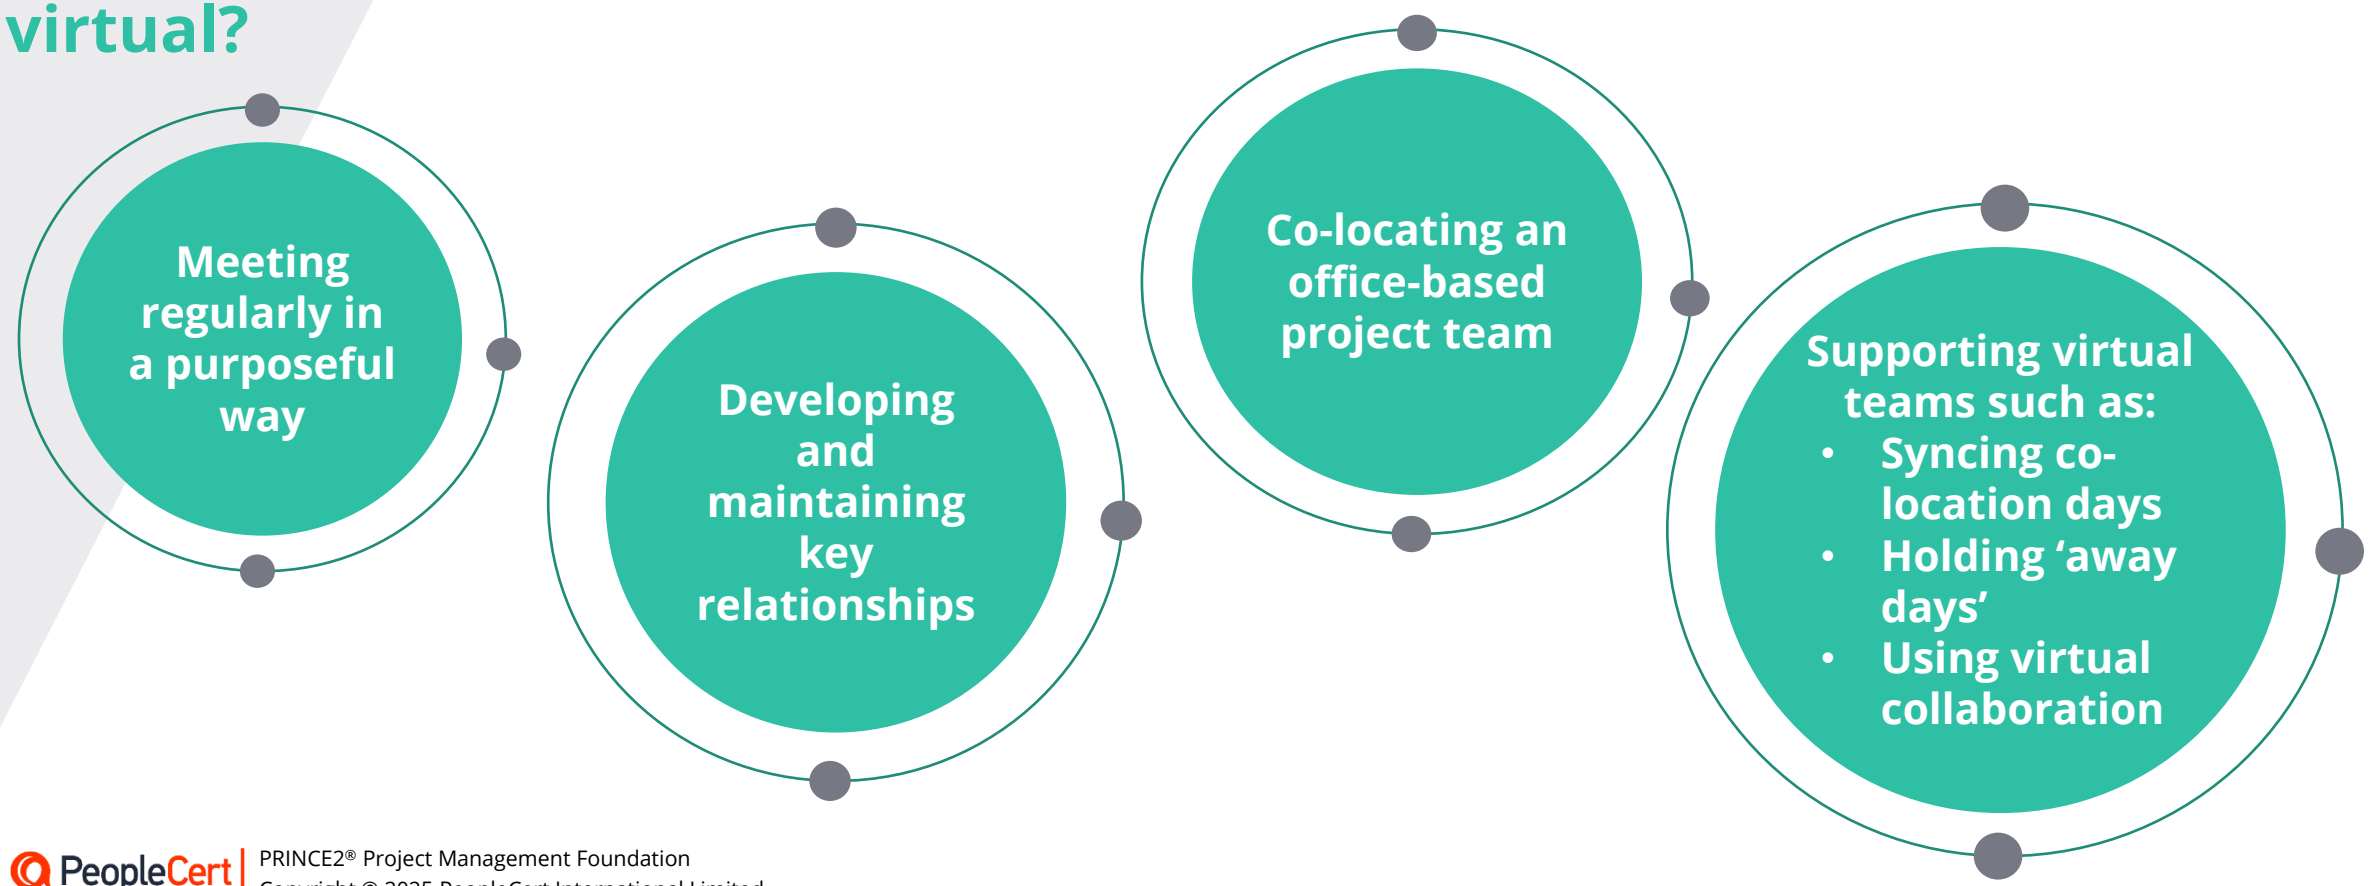

Copyright © 2025 PeopleCert International Limited.

The communication management approach



Defines and describes the **means** and **frequency** of communication with and receiving of feedback from across the project ecosystem.

The **project manager is responsible** for documenting the communication management approach during the ‘initiating a project’ process.



Copyright © 2025 PeopleCert International Limited.

Using the communication management approach

Where would you record the communication management approach?


- a stand-alone product or a section of the Project Initiation Documentation (PID)
- a document, spreadsheet, or mind map
- an entry in a project management tool.



Copyright © 2025 PeopleCert International Limited.

People are central to the PRINCE2 Project Management method

People factors are represented in all practices, with a focus on the ‘organization’ practice.

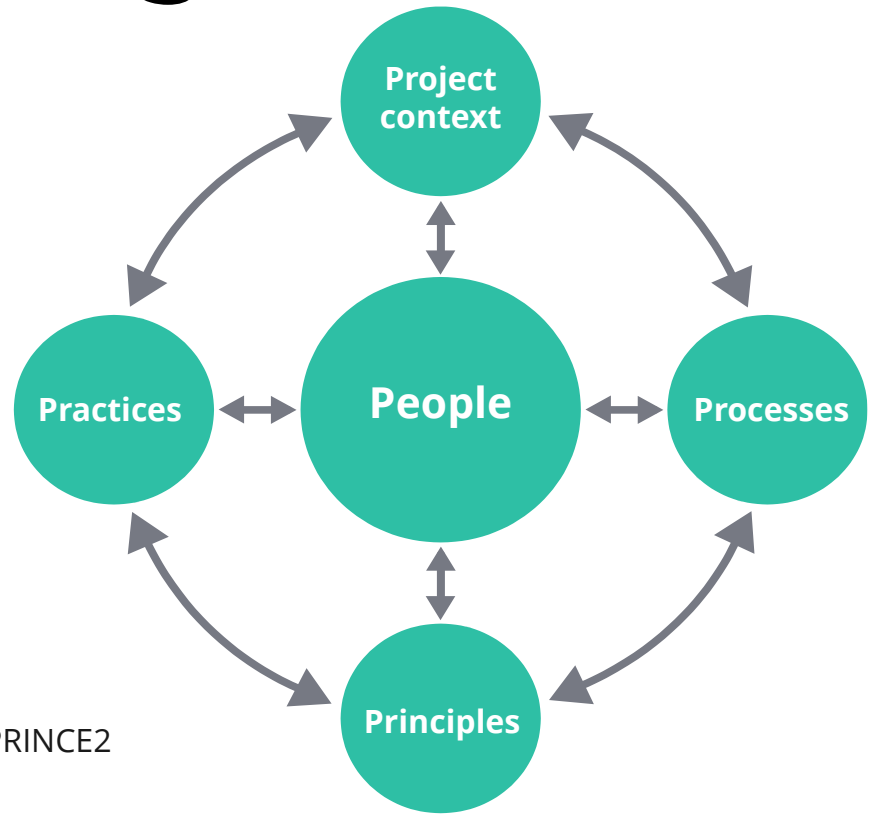

People interface between the four layers into which processes are organized.

Figure 1.1 The five integrated elements of PRINCE2 Project Management

People factors permeate all principles, particularly roles, responsibilities and relationships.

Copyright © 2025 PeopleCert International Limited.

20 minutes

People

Activity 1

Project stakeholders

20 minutes

Look at the potential NowByou stakeholders in the scenario.

Which stakeholders would you consider to be influential because they are at the interface between the two ecosystems?



Use your Learner Workbook to note down your ideas.

Copyright © 2025 PeopleCert International Limited.

Key stakeholders




Stakeholder	Influential?	Reason for the influence

Copyright © 2025 PeopleCert International Limited.

Module 3

Organization


The integrated elements of PRINCE2 Project Management

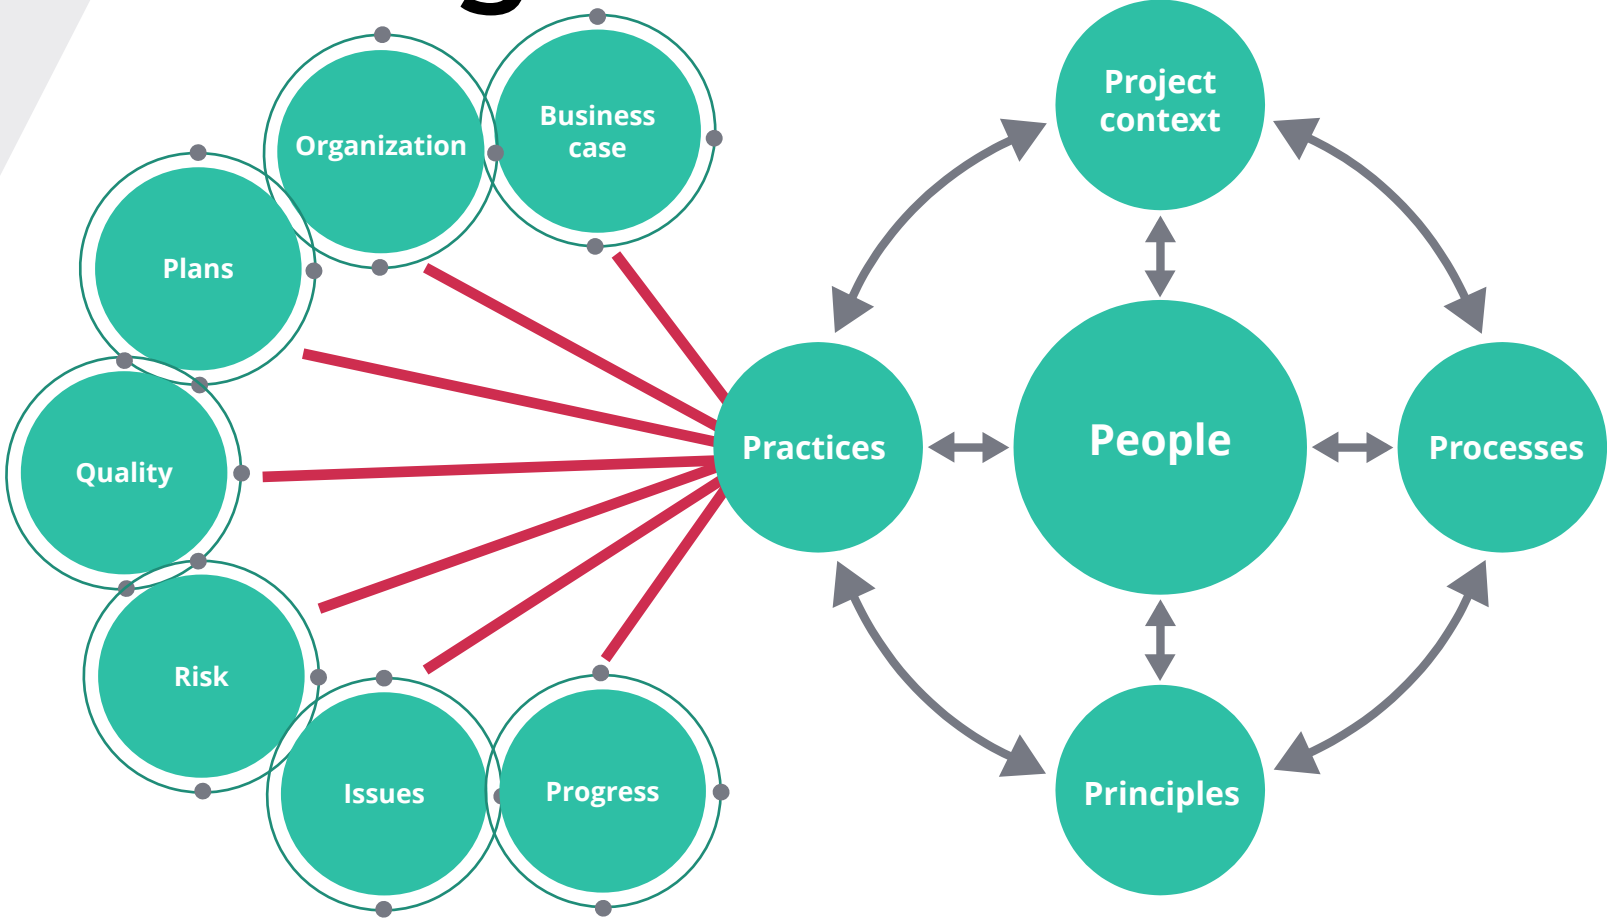

Adapted from Figure 1.1 The five integrated elements of PRINCE2 Project Management

Copyright © 2025 PeopleCert International Limited.

Applying the PRINCE2 Project Management practices

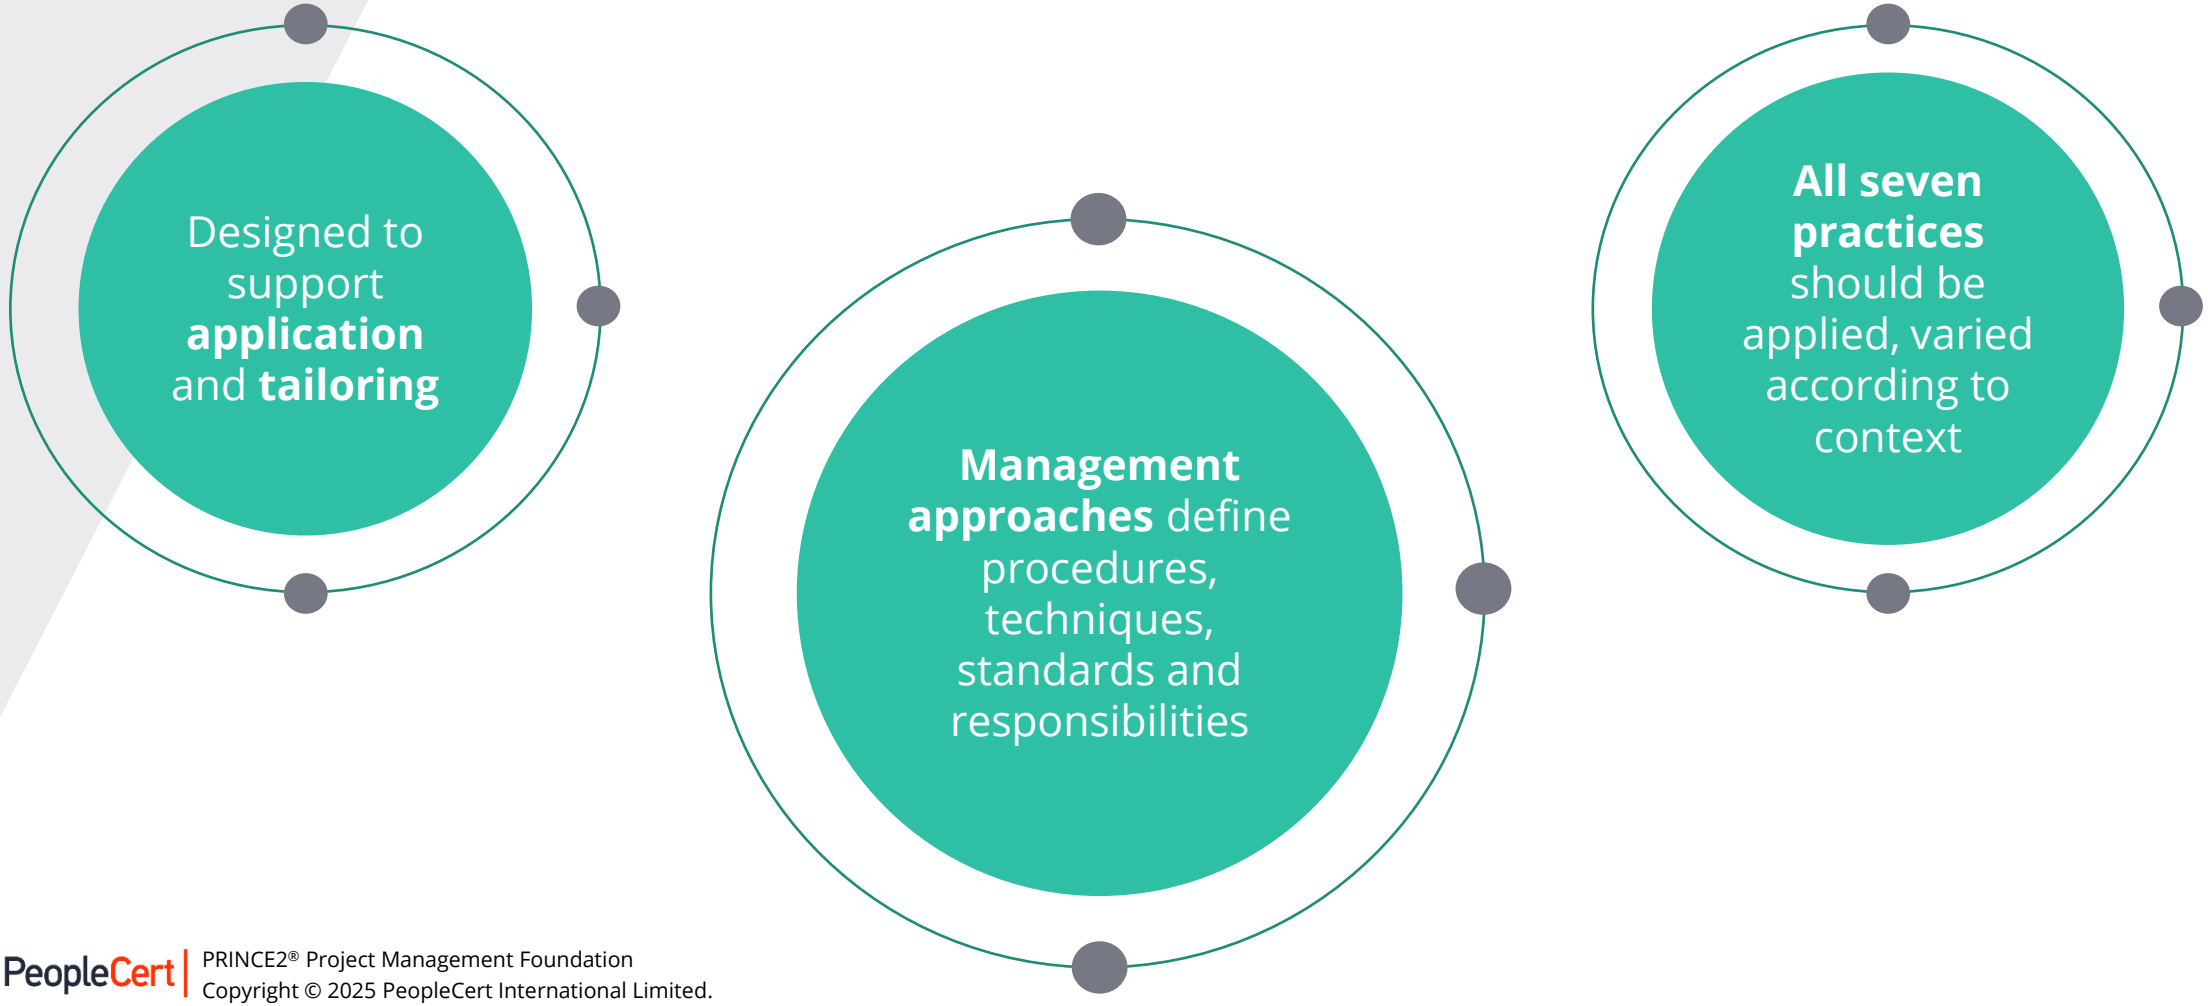

Copyright © 2025 PeopleCert International Limited.

Management products

The management products of PRINCE2 Project Management describe the information that will be required to manage the project.



Project Initiation Documentation (PID)




Project log

Copyright © 2025 PeopleCert International Limited.

Project Initiation Documentation (PID)


- sound basis for commitment
- base document for ongoing assessment
- single source of reference.

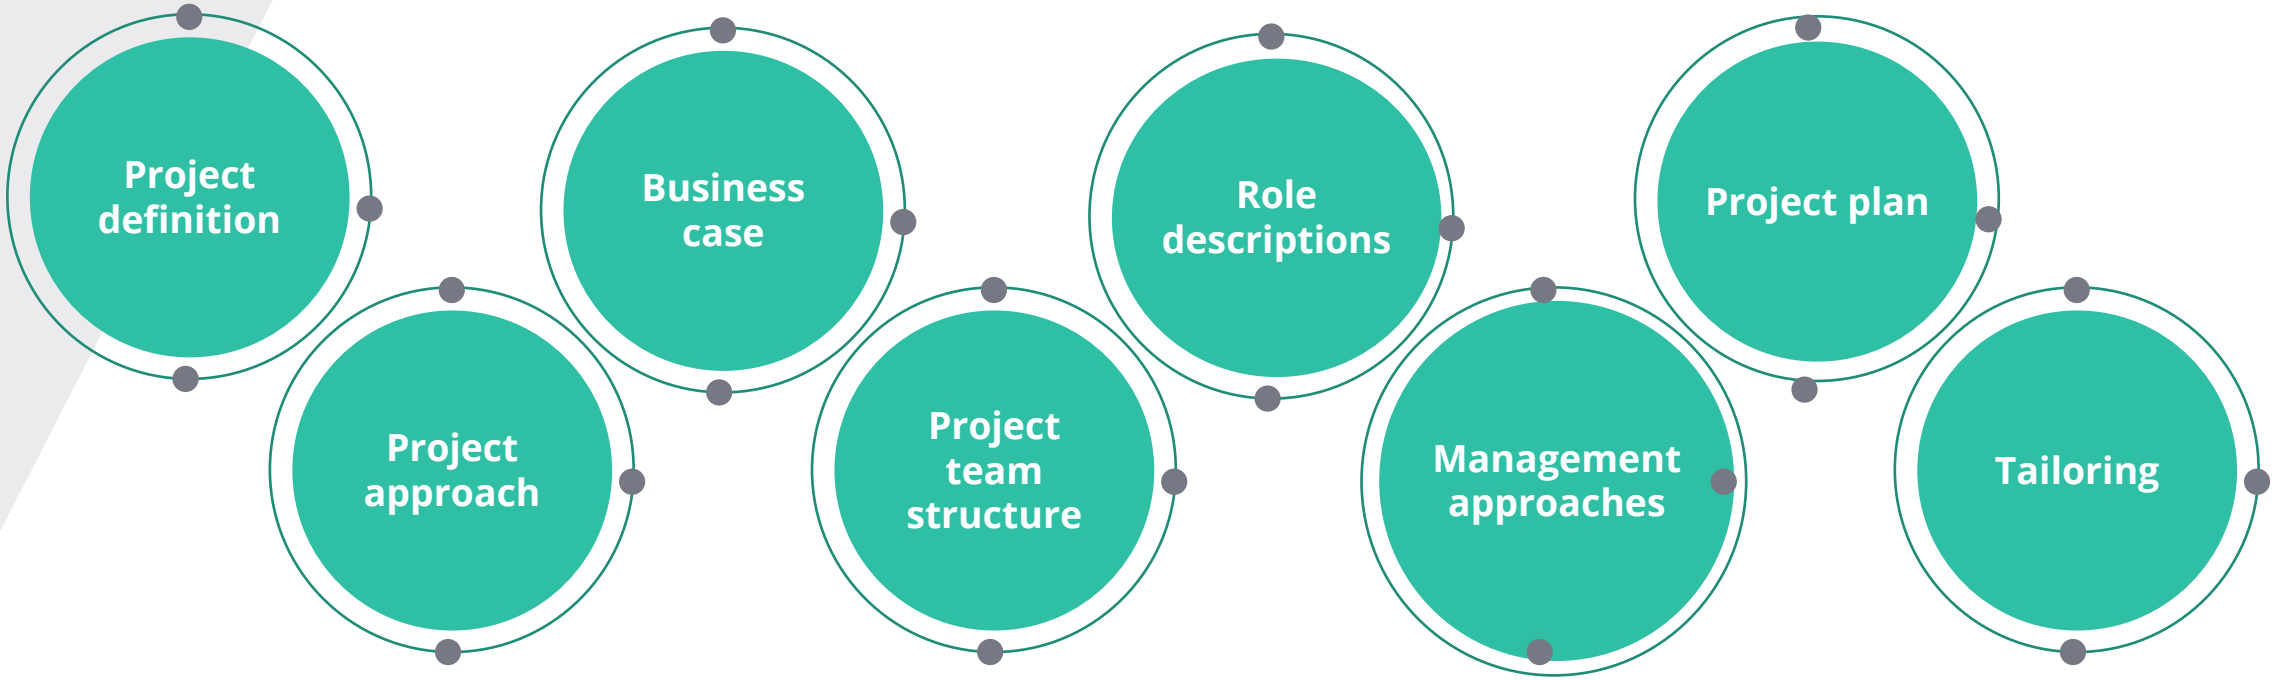

Copyright © 2025 PeopleCert International Limited.

Project log

The purpose of the project log is to capture the continually changing records of issues, lessons, products, quality, risk, and other informal actions or events.

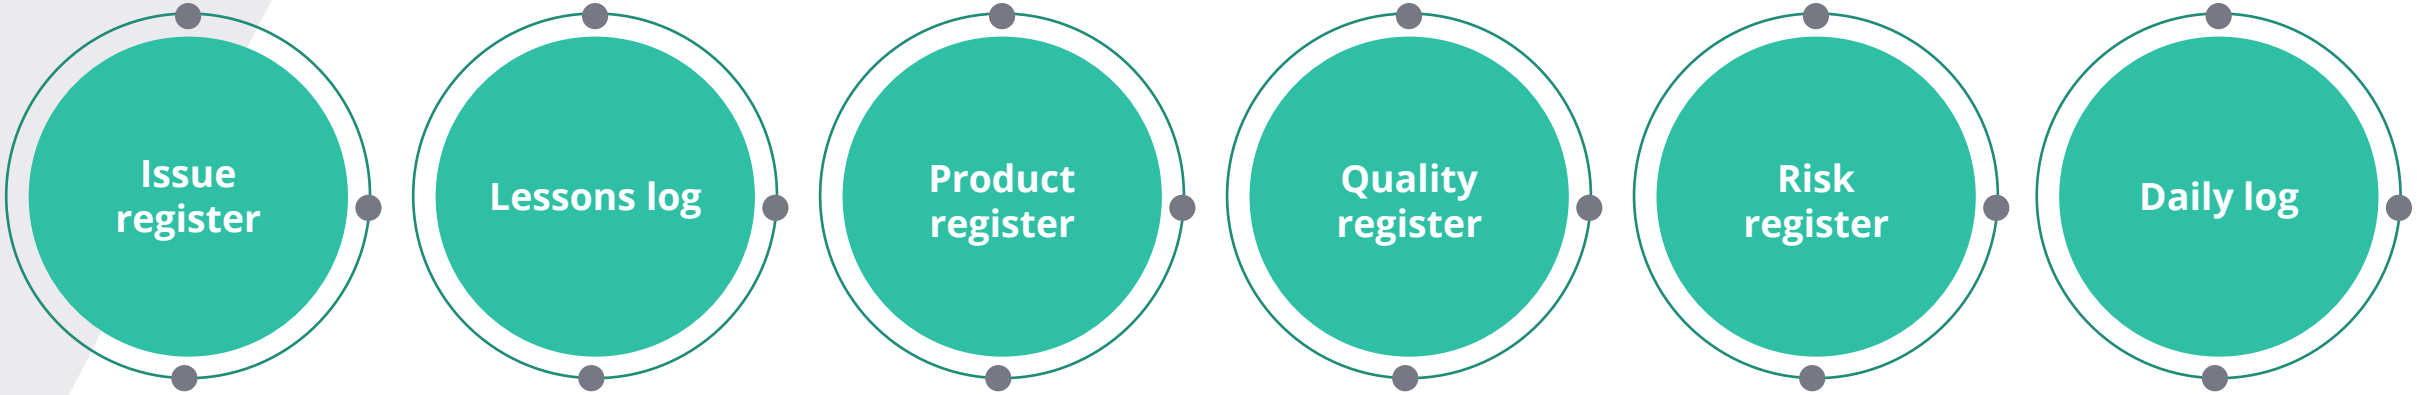

Copyright © 2025 PeopleCert International Limited.

Purpose of the organization practice



The purpose of the organization practice is to **define** and **establish** the project's structure of **accountability** and **responsibilities** (the 'who').



Copyright © 2025 PeopleCert International Limited.

The three principal project interests


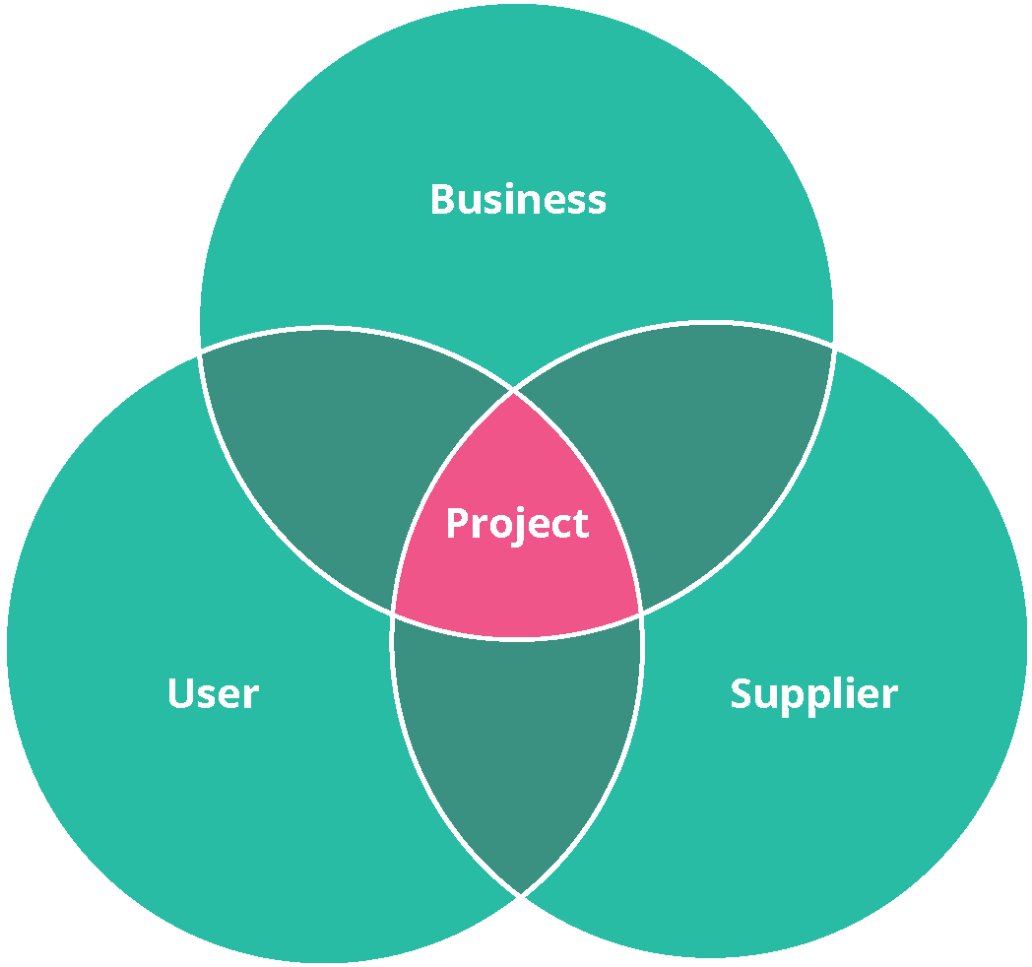


Figure 6.1 The three project stakeholder groups

Copyright © 2025 PeopleCert International Limited.

The business

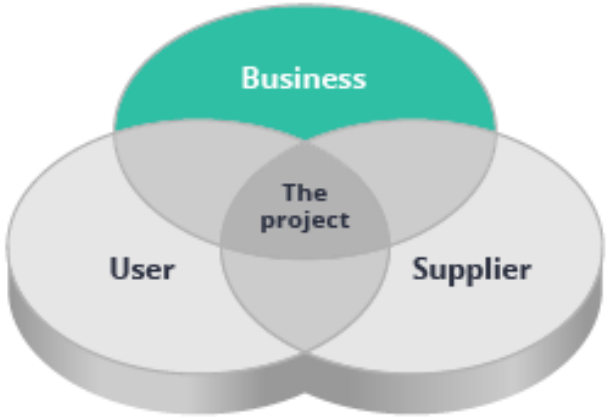

PROJECT



Meet a business need.



Ensure value for money.




ROLE

The **executive** represents the business interests on the project.

Copyright © 2025 PeopleCert International Limited.

The user

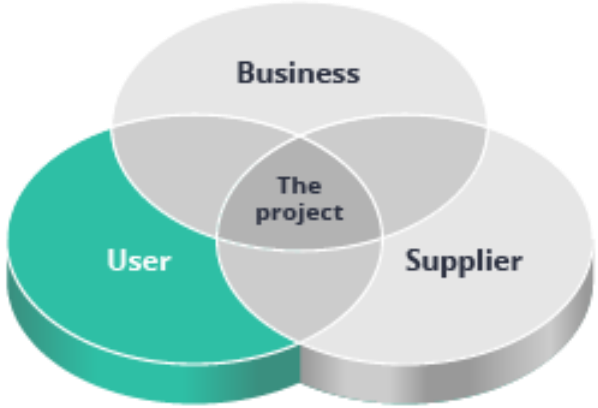

USER

will use the outputs of the project to realize the benefits

will operate, maintain, or support the project's outputs


the **outputs** of the project will **impact** them.

ROLE

Senior user(s) are needed to represent user interests on the project.

Copyright © 2025 PeopleCert International Limited.

The supplier

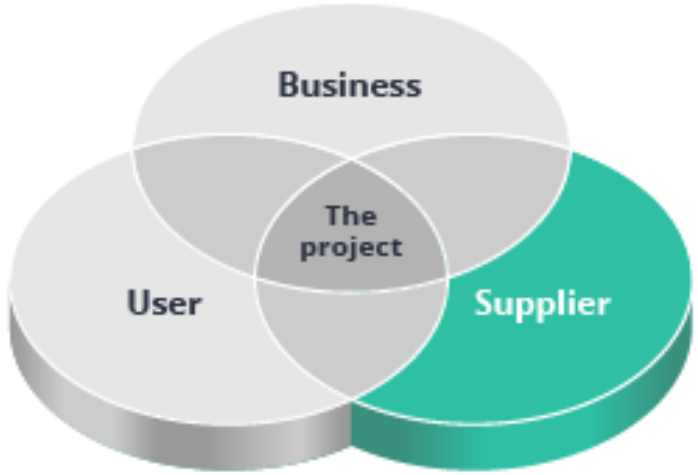

- The creation of the project's outputs will require resources with specific skills.
- The supplier viewpoint should represent those who will provide these skills and contribute to producing the project's product.

ROLE

Senior supplier(s) are needed to represent supplier interest on the project.

Copyright © 2025 PeopleCert International Limited.

Organizational levels

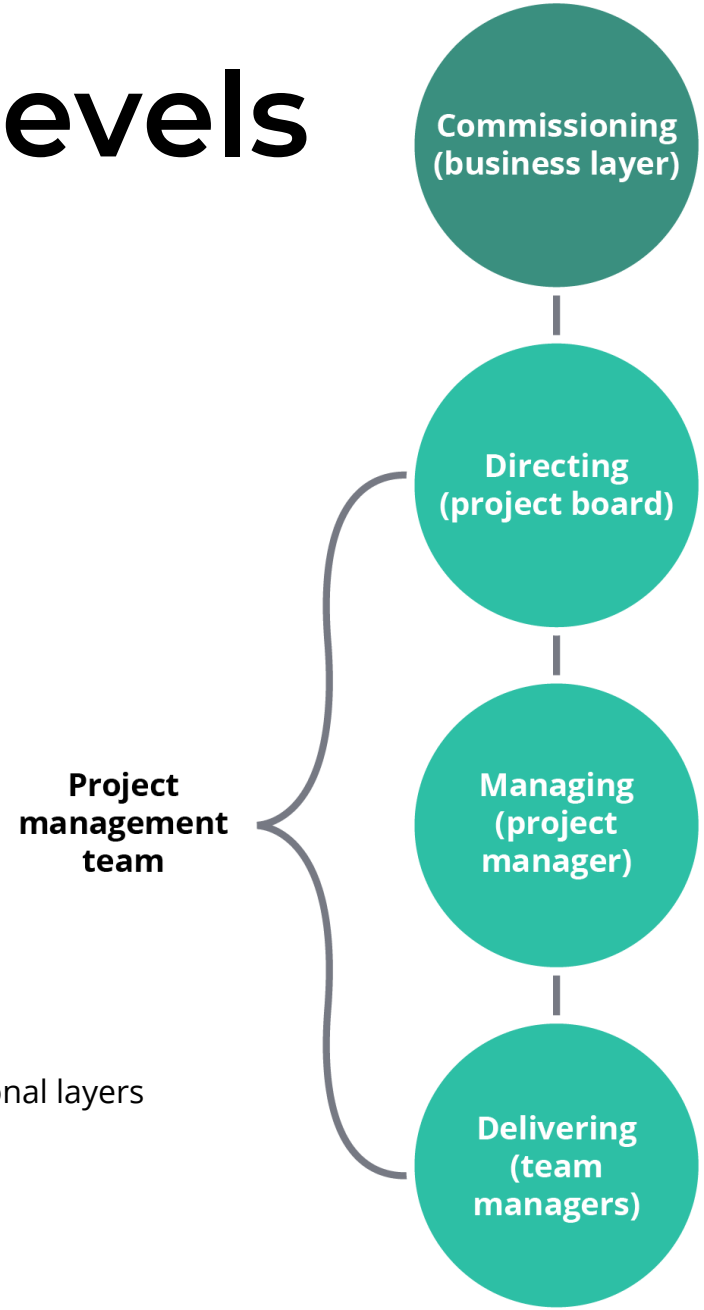


Figure 6.2 The four organizational layers

Copyright © 2025 PeopleCert International Limited.

Project management team roles

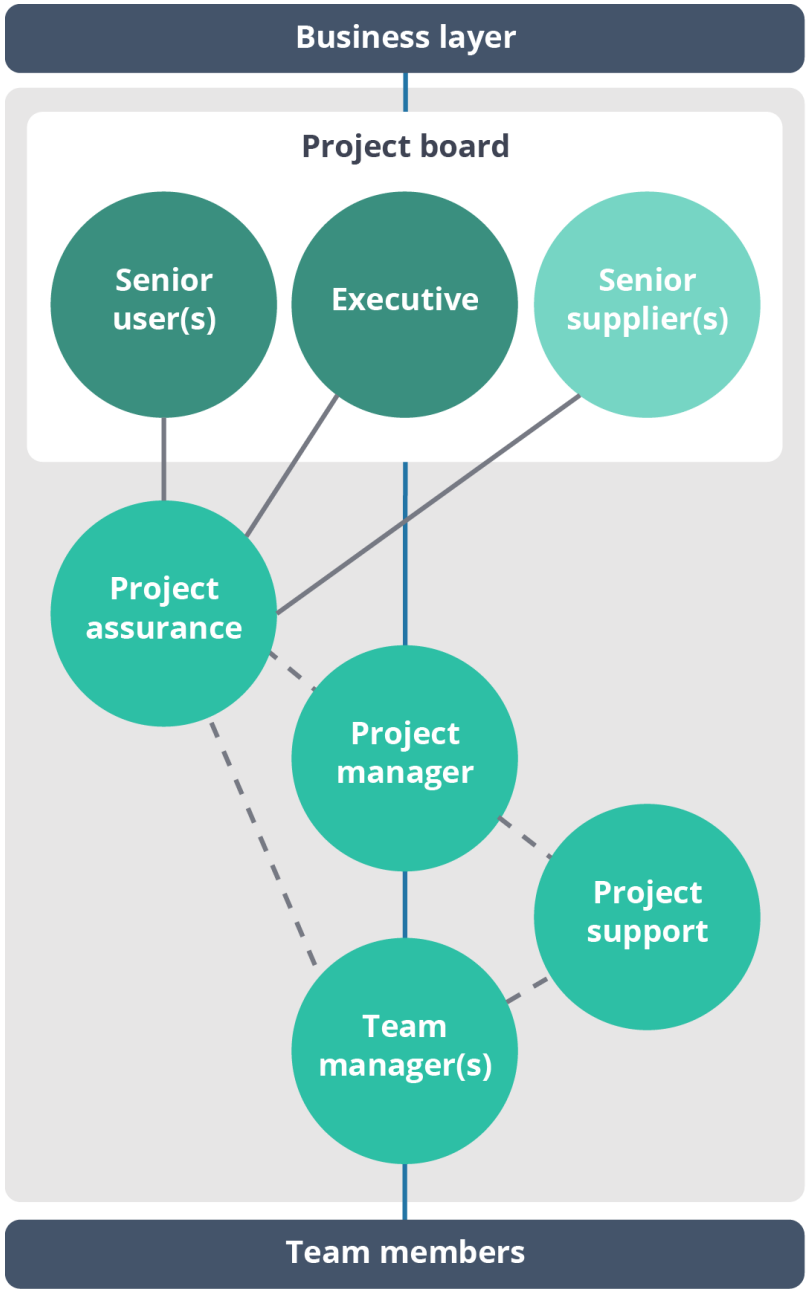


Figure 6.3 Project management team structure

Copyright © 2025 PeopleCert International Limited.

The project management team

A successful project management team:



has **business, user,** and **supplier** stakeholder representation



ensures appropriate governance by **defining responsibilities** at each level



reviews the project **roles** throughout the project



has an effective approach to manage **communication flows** to and from stakeholders

Copyright © 2025 PeopleCert International Limited.

Project board

Senior user(s)


Represents the user community and is **accountable** for the approach taken to capture user requirements and specification of benefits aligned to the business case.

Project executive

Appointed by the business as the **single point of accountability** for the project. This accountability cannot be delegated.

Senior supplier(s)

Is **accountable** for the **quality of the products** delivered by the suppliers and for the **technical integrity** of the project.

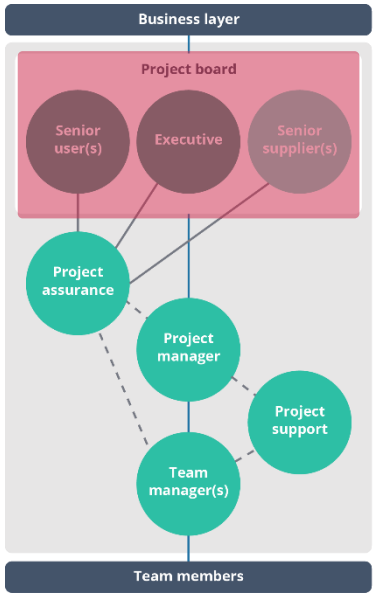

Adapted from Figure 6.3 Project management team structure




Copyright © 2025 PeopleCert International Limited.


Project manager

How would you define the project manager's role?

The project manager is responsible for day-to-day management of a project.

They have authority to run the project on behalf of the project board, within agreed stage tolerances and constraints.

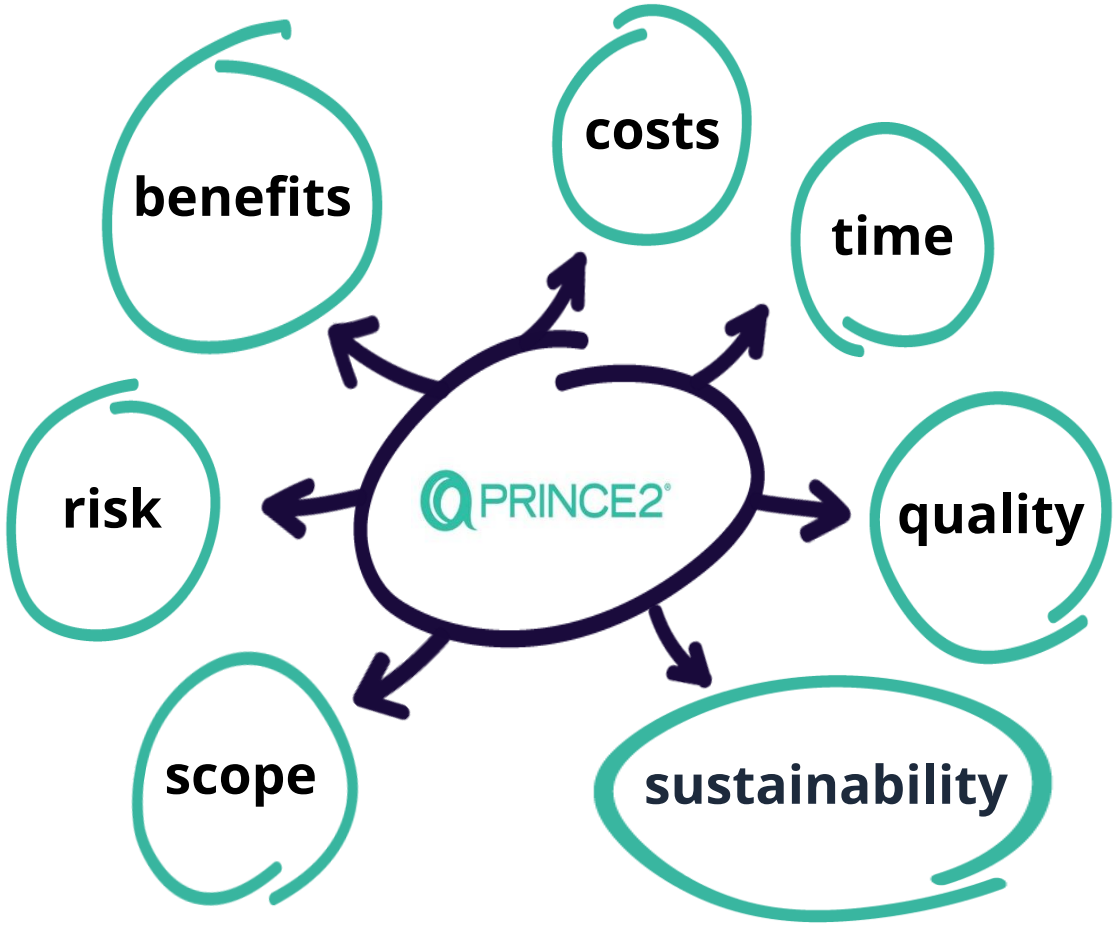

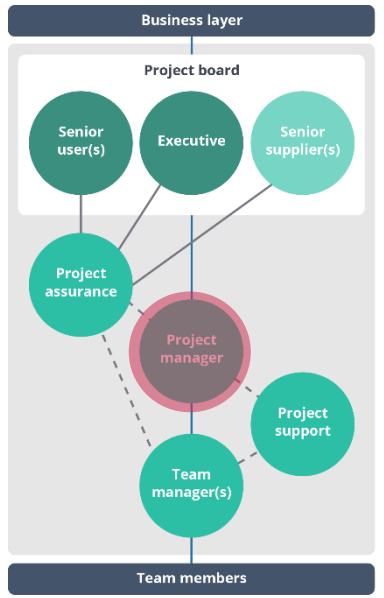

Adapted from Figure 6.3 Project management team structure

Copyright © 2025 PeopleCert International Limited.


Team manager



The project manager is responsible for **delivering the work** to agreed specifications and within the tolerances and constraints agreed with the project manager.

They allocate work to a team manager through **work package descriptions**, in line with the commercial management approach.

They manage **relationships** in their teams and interfaces with other teams.

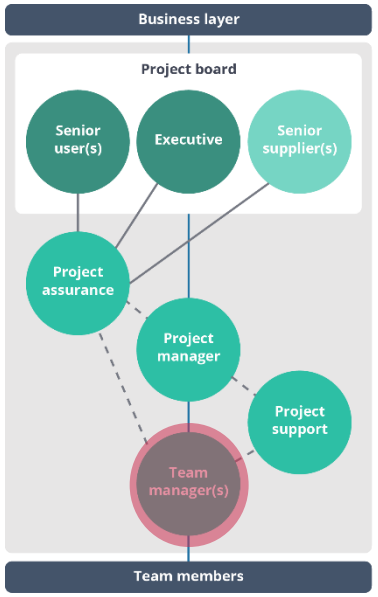

Adapted from Figure 6.3 Project management team structure



Copyright © 2025 PeopleCert International Limited.


Other roles

Project assurance

- Project board members are accountable for assurance of respective areas.
- The project board may appoint separate individuals, but not project manager, team members or project support.

Project support

- It includes services such as administrative support, guidance on project tools, planning and so on.
- It is the responsibility of project manager but may be delegated.
- A project office may be established.

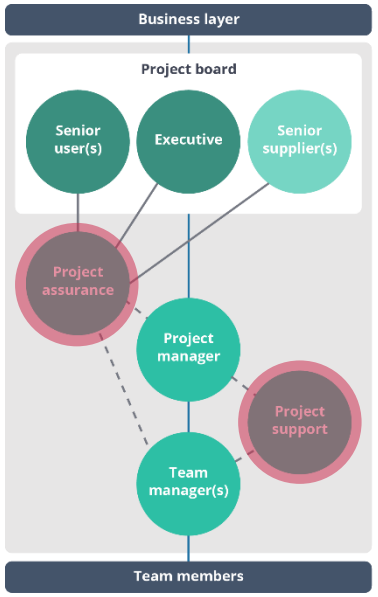

Adapted from Figure 6.3 Project management team structure



Copyright © 2025 PeopleCert International Limited.

Roles and responsibilities

Projects must have an explicit project management team structure.

People involved in the project should have defined roles and responsibilities.

There should be a means for effective communication between them.



Copyright © 2025 PeopleCert International Limited.

Work breakdown structure


- supports project manager in **structuring teams** and setting **boundaries**
- assists in managing a mix of **internal** and **external work packages.**



A **hierarchy** of all work to be done during a project that forms a link between the **product breakdown structure** and the **work packages**.

Copyright © 2025 PeopleCert International Limited.

The PRINCE2 Project Management technique for organizing

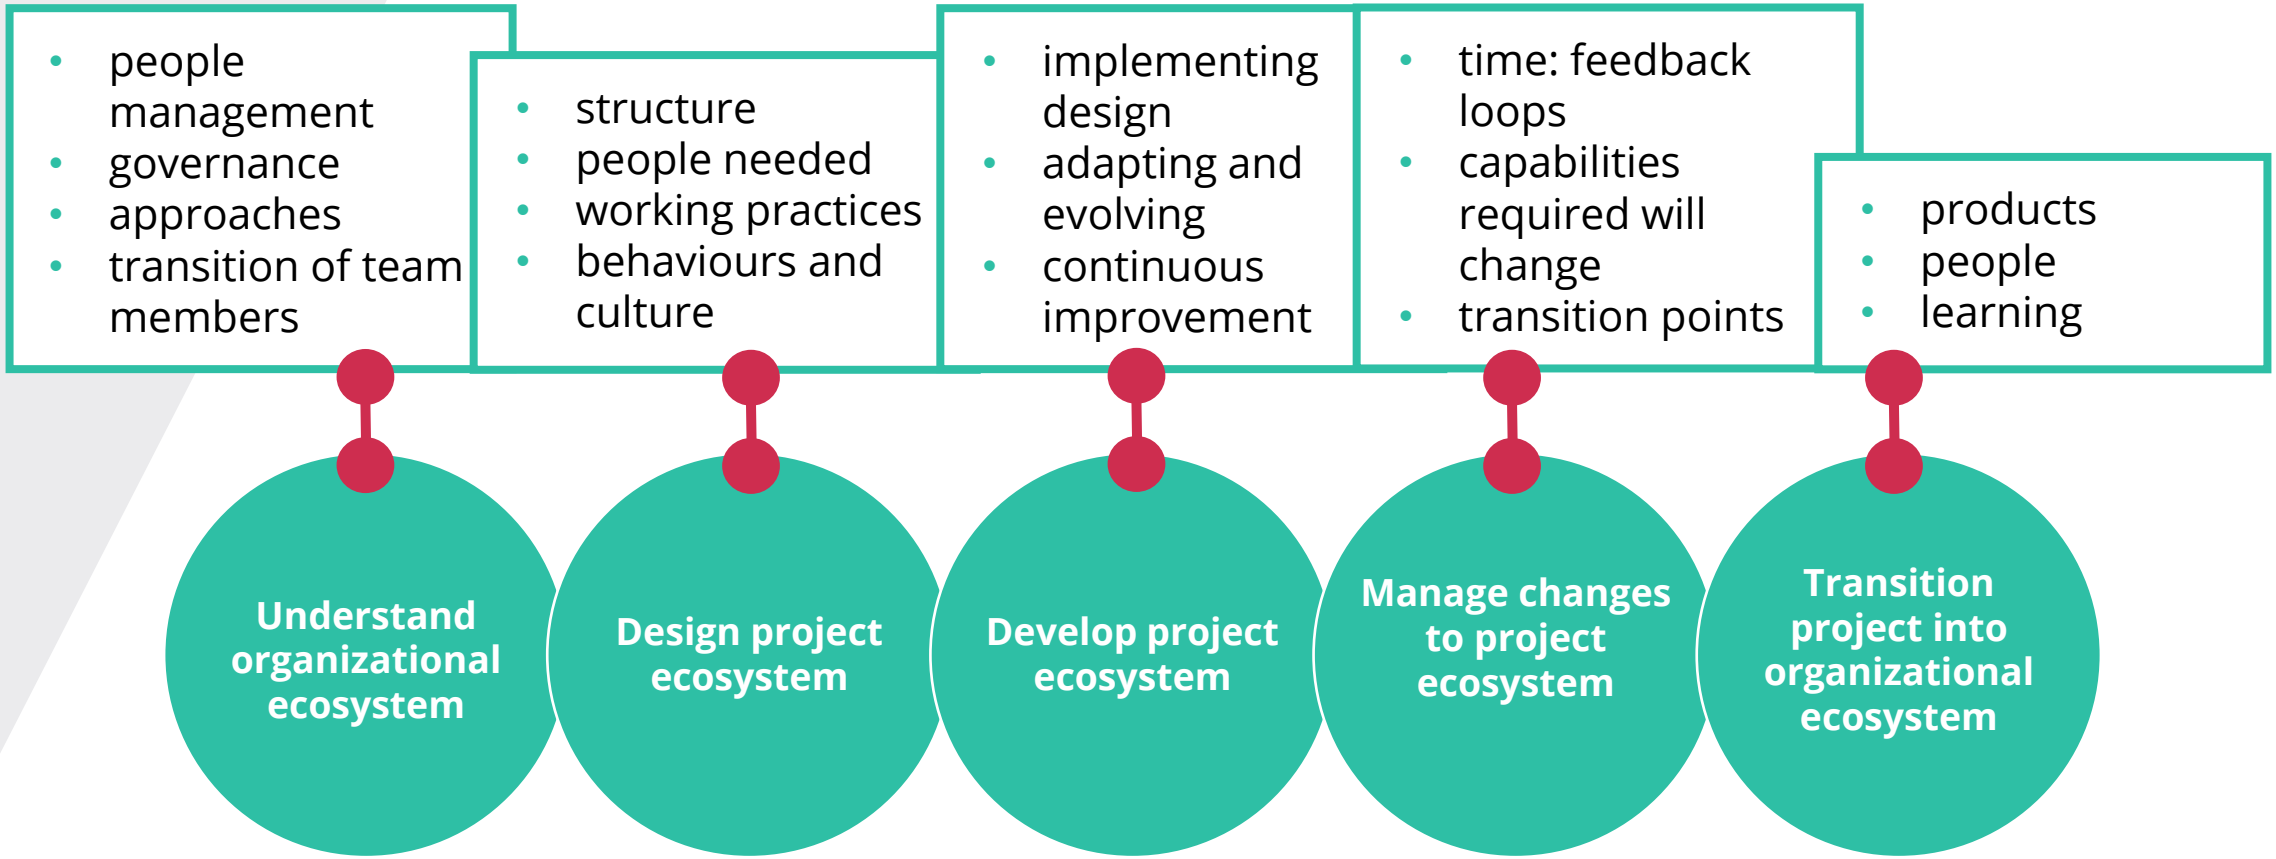

Adapted from Figure 6.4 PRINCE2 Project Management technique for organizational design and development

Copyright © 2025 PeopleCert International Limited.

Management products

Commercial management approach

Describes the **procedures, techniques, standards** and **responsibilities** for effective commercial management.

Covers the approach to **secure, service,** and **maintain all commercial agreements** required for the project to be a success.

Project management team structure

Defines **who** is involved in the project, their **relationships,** and **how** they will work together, including relevant key personnel outside the project team.

Role descriptions

Describe the **roles** of those in the project management team and their **specific responsibilities.**




Copyright © 2025 PeopleCert International Limited.

Applying the principles

assigning a business representative to the project executive role with the right authority and availability

using lessons to inform the team structure and ensure the right people are in the right roles to deliver the project

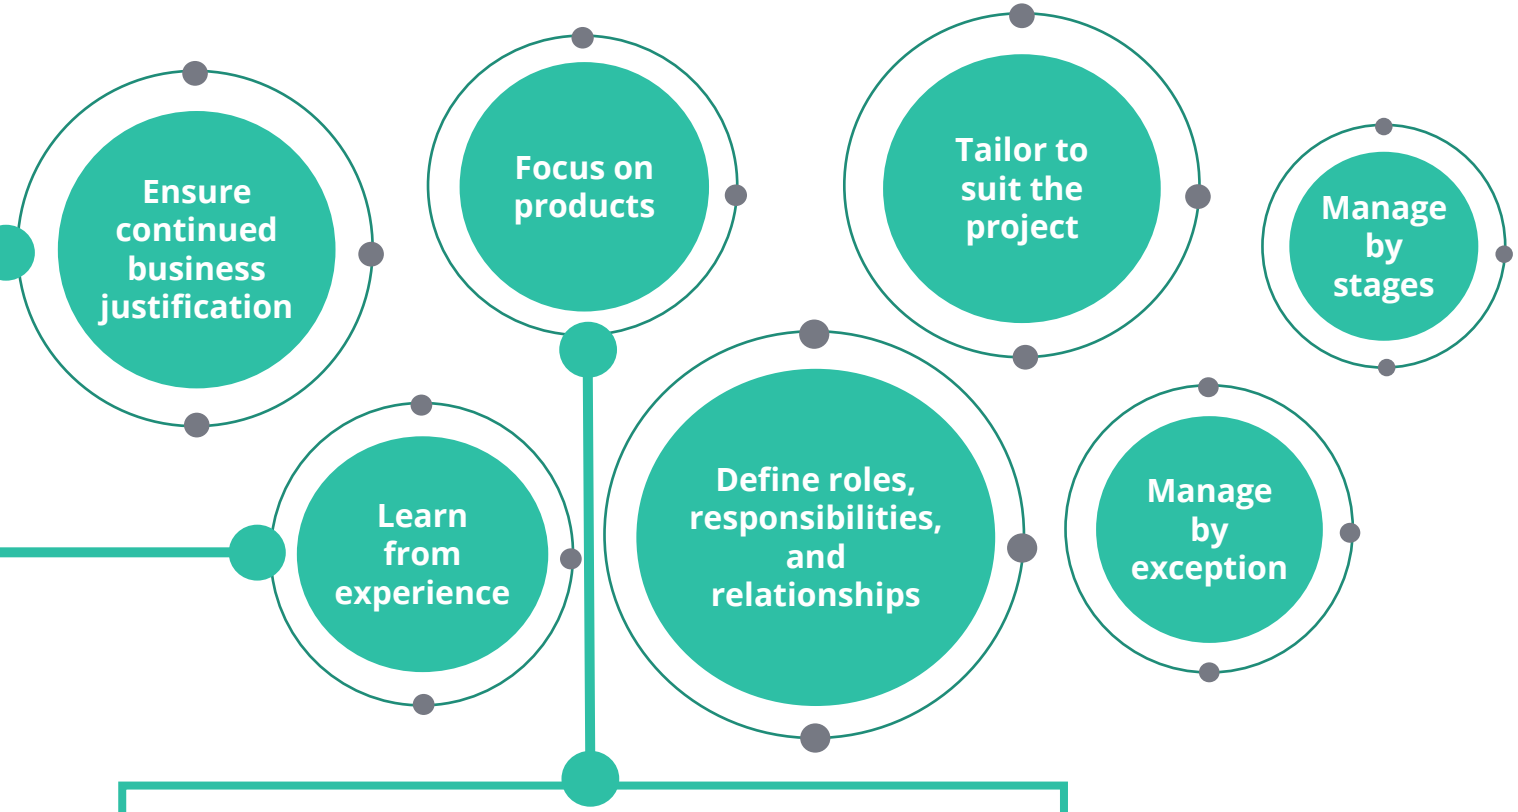

ensuring those who will use the project product are on the project management team to support acceptance and are ready use of the end product

Copyright © 2025 PeopleCert International Limited.

Supporting techniques for organization

Delivery model

The organizational and commercial arrangements to be deployed to meet the project ctivctives given the project constraints and capabilities of the user, business, and supplier organizations. It is described in the **commercial management approach** and reflected in the project management **team structure.**

RACI chart

- **Responsible:** one or more people who perform the task.
- **Accountable:** the single person who 'owns' the task.
- **Consulted:** the people whose input is required for the task.
- **Informed:** the people who are informed of progress or completion of the task.



Copyright © 2025 PeopleCert International Limited

30 minutes

Organization

Activity

Design a project management team

Look at the NowByou employees and stakeholders in the scenario.

What roles could they have in a project team?



Copyright © 2025 PeopleCert International Limited.

NowByou employees and stakeholders



The Chief Executive Officer (CEO) of NowByou is a founding member and has held the position since the organization's inception. She is very experienced in the not-for-profit sector.



The Chief Finance Officer (CFO) of NowByou was appointed 6 months ago and has been very active with donors and partners to increase the financial standing of the organization. Previously, he was a senior executive at a major bank and is eager to introduce strong portfolio and project management practices at NowByou.



Head of Fund-Raising reports to the CFO. She previously worked within an organization with good portfolio, programme, and project management practices and helped gain approval for the appointment of the external professional project manager and the establishment of a Portfolio Office in NowByou. She is PRINCE2 qualified.



The NowByou Director of Campaigns has recently joined NowByou, having previously been a senior marketing manager with a commercial manufacturing organization. He has overall responsibilities for all campaigns.



A Portfolio Office Manager, previously a senior administrative officer for NowByou, has been appointed to set up the portfolio office and work with the Contracted Project Manager to implement and establish the initial project management documentation and processes.



The Contracted Project Manager has worked with many NGO's across the world, successfully helping them manage and deliver projects. This contract is initially for 50% of her time but this is expected to decrease to 25% after the first three months.



The Police Liaison Officer joined NowByou five years ago, after retiring from a successful career with the national police force. He has worked closely with the HR Director on past initiatives and has been establishing a close professional relationship with the new Director of Campaigns.



The HR Director launched a **graduate trainee programme** two years ago. The first four trainees will complete their two-year training in two months and have all received PRINCE2 Project Management certification.



The Head of Publicity and Social Media reports to the Director of Campaigns and is responsible for Brand management, press release and social media.



Marketing Agency Director: NowByou has a relationship with a commercial marketing agency, CharityM, who work with the Head of Publicity and Social Media in developing and placing advertising on TV and Radio stations.

Copyright © 2025 PeopleCert International Limited.

Suggested team



Executive
CFO



Senior user
Director of campaigns



Project manager
Graduate trainee



Senior supplier
Marketing agency director



Project assurance
Head of fundraising/police liaison officer



Team manager
Marketing agency/ Staff member



Project support
Portfolio office manager

Copyright © 2025 PeopleCert International Limited.


Module 4

Starting up a project and initiating a project

Starting up a project

PRINCE2 Project Management processes

‘Starting up a project’ is **the first process** in PRINCE2 Project Management.

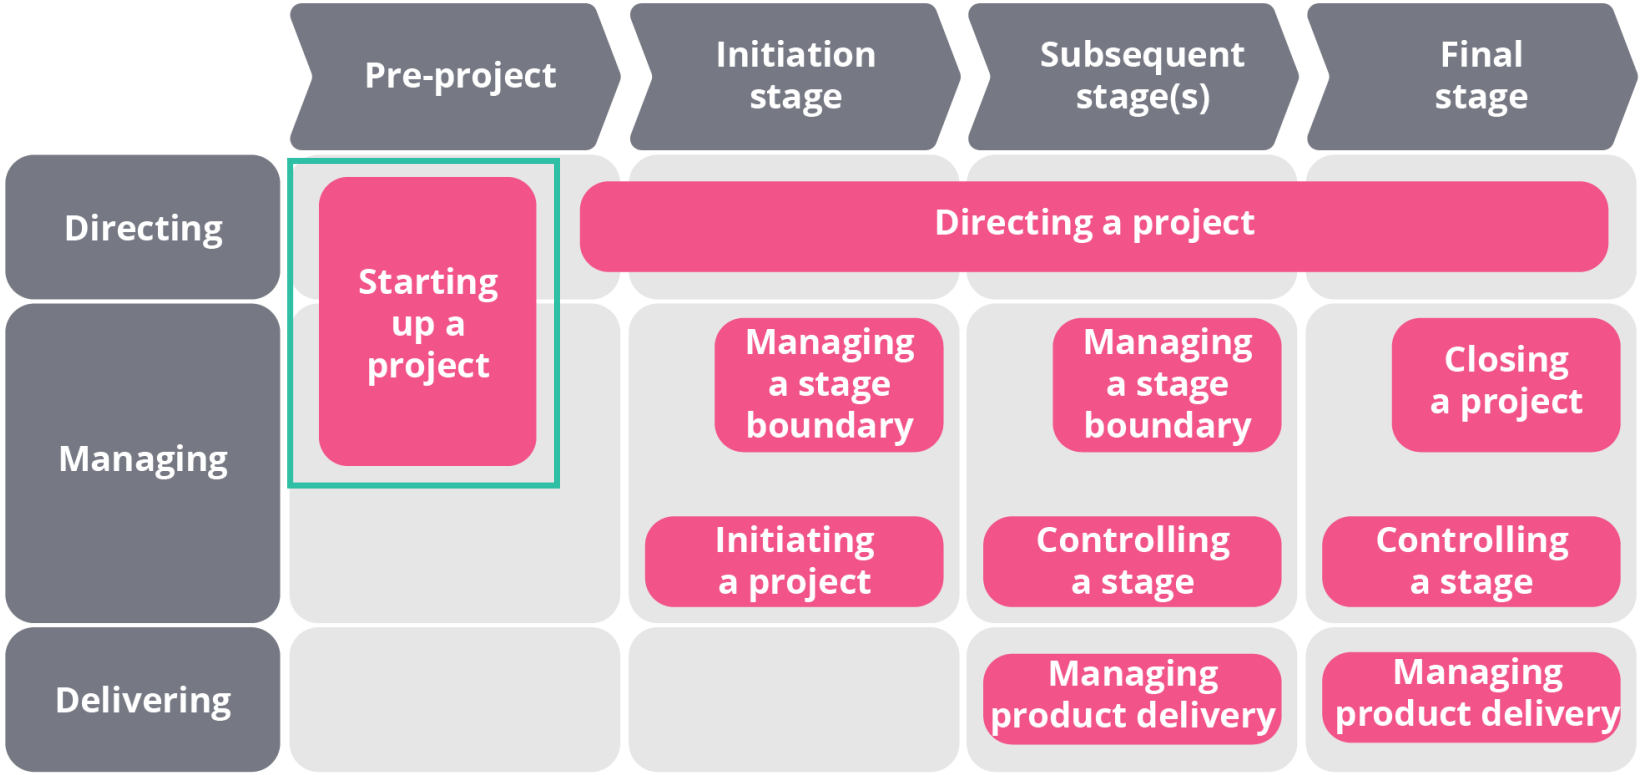

Note

- Starting up a project is used by both the directing and managing levels.
- There should be at least two stages, the first of which is the initiation stage.
- Managing a stage boundary is first used at the end of the initiation stage and repeated at the end of each subsequent stage except the final stage. It is also used to prepare exception plans, which can be done at any time including in the final stage.

Adapted from Figure 12.1 The PRINCE2 Project Management processes

Copyright © 2025 PeopleCert International Limited.

The purpose of ‘starting up a project’




Ensure that the **prerequisites** for **initiating a project** are established by answering the question, **‘do we have a viable and worthwhile project?’**



Copyright © 2025 PeopleCert International Limited.

The objectives of ‘starting up a project’

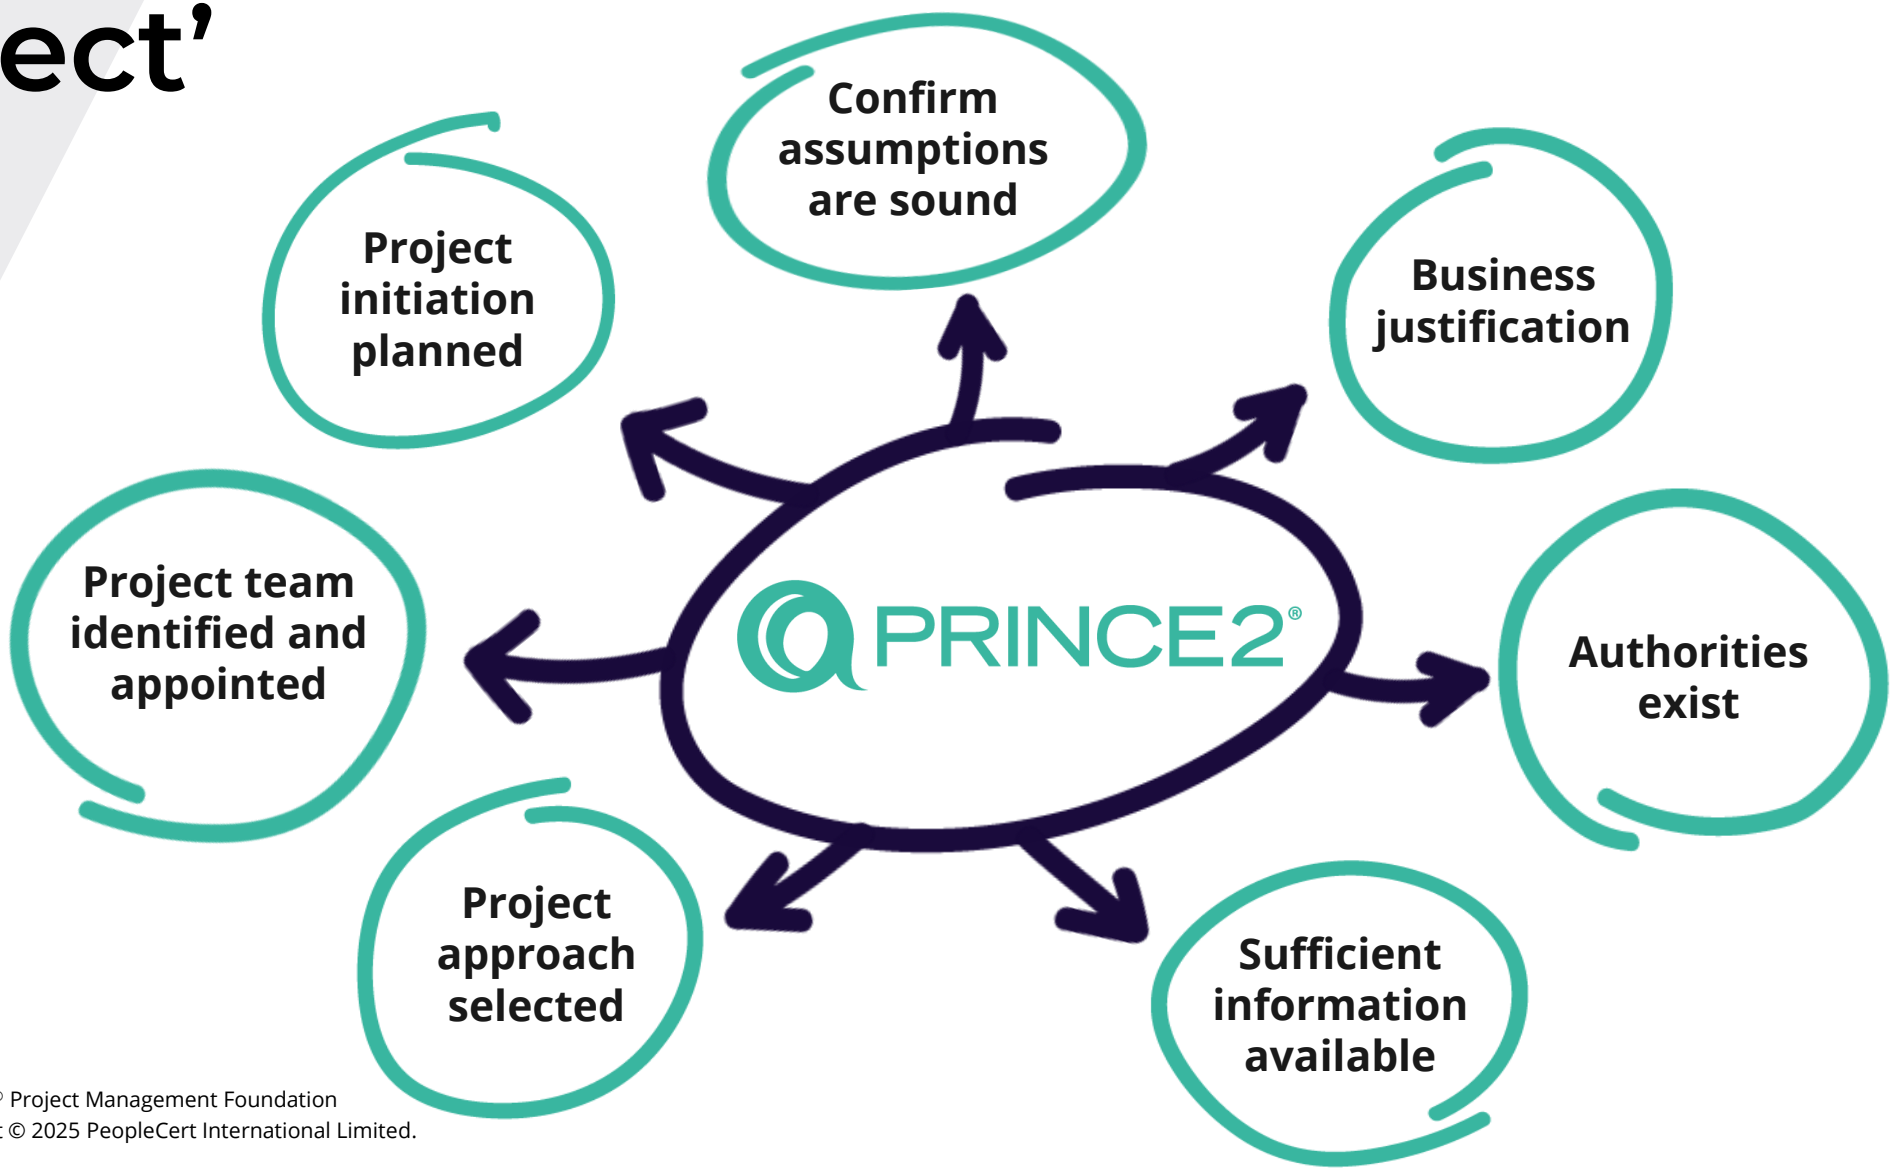

Copyright © 2025 PeopleCert International Limited.

Overview of ‘starting up a project’

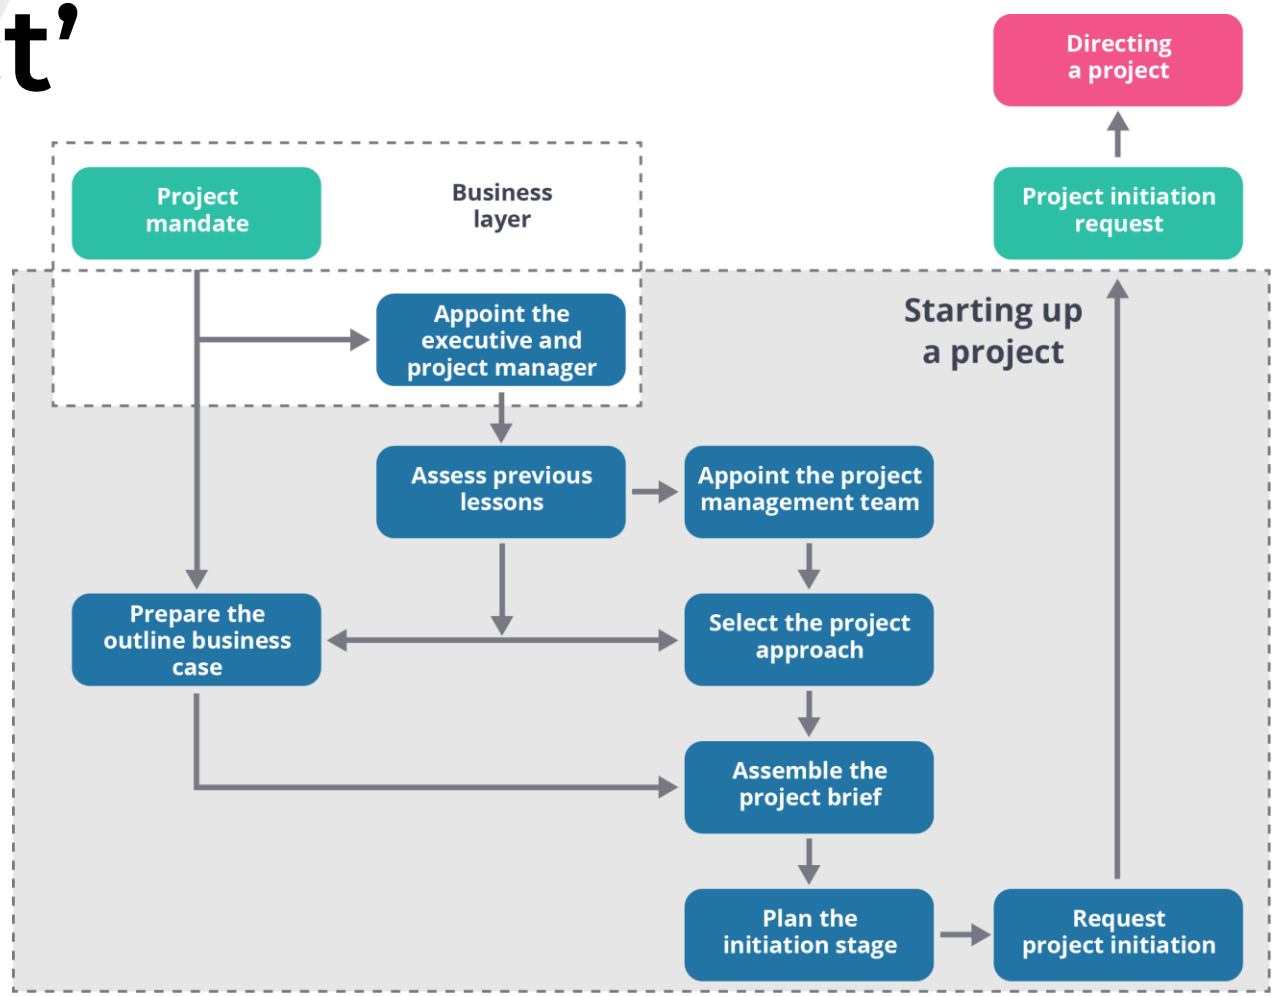


Figure 13.1 Overview of ‘starting up a project’

Copyright © 2025 PeopleCert International Limited.

‘Starting up a project’ roles and responsibilities

Table 13.2 RACI chart for ‘starting up a project’

Activity	Business layer	Project executive	Senior user	Senior supplier	Project manager	Team manager	Project assurance	Project support
Appoint the project executive and project manager	A/R[1]	R						
Assess previous lessons	C	A			R			
Prepare the outline business case	C	A/R[1]	C[3]	C[3]	R			
Appoint the project management team	A	R						
Select the project approach		A	C	C	R	C[2]	C	
Assemble the project brief		A	C	C	R		C	C
Plan the initiation stage		A	C	C	R	I[2]	C	C
Request project initiation		A	C	C	R	I[2]	C	I

R = Responsible, A = Accountable, C = Consulted, I = Informed

A/R[1]: Business is accountable for the appointment of the project executive and the project manager. They are also responsible for appointing the project executive.

C2/I[2] : If any team managers have been identified when designing and appointing the project management team, then it is good practice to consult them on the project approach and inform them of key details in the stage plan for the initiation stage should they be involved in that stage.


C[3]: if/when appointed.

Copyright © 2025 PeopleCert International Limited

Initiating a project

PRINCE2 Project Management processes

'Initiating a project': the process used for **the initiation stage** of a PRINCE2 Project Management project.

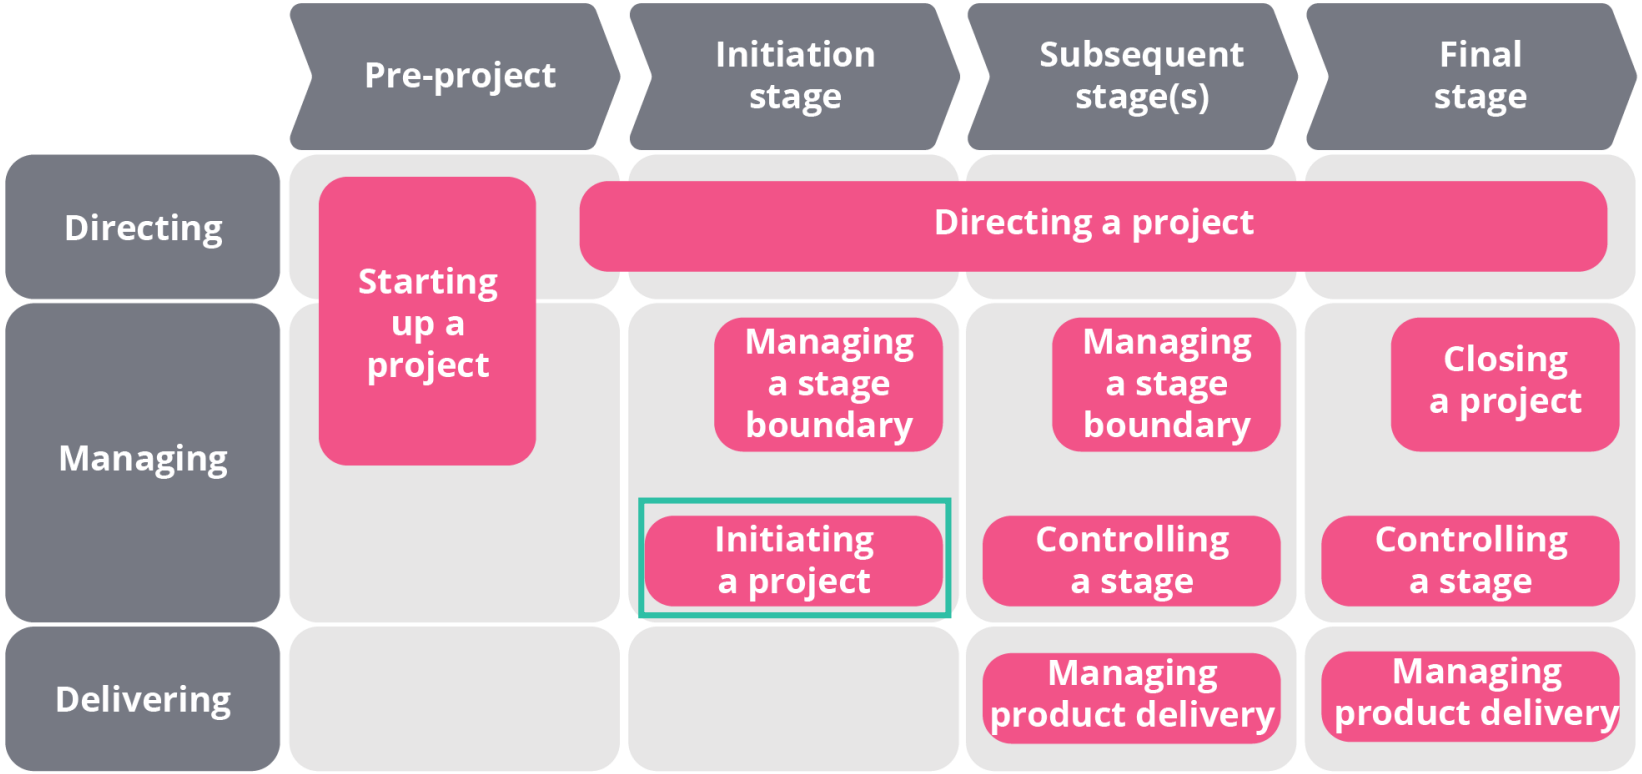

Note

- Starting up a project is used by both the directing and managing levels.
- There should be at least two stages, the first of which is the initiation stage.
- Managing a stage boundary is first used at the end of the initiation stage and repeated at the end of each subsequent stage except the final stage. It is also used to prepare exception plans, which can be done at any time including in the final stage.

Adapted from Figure 12.1 The PRINCE2 Project Management processes

Copyright © 2025 PeopleCert International Limited.

The purpose of ‘initiating a project’

The purpose of ‘initiating a project’ is to establish a **solid baseline** for the project.

It assures a common understanding of **all aspects** of the proposed project: **reasons**, **scope**, **timescales**, **decision-making**, **quality**, **risk management**, **change**, **communication**, **monitoring**, and **tailoring**.



Copyright © 2025 PeopleCert International Limited.

The objectives of ‘initiating a project’

Reasons
Benefits expected, and associated risks

Scope
The products to be delivered

Delivery
How and when the project product will be delivered and at what cost

Decisions
Who is to be involved in the decision-making

Quality
How the quality required will be achieved


Baselines
How baselines will be established and controlled

Risks
How risks, issues, and changes will be identified, assessed, and controlled

Progress
How progress will be monitored and controlled

Information
Who needs the information, in what format, and at what time

Application
How the project applies business policies, methods, and guidance

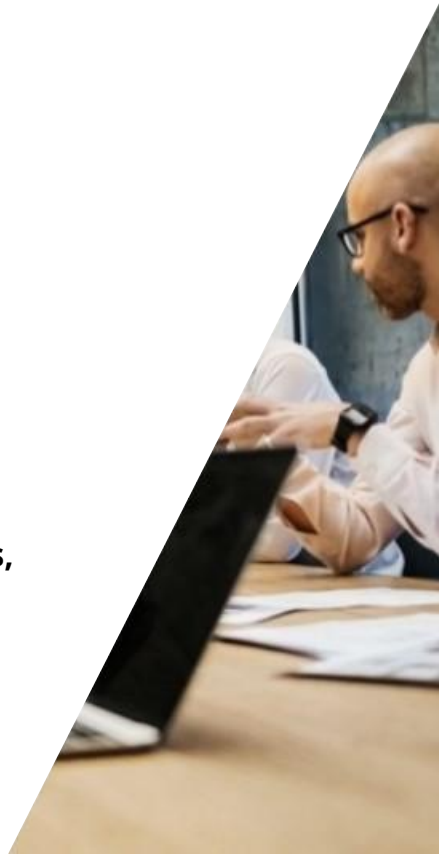

Copyright © 2025 PeopleCert International Limited.

Overview of ‘initiating a project’

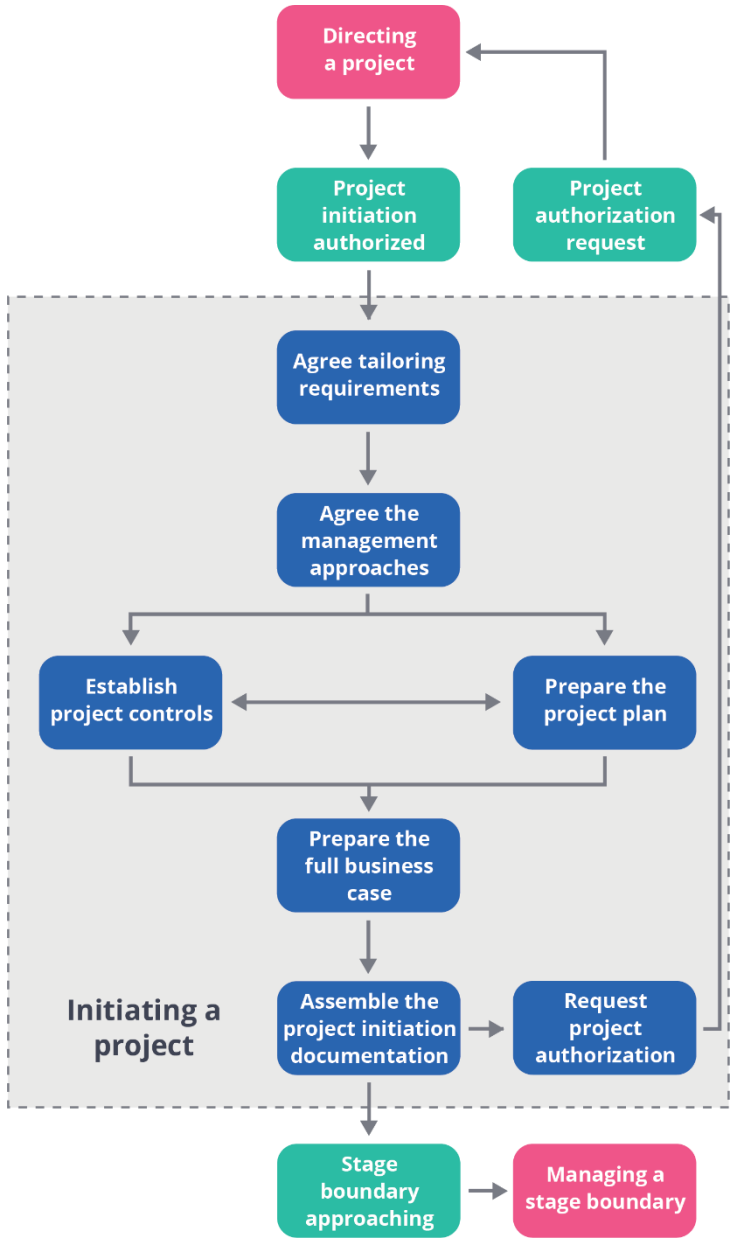


Figure 15.1 Overview of ‘initiating a project’

Copyright © 2025 PeopleCert International Limited.

The PID

This is the **focal point** at which all information relating to the **'what, why, how, where, when and how much'** of the project is **collated.**



Copyright © 2025 PeopleCert International Limited.

‘Initiating a project’ roles and responsibilities

Table 15.2 RACI chart for ‘initiating a project’

Activity	Business layer	Project executive	Senior user	Senior supplier	Project manager	Team manager	Project assurance	Project support
Agree tailoring requirements		A	C	C	R	C	C	I
Agree the management approaches		A	C	C	R	C	C	I
Establish project controls		A	C	C	R	C	C	I
Prepare the project plan		A	C	C	R	C	C	C
Prepare the full business case		A	C	C	R	C	C	I
Assemble the project initiation documentation		C	C	C	A	C	C	R
Request project authorization	I	A	C	C	R	I	C	I

R = Responsible, A = Accountable, C = Consulted, I = Informed

Copyright © 2025 PeopleCert International Limited

Module 5

Business case

Purpose of the business case practice



The purpose of the business case practice is to establish **mechanisms** to judge whether a project is (and remains) **desirable, viable,** and **achievable.**



Copyright © 2025 PeopleCert International Limited.

The relationship between outputs, outcomes, and benefits

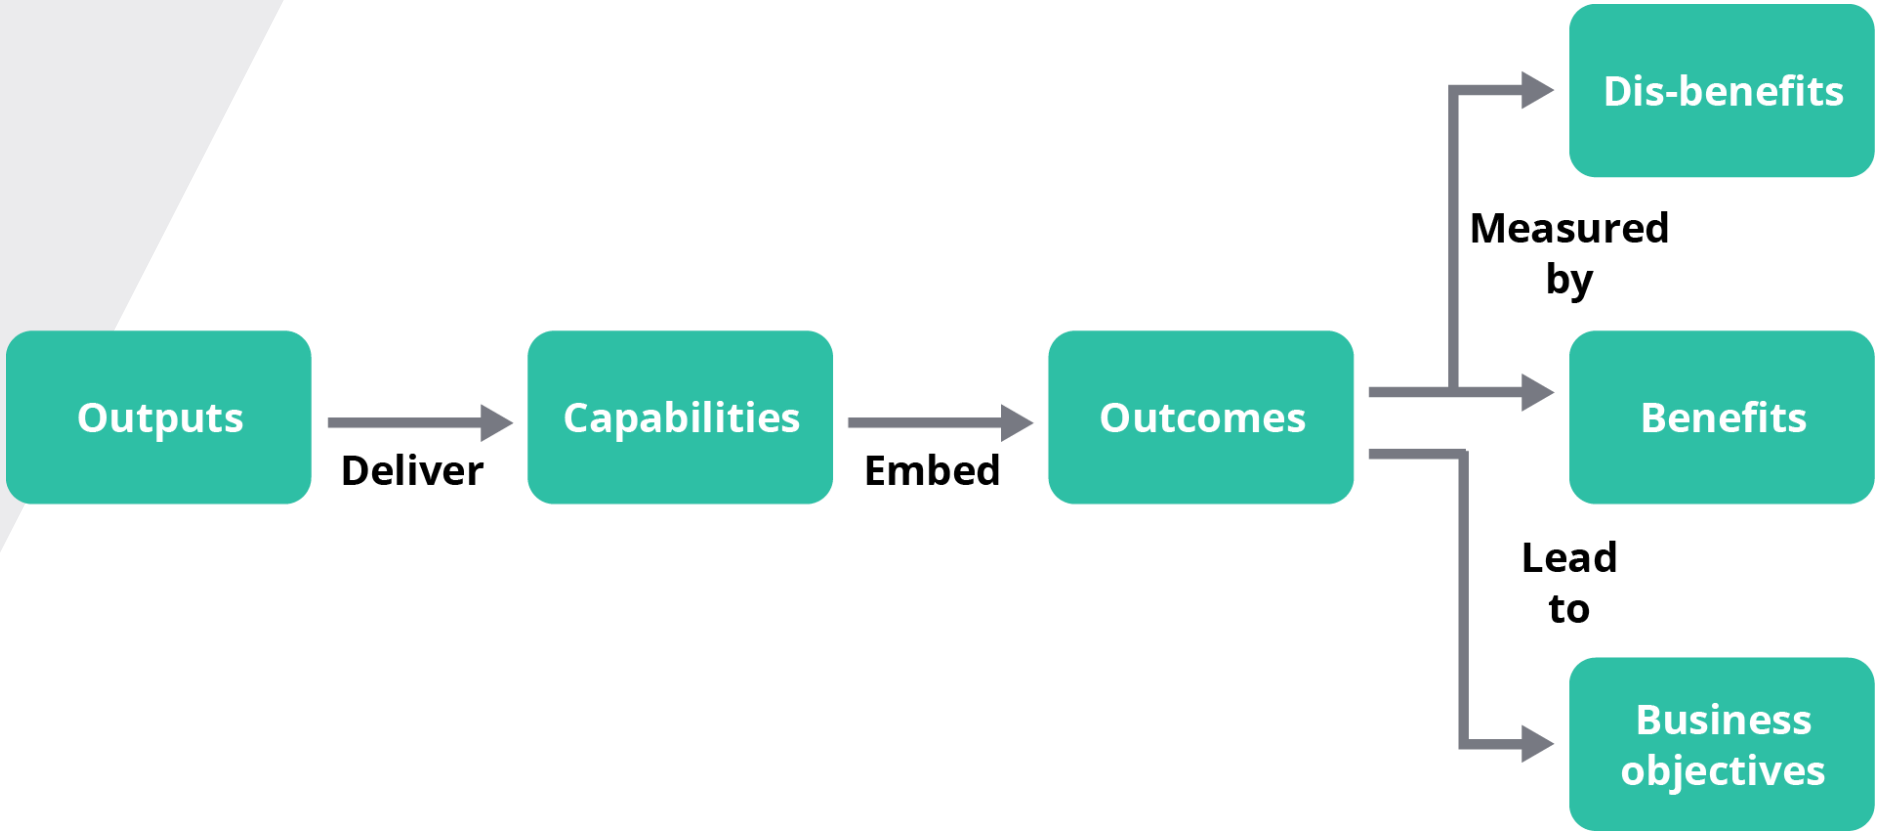


Figure 5.1 Relationship between outputs, outcomes, and benefits

Copyright © 2025 PeopleCert International Limited.

Business case lifecycle

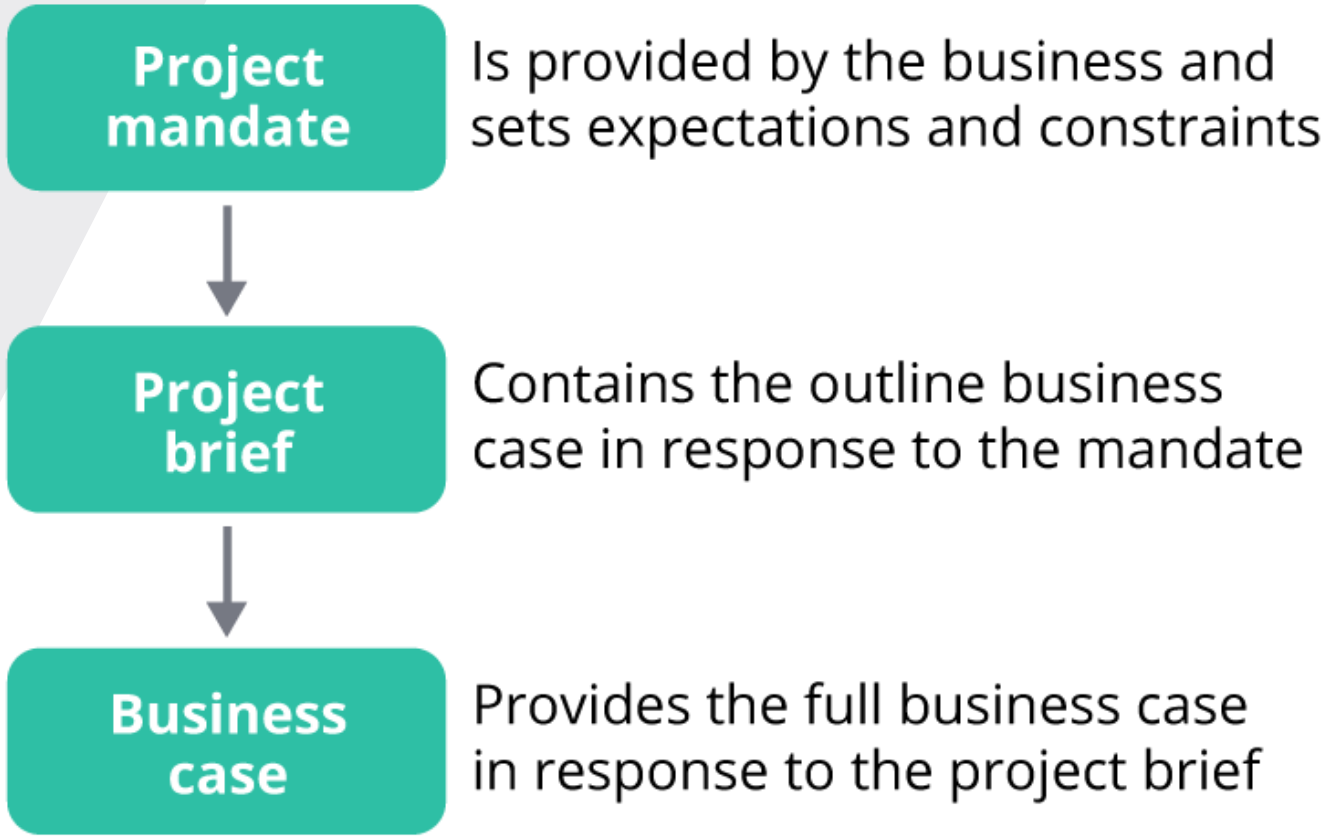


Figure 5.2 Evolution of the business case




Copyright © 2025 PeopleCert International Limited.

Effective business case management

Aligning products to business objectives and tolerances

To realize the benefits, the outcomes must be achieved through the outputs being used as intended, new capability defined, and barriers overcome.

The benefits management approach includes the forecast amount and timing of benefits and tolerances against these targets.

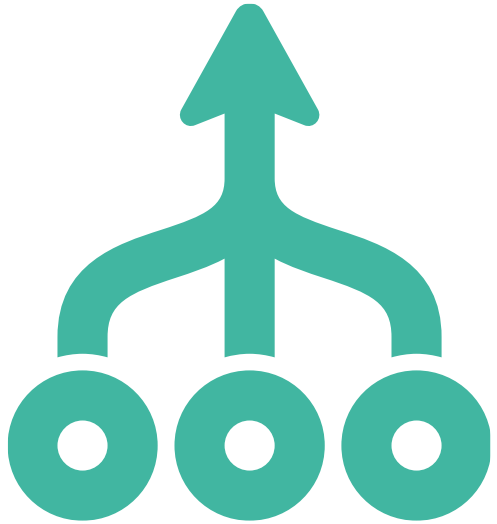

Establishing business justification

There will be trade-offs between the seven aspects of the project's performance targets.

The business case considers options to achieve the required outcomes or 'business options' and selects the one that is the best balance between the different performance aspects.



Copyright © 2025 PeopleCert International Limited.

Business case through the project lifecycle


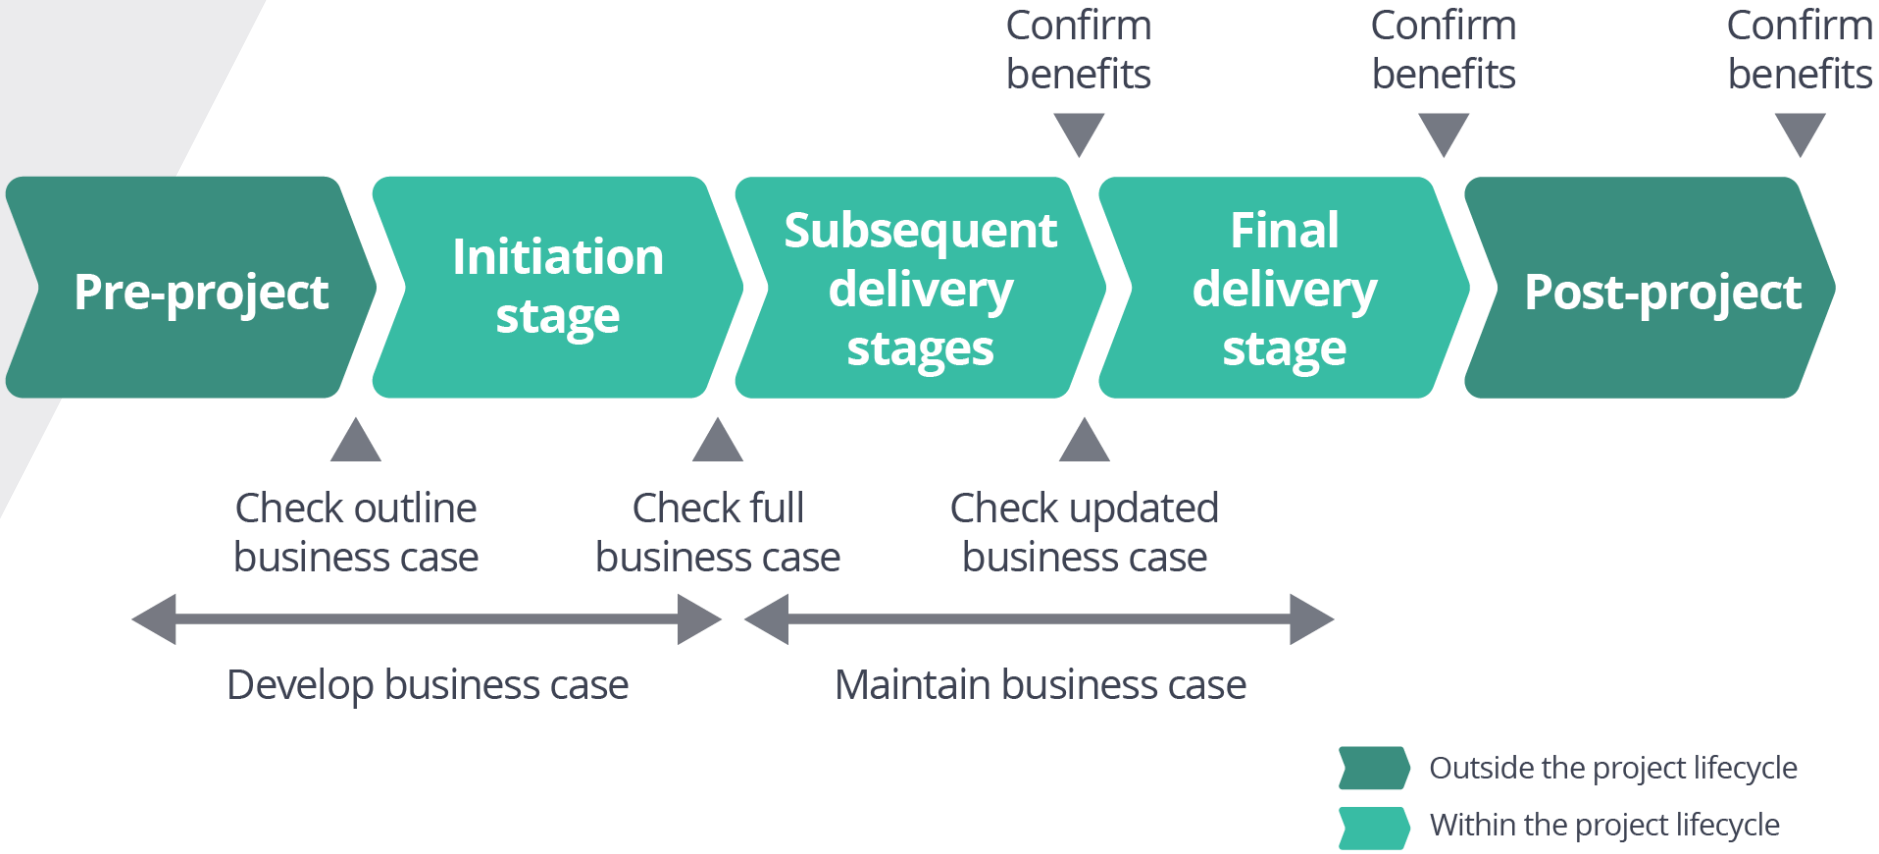


Figure 5.3 Business case through the project lifecycle

Copyright © 2025 PeopleCert International Limited.

Business case

Documents the business justification for a project, based on:

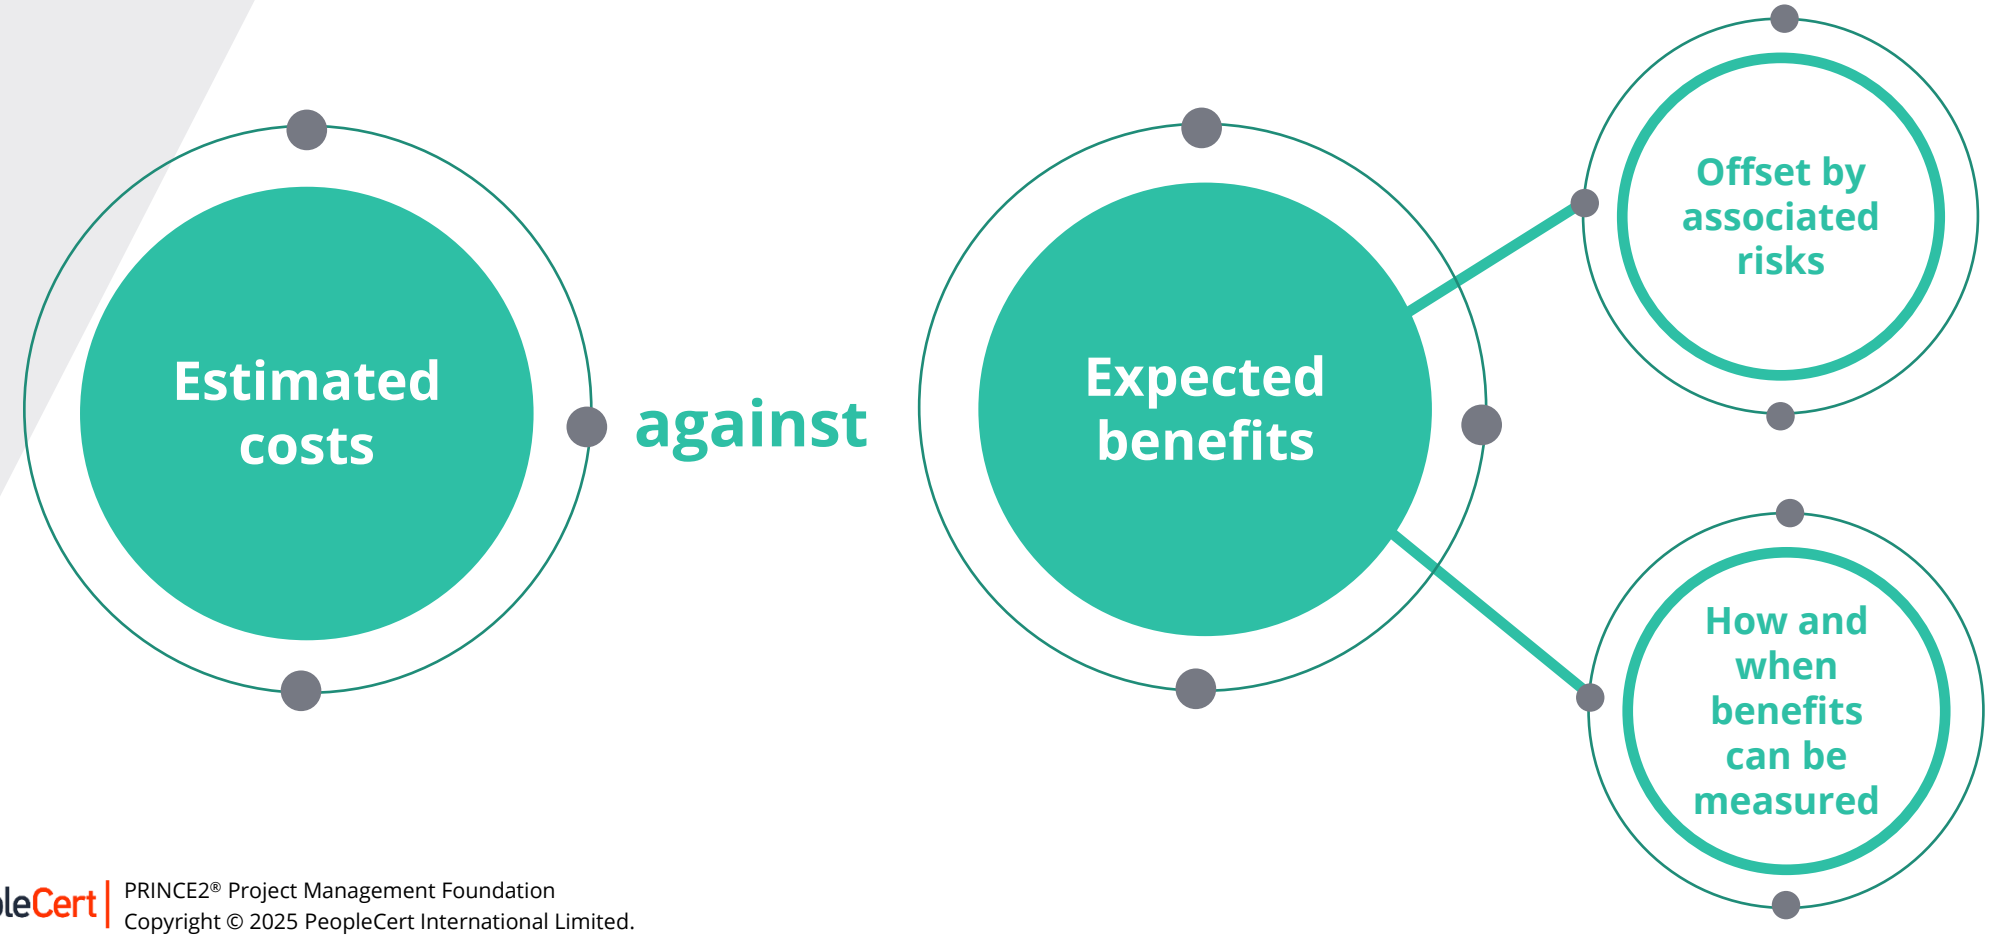

Copyright © 2025 PeopleCert International Limited.

The benefits management approach

The benefits management approach defines the **management actions** that will be put in place to ensure that the project's **outcomes** are achieved and confirm that the project's **benefits** are realized.



Copyright © 2025 PeopleCert International Limited.


Sustainability management approach



Copyright © 2025 PeopleCert International Limited.


Applying the principles



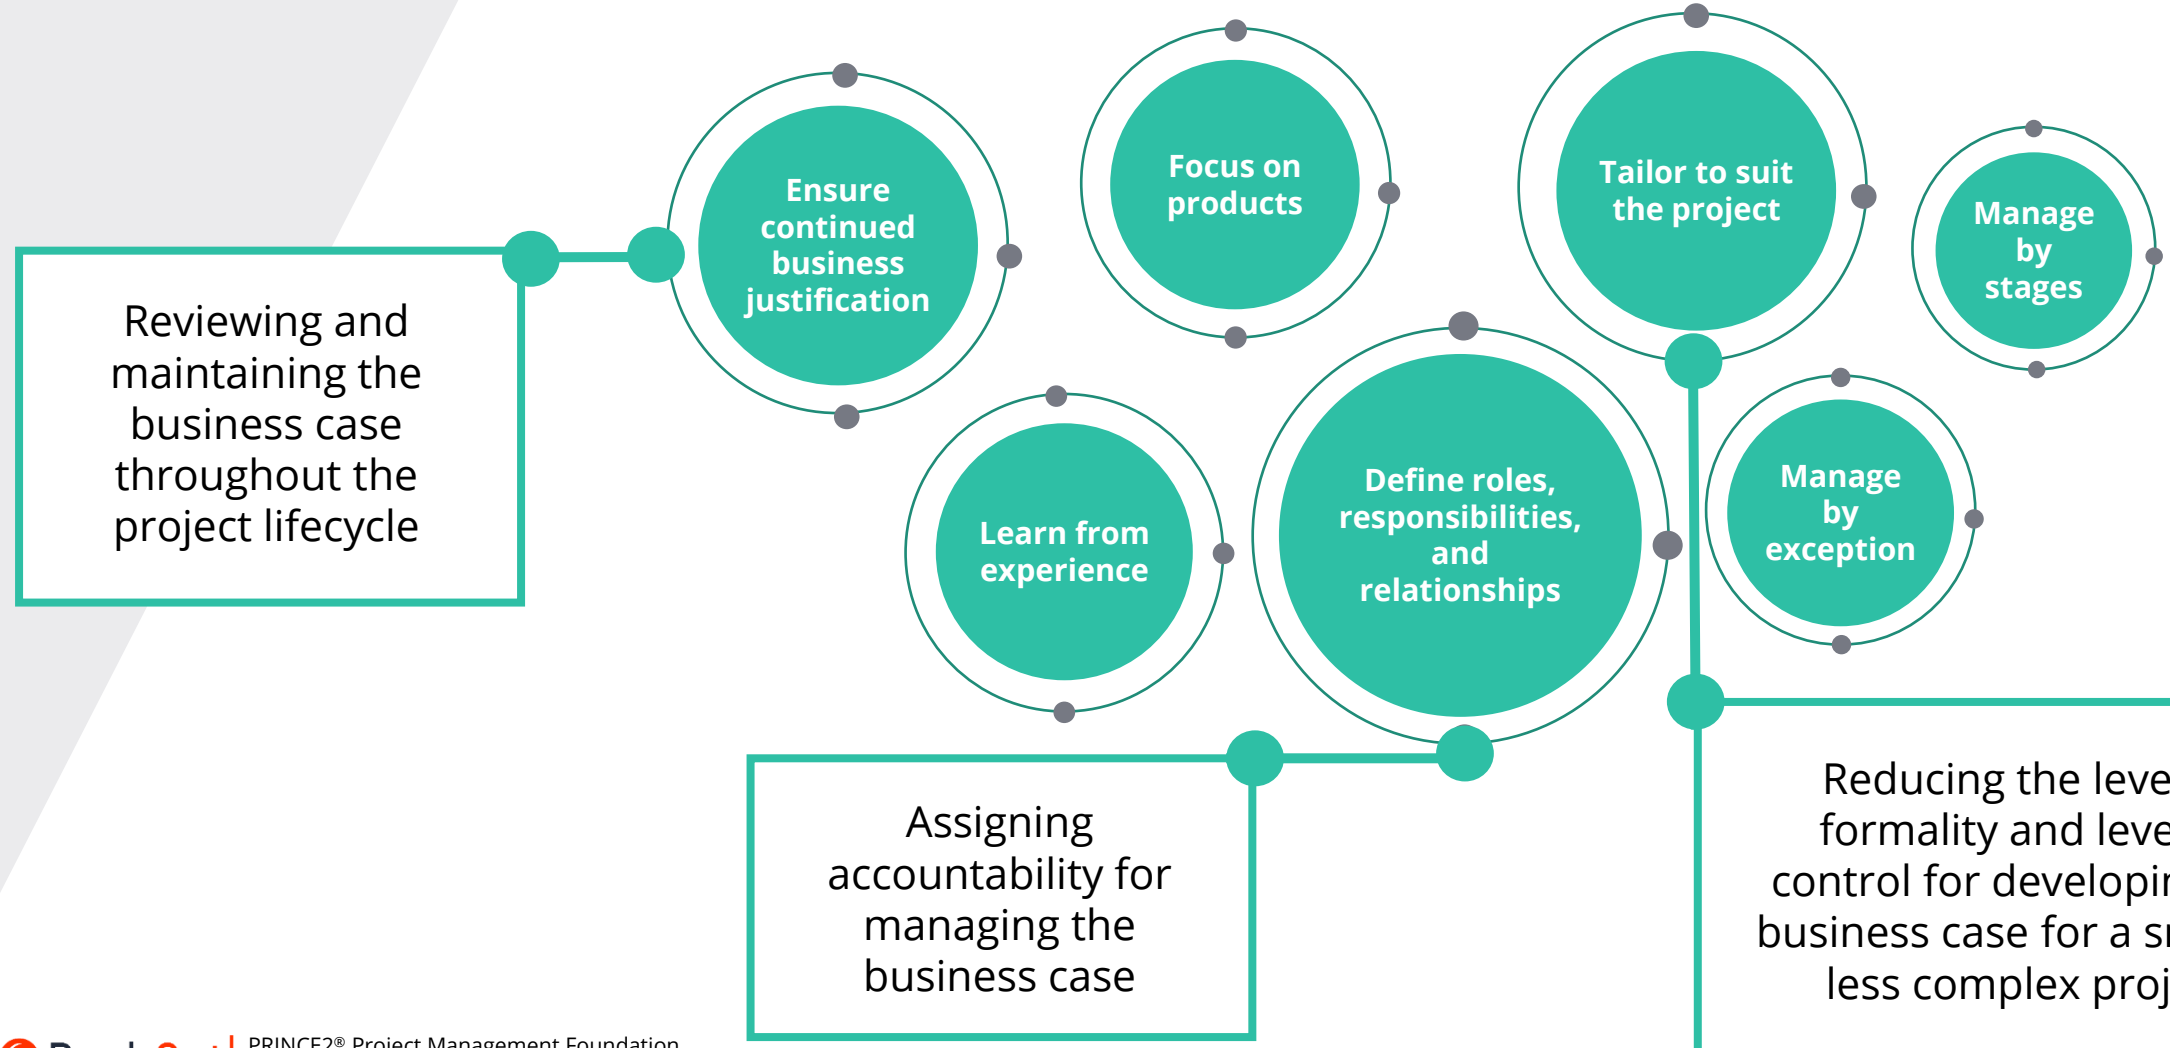


Copyright © 2025 PeopleCert International Limited.

Supporting techniques for the business case

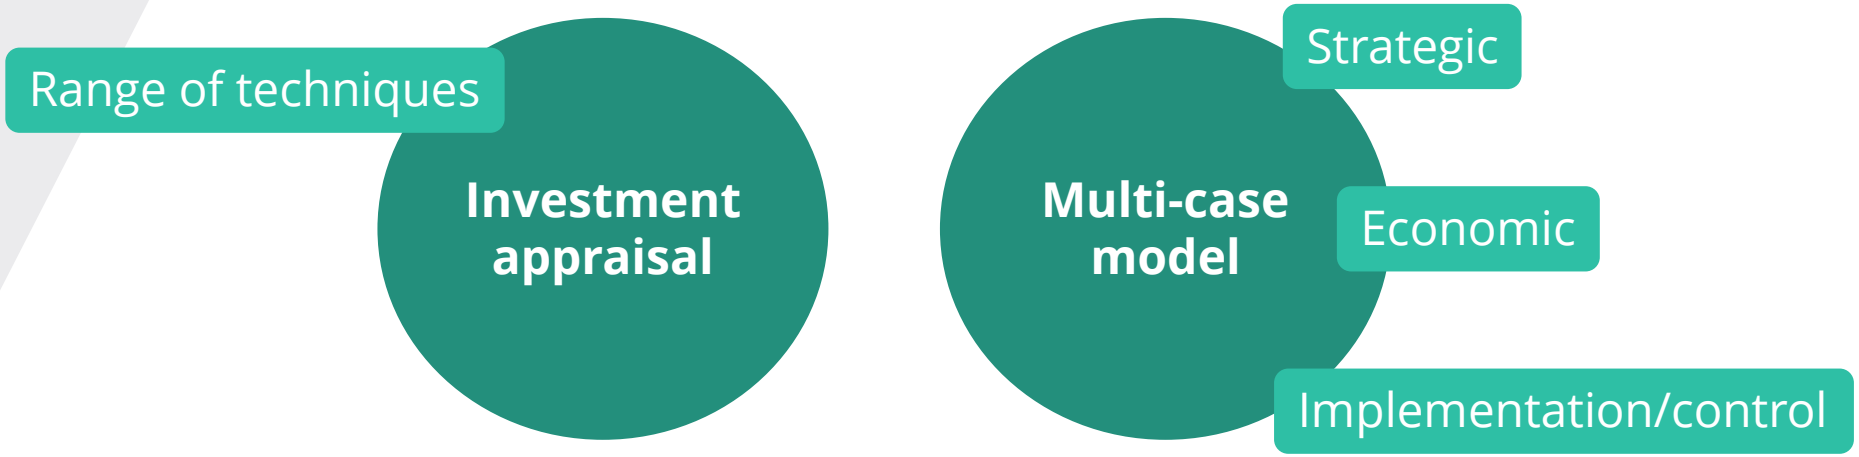

Copyright © 2025 PeopleCert International Limited

Applying the business case practice

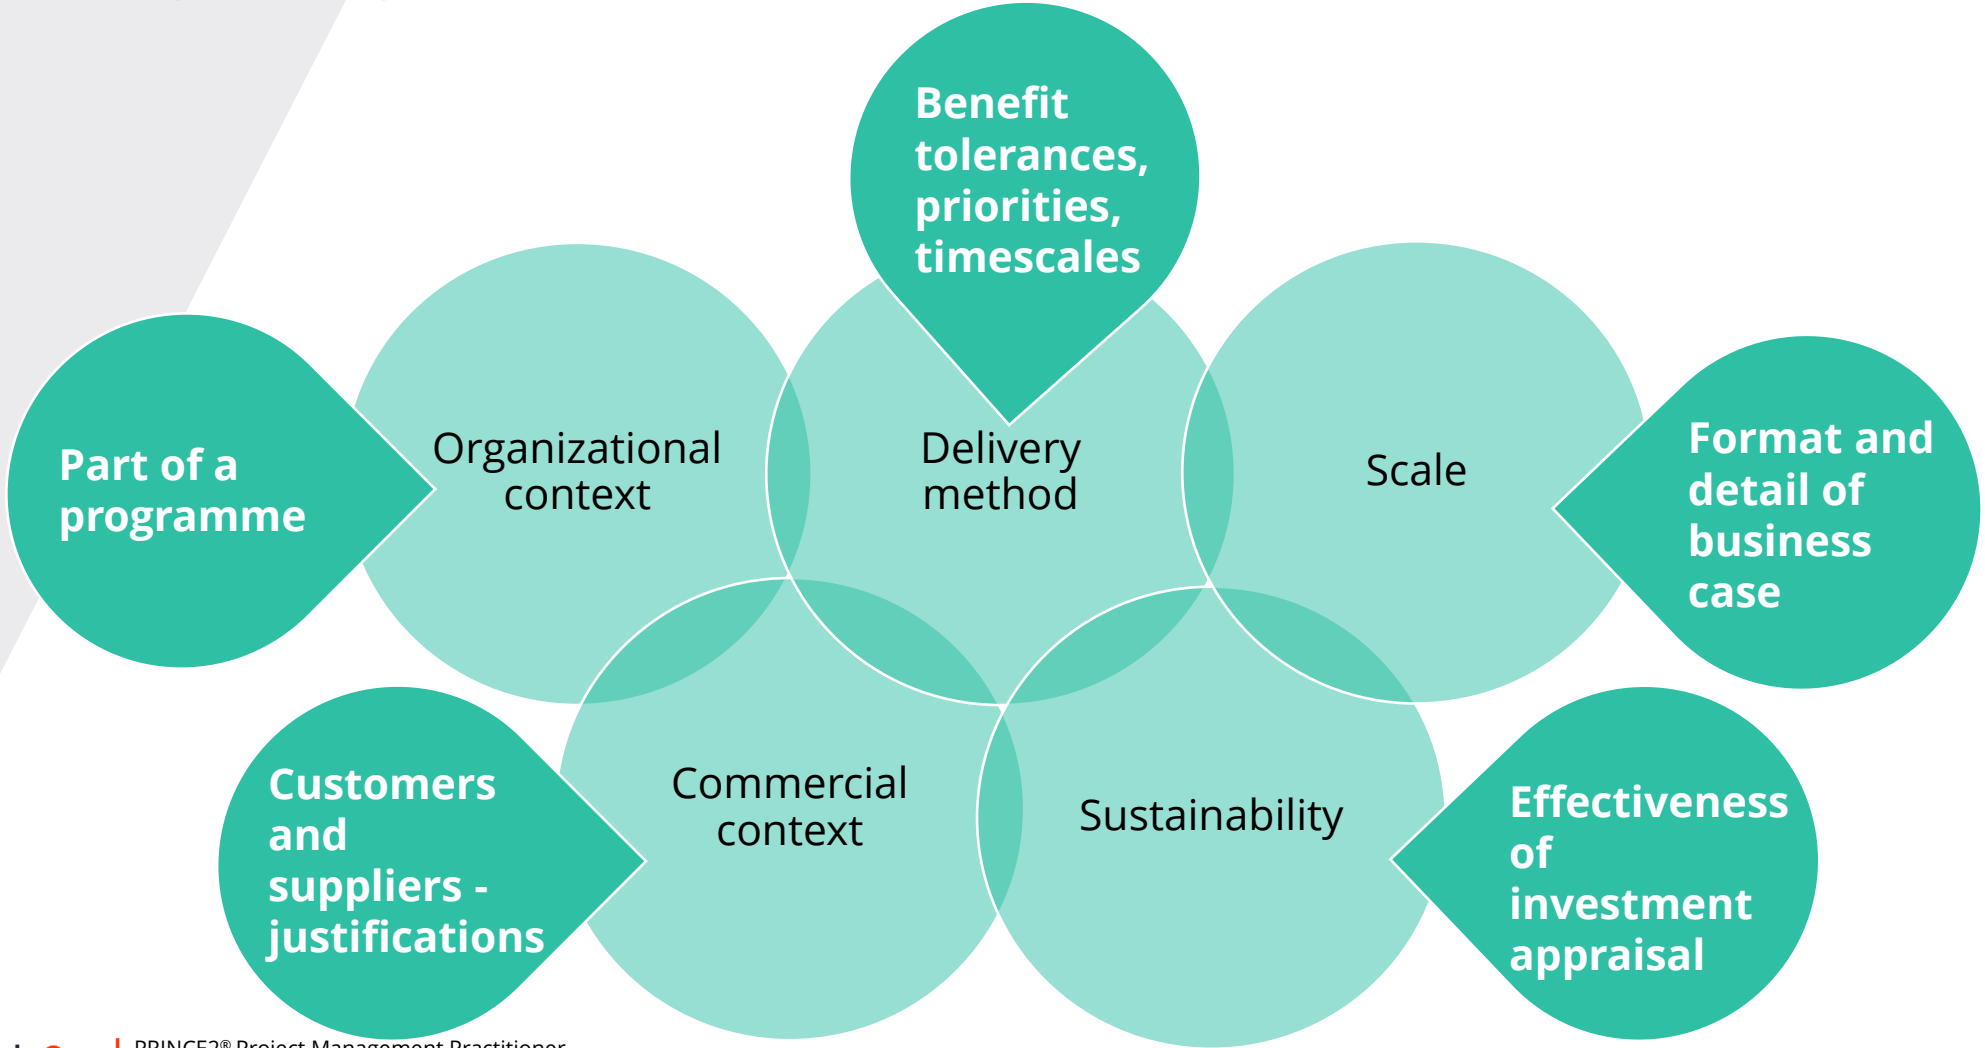

Copyright © 2025 PeopleCert International Limited

25 minutes

Business case

Activity

The business case

Objective: describe the key concepts related to business justification and the differences between them.

Task: draft the outline business case for NowByou, focusing on the reasons, benefits, and major risks of the project.

25 minutes



Use your Learner Workbook to note down your ideas.

Copyright © 2025 PeopleCert International Limited.

Why?

Reason

- Discrimination is growing at a concerning rate.

Benefits

- raising awareness
- increased brand recognition.



Copyright © 2025 PeopleCert International Limited.

Major risks



Financial aid from donors and partners may decrease due to external factors.



High-level requirements gathering could be flawed, resulting in an awareness campaign delivering wrong messages.



Low project management maturity may result in poor control over the project, leading to delays and overspending.

Copyright © 2025 PeopleCert International Limited.

Module 6

Plans

Purpose of the plans practice

The purpose of the plans practice is to facilitate **communication** and **control** by defining the products and the means of delivering them:

What? **By whom?** **How?**

Where? **When?** **Why?**



Copyright © 2025 PeopleCert International Limited.

Definition of a plan

A **proposal** that outlines the what, where, when, how, who and cost of the project as a whole (or a subset of activities).



Copyright © 2025 PeopleCert International Limited.

Plans in PRINCE2 Project Management



Copyright © 2025 PeopleCert International Limited.

How PRINCE2 Project Management's plans relate to each other


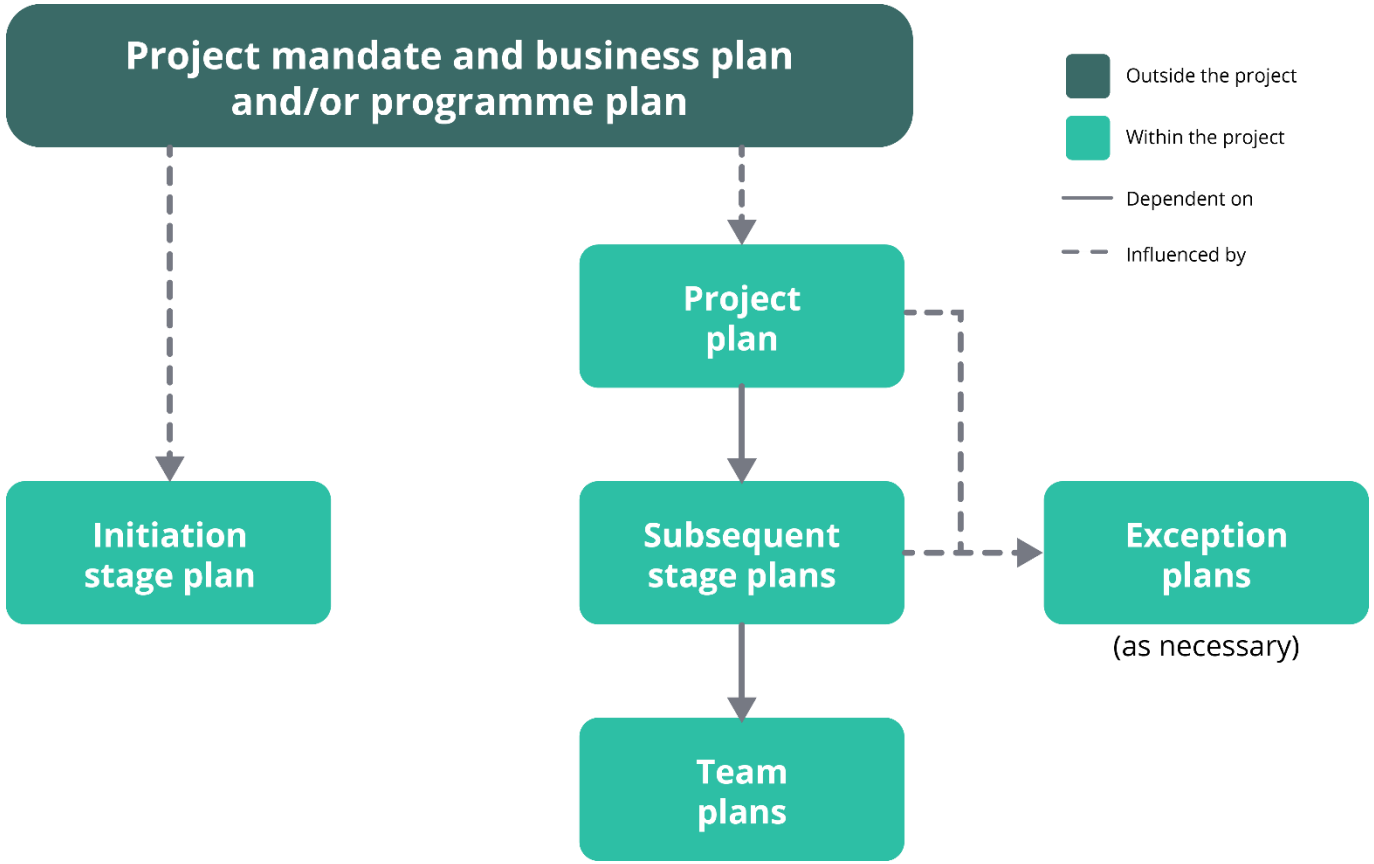


Figure 7.1 Relationship between PRINCE2 Project Management plans

Copyright © 2025 PeopleCert International Limited.

Stages



Factors to balance:

- delivery method
- sequence of activities
- people and resources
- key decision points
- risk
- time horizon.

Number of stages based on:

- nature of products and necessary delivery activities
- trade-off between degree of control and management involvement.


Length of stages determined by:

- complexity
- risk
- planning horizon
- decision points
- alignment with programme activities.

Copyright © 2025 PeopleCert International Limited.

Stages and work packages

An example

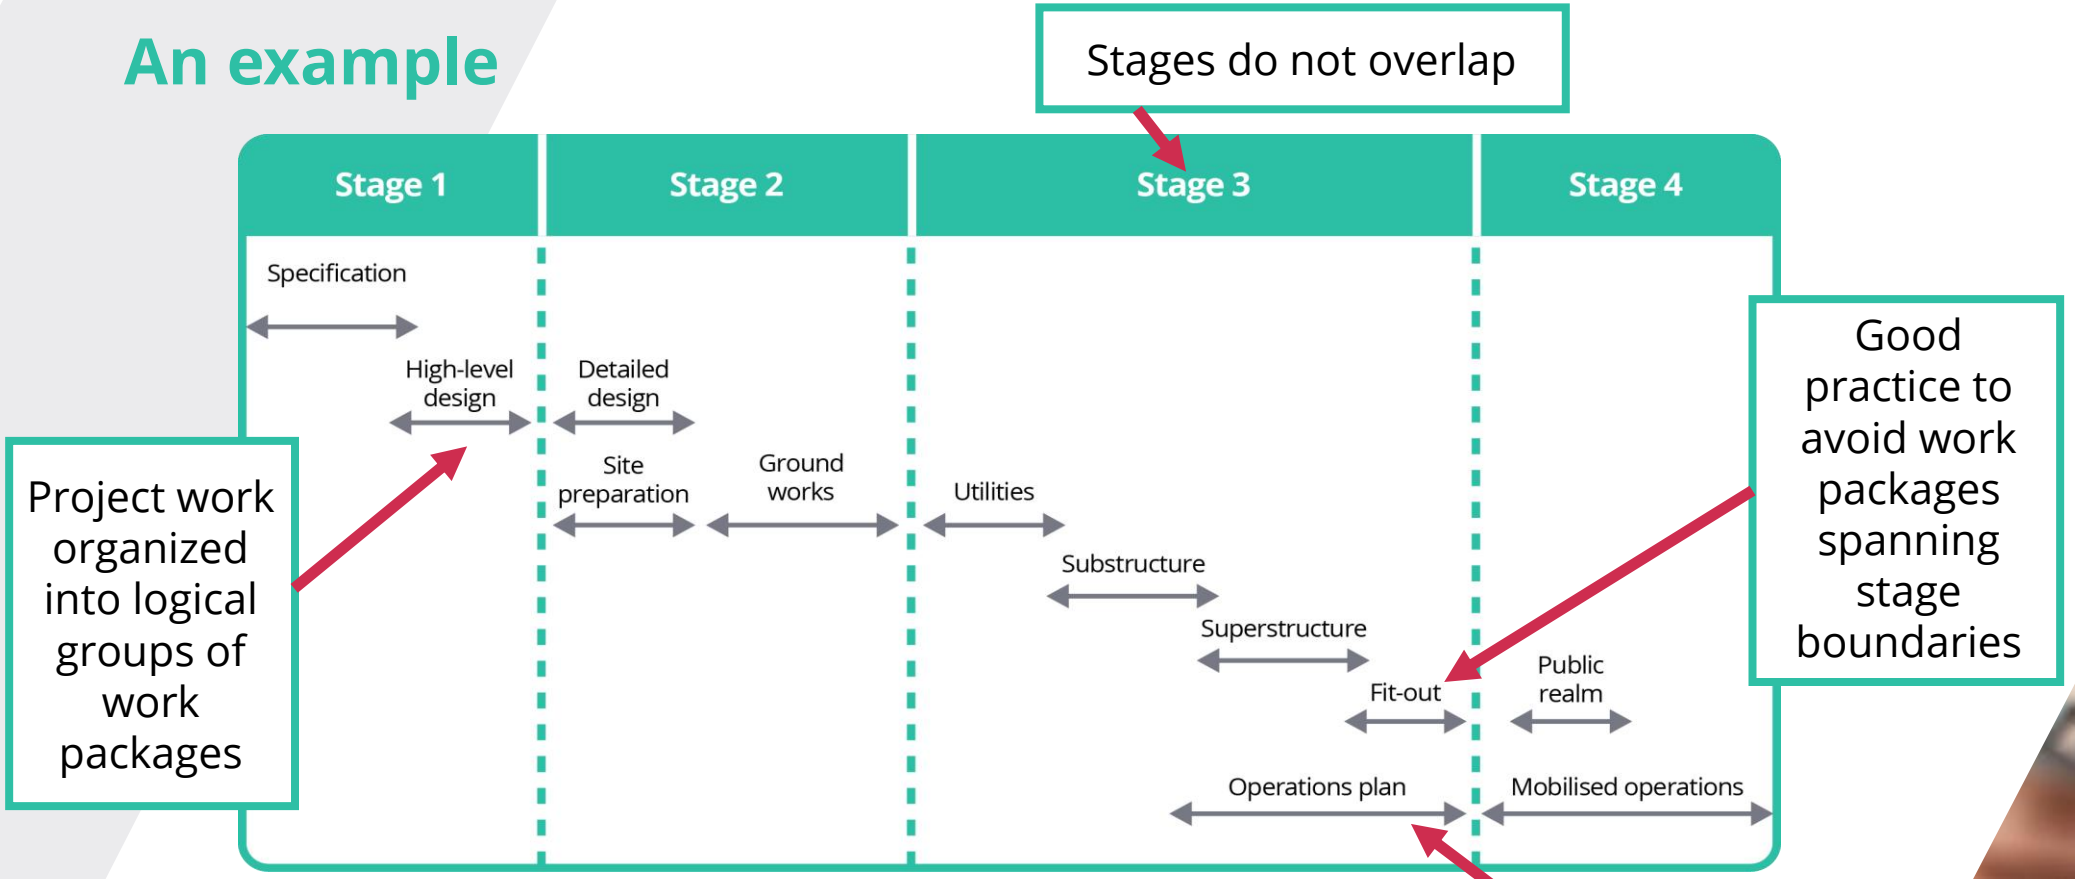

Adapted from Figure 7.2 Illustration of stages and work packages



Copyright © 2025 PeopleCert International Limited.

Tolerances in planning



Copyright © 2025 PeopleCert International Limited.

Product-based planning

- **Focus on products** is a PRINCE2 Project Management principle.
- **Identify the required products** first and then **determine the best way to deliver** them.



Copyright © 2025 PeopleCert International Limited.


PRINCE2 Project Management technique for planning

- throughout procedure
- decisions on inherent risks

- graphical representation
- sequence
- resource allocations

- costs of activities
- risk budget
- change budget
- cost tolerances

- plan has various parts
- narrative document helps explain at high level

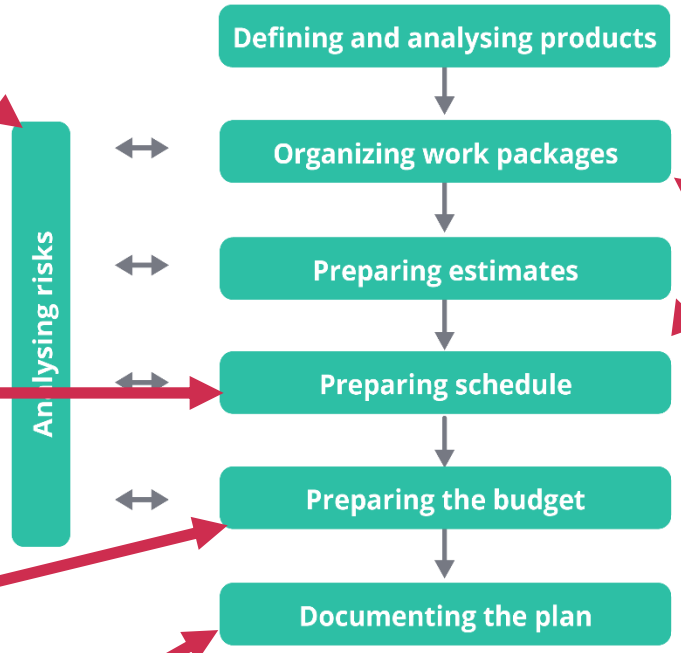

Repeated for:
- Project plan
- Stage plan
- Team plan

Adapted from Figure 7.3 The PRINCE2 Project Management planning technique

- **For project plan:** write a project product description.
- **For all levels of plan:** create a product breakdown structure, write product descriptions and create a product flow diagram.

- **products/activities** organized into work packages
- closely related **people, resources, activities**
- at least **one product**
- **dependencies:** documented
- no overlap

- resources
- people
- duration
- cost
- benefits
- risk

Copyright © 2025 PeopleCert International Limited.

Product breakdown structure


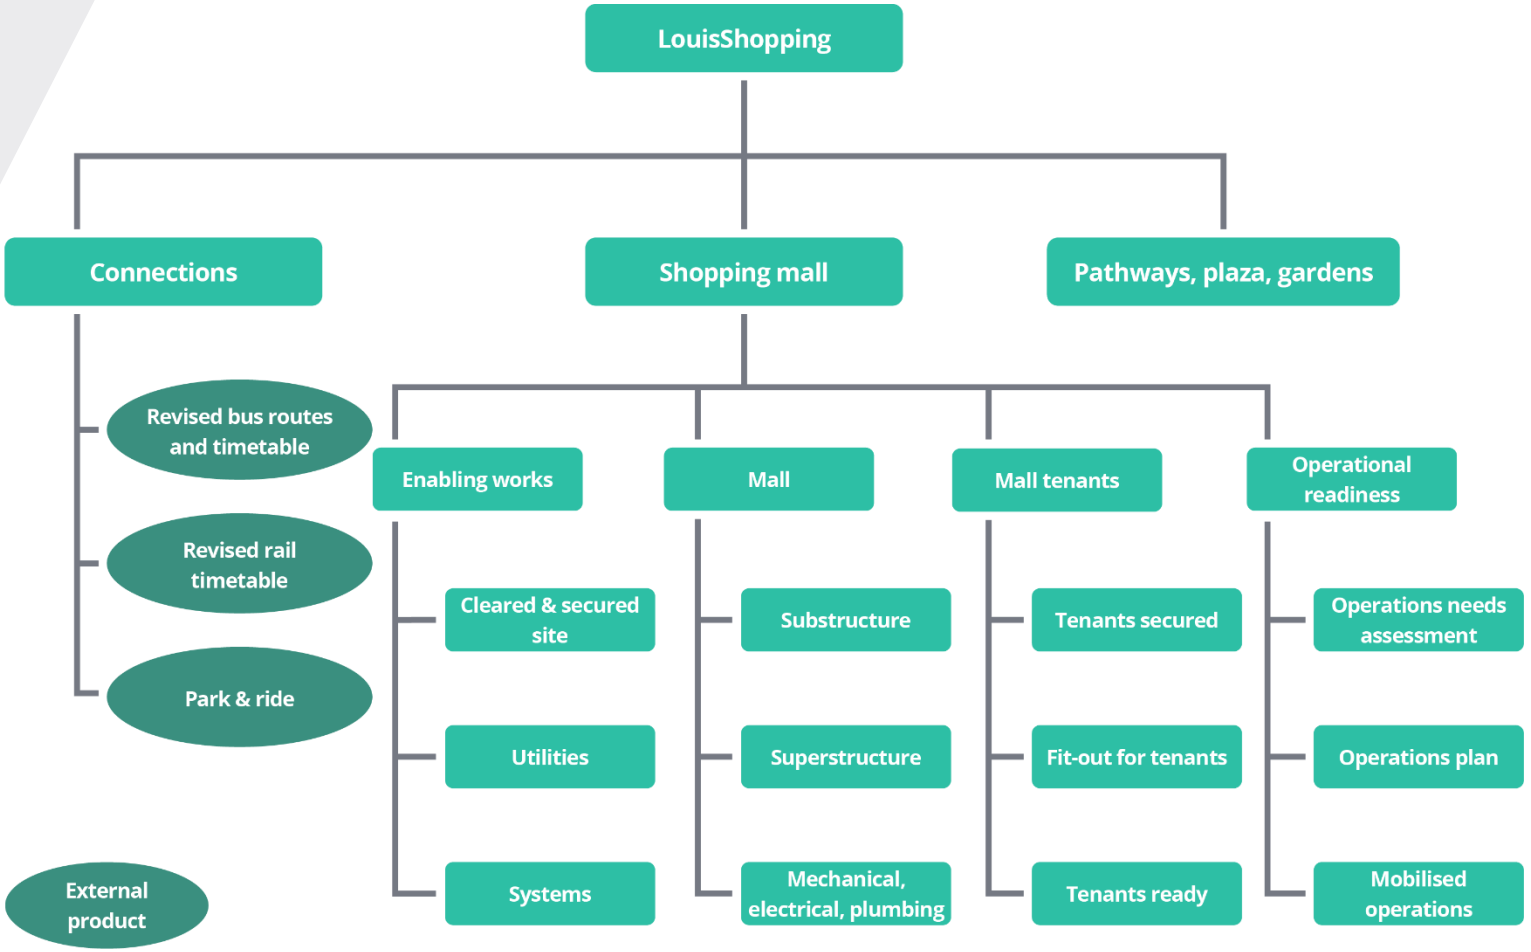


Figure 7.5 Product breakdown structure for LouisShopping project

Copyright © 2025 PeopleCert International Limited.

Management products

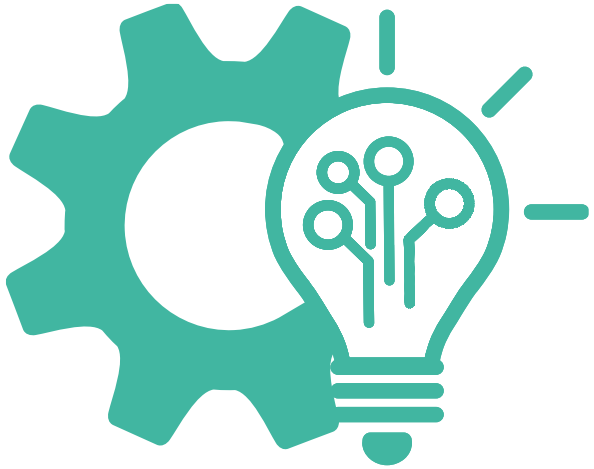

Plan

Project product description

Work package description

Copyright © 2025 PeopleCert International Limited.

Applying the principles



Aligning plan's performance targets to the business case objectives

Ensure continued business justification

Focus on products

Tailor to suit the project

Manage by stages

Sharing planning lessons for future projects

Learn from experience


Define roles, responsibilities, and relationships

Manage by exception

Defining levels of plan and establishing targets and tolerances for them


Copyright © 2025 PeopleCert International Limited.

Supporting techniques for the plans practice

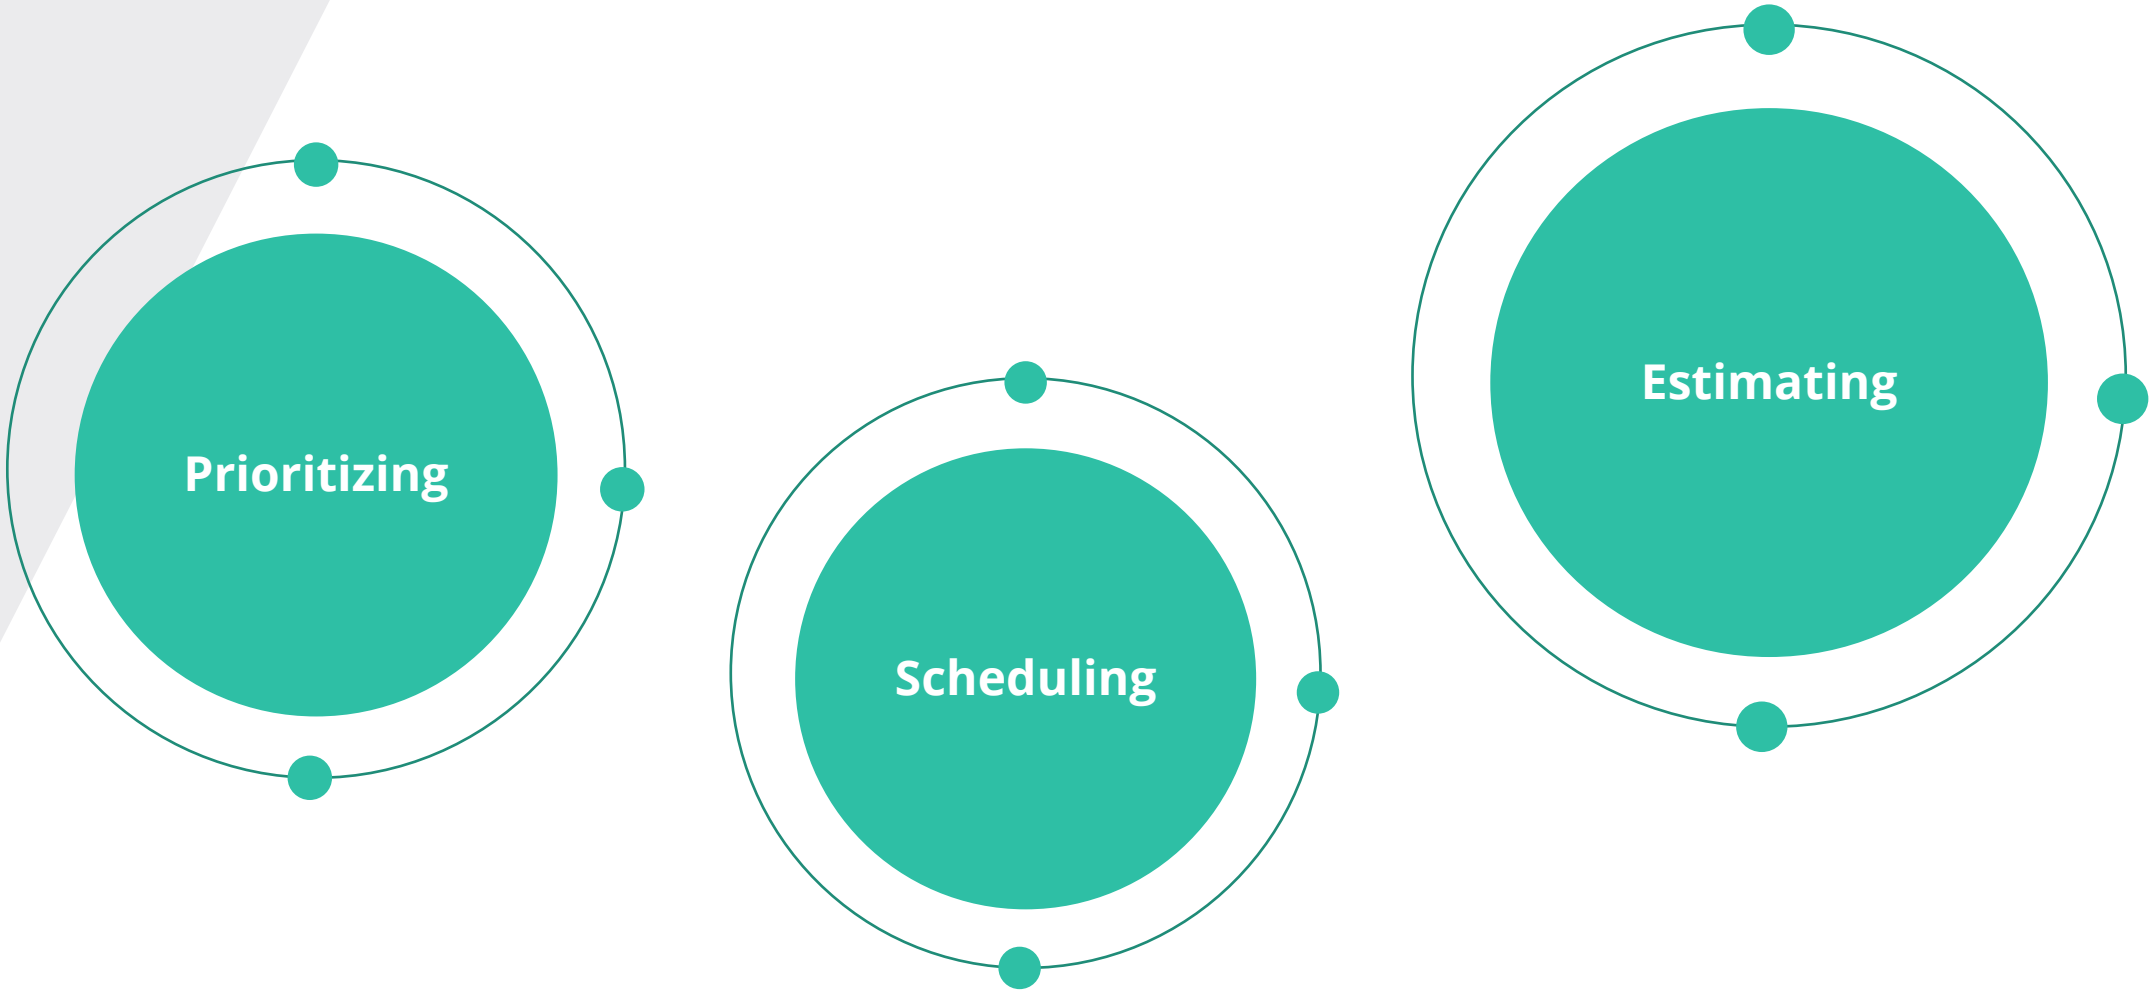

Copyright © 2025 PeopleCert International Limited

Applying the plans practice

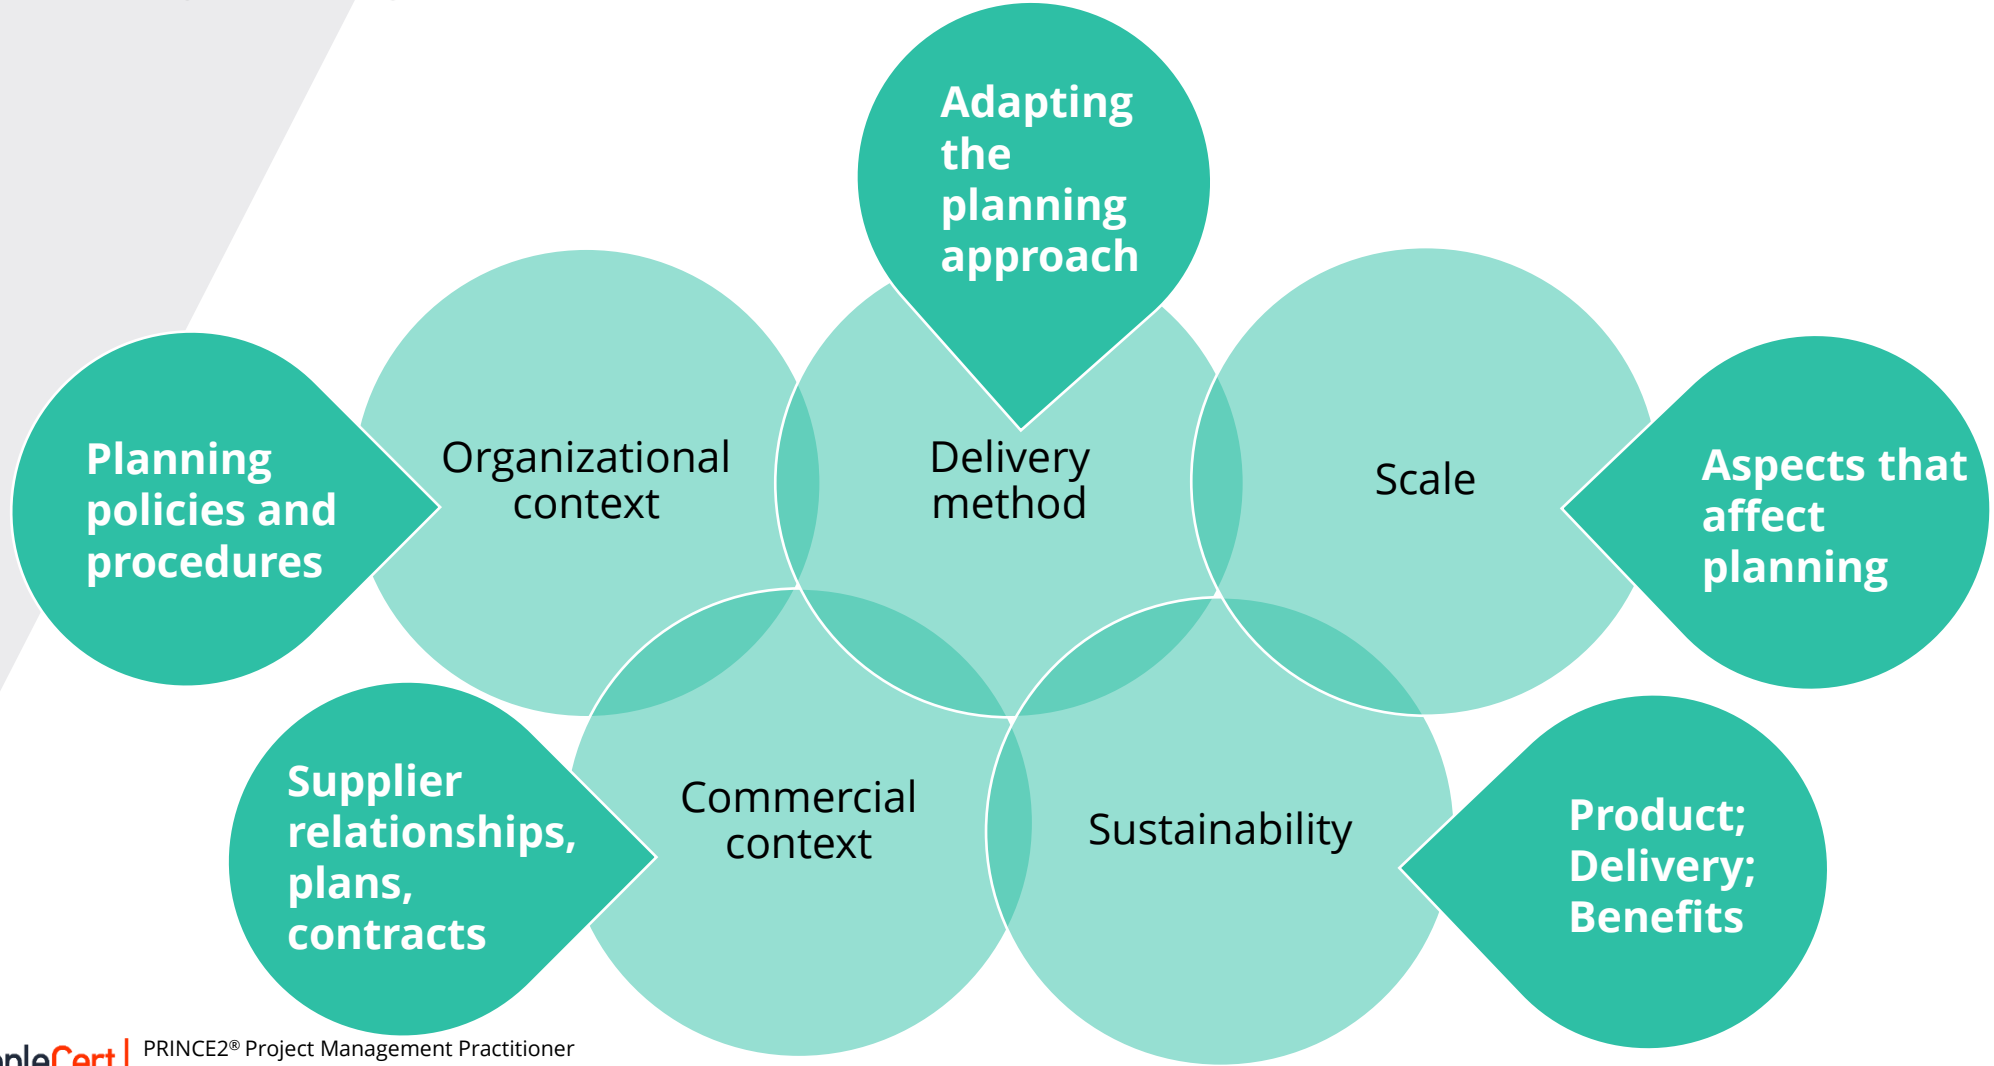

Copyright © 2025 PeopleCert International Limited

20 minutes

Plans

Activity


Create a product breakdown structure

Create a draft product breakdown structure using the information in the NowByou scenario.



Copyright © 2025 PeopleCert International Limited.

NowByou: Suggested product breakdown structure

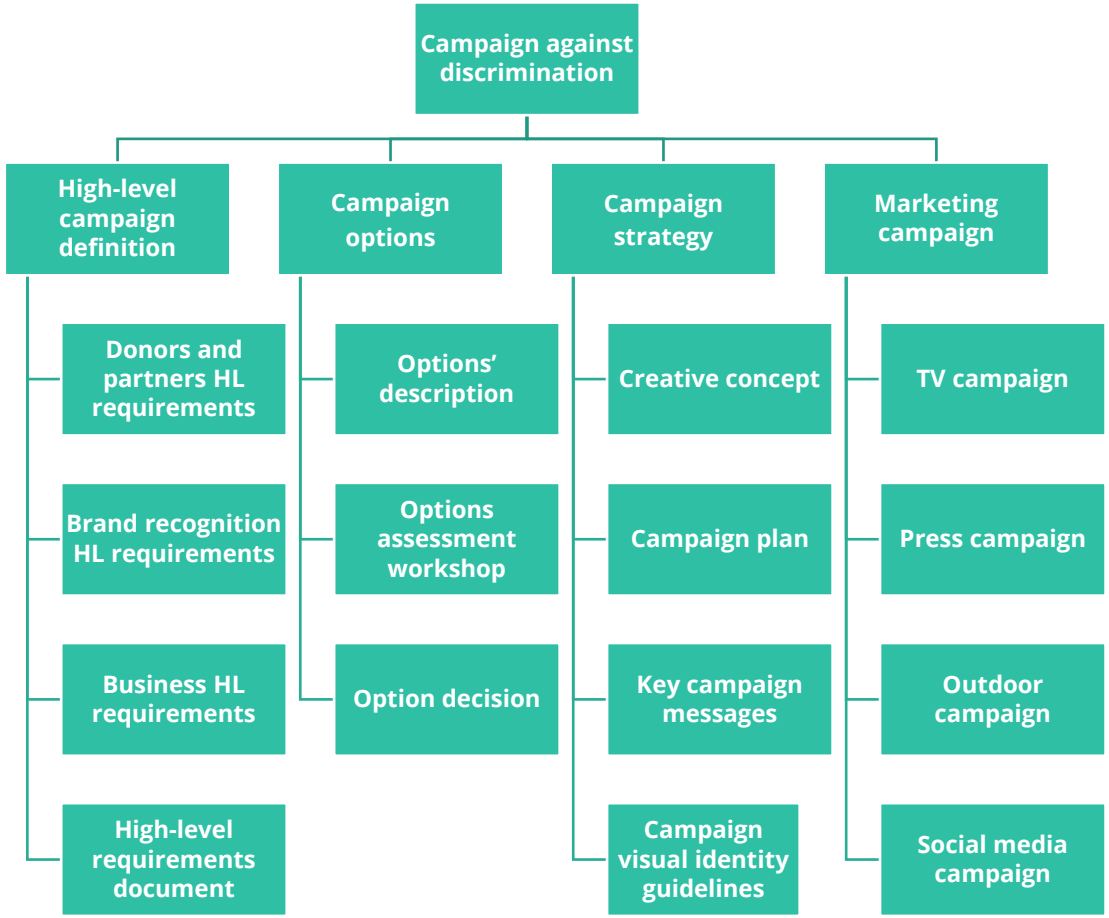

Copyright © 2025 PeopleCert International Limited.

Module 7

Quality

The purpose of the quality practice

The purpose of the quality practice is to **document** the **user's requirements** of the project products and to **establish** the **means** by which they will be **met.**



Copyright © 2025 PeopleCert International Limited.

Quality terminology


A. Quality → 1. A statement about the quality expected from the project product, captured in the project product description.

B. Requirement → 2. The degree to which a set of inherent characteristics of a product, service, process, person, organization, system, or resource fulfils requirements.

C. User's quality expectations → 3. A prioritized list of criteria that the project product must meet before the user will accept it.

D. Acceptance criteria → 4. A description of the quality measures that will be applied by those performing quality control and the levels that the finished product must meet.

E. Quality specifications → 5. A need or expectation that is documented in an approved management product.

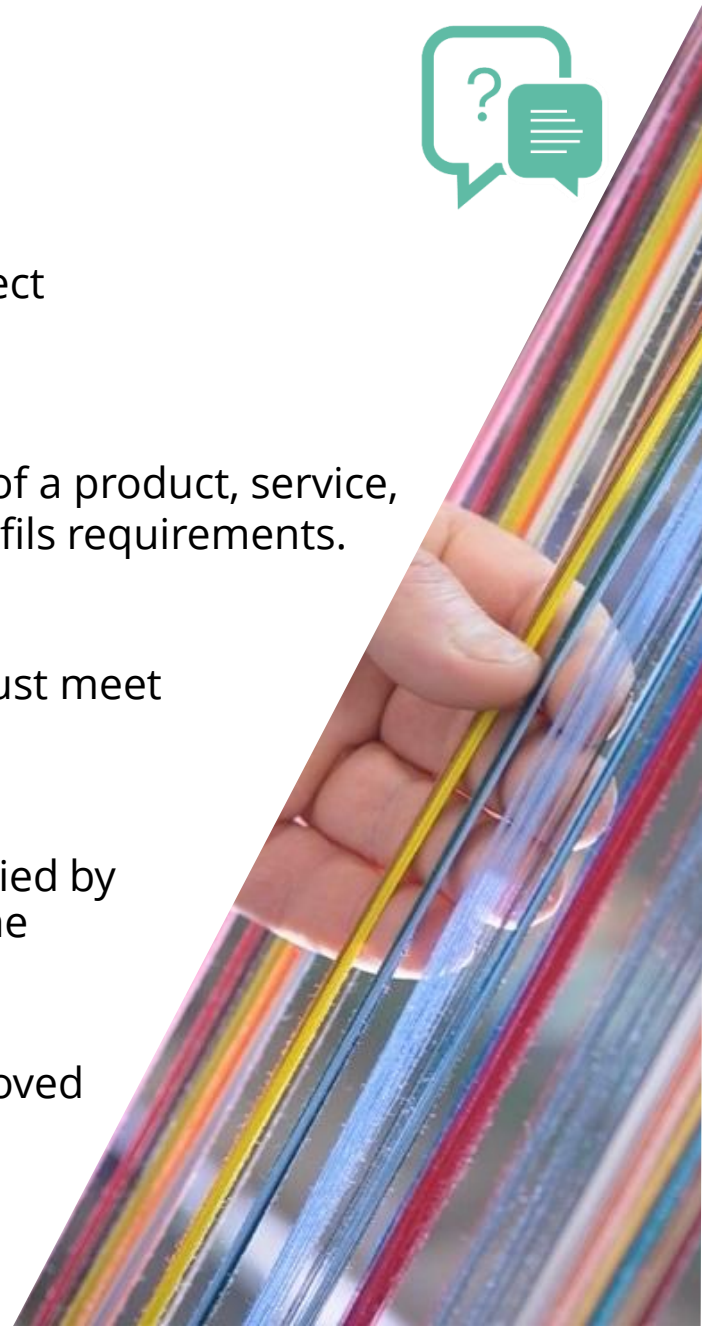

Copyright © 2025 PeopleCert International Limited.

Quality terminology | Answer

A. Quality → 2. The degree to which a set of inherent characteristics of a product, service, process, person, organization, system, or resource fulfils requirements.

B. Requirement → 5. A need or expectation that is documented in an approved management product.

C. User's quality expectations → 1. A statement about the quality expected from the project product, captured in the project product description.

D. Acceptance criteria → 3. A prioritized list of criteria that the project product must meet before the user will accept it.

E. Quality specifications → 4. A description of the quality measures that will be applied by those performing quality control and the levels that the finished product must meet.



Copyright © 2025 PeopleCert International Limited.

Product-based quality approach




Aims to translate requirements into acceptance criteria and quality specifications for project products and the activities to deliver them.

Avoids work that cannot be traced back to the project's business justification.

Clear traceability of quality specifications and control to required products.

Copyright © 2025 PeopleCert International Limited.

Quality management

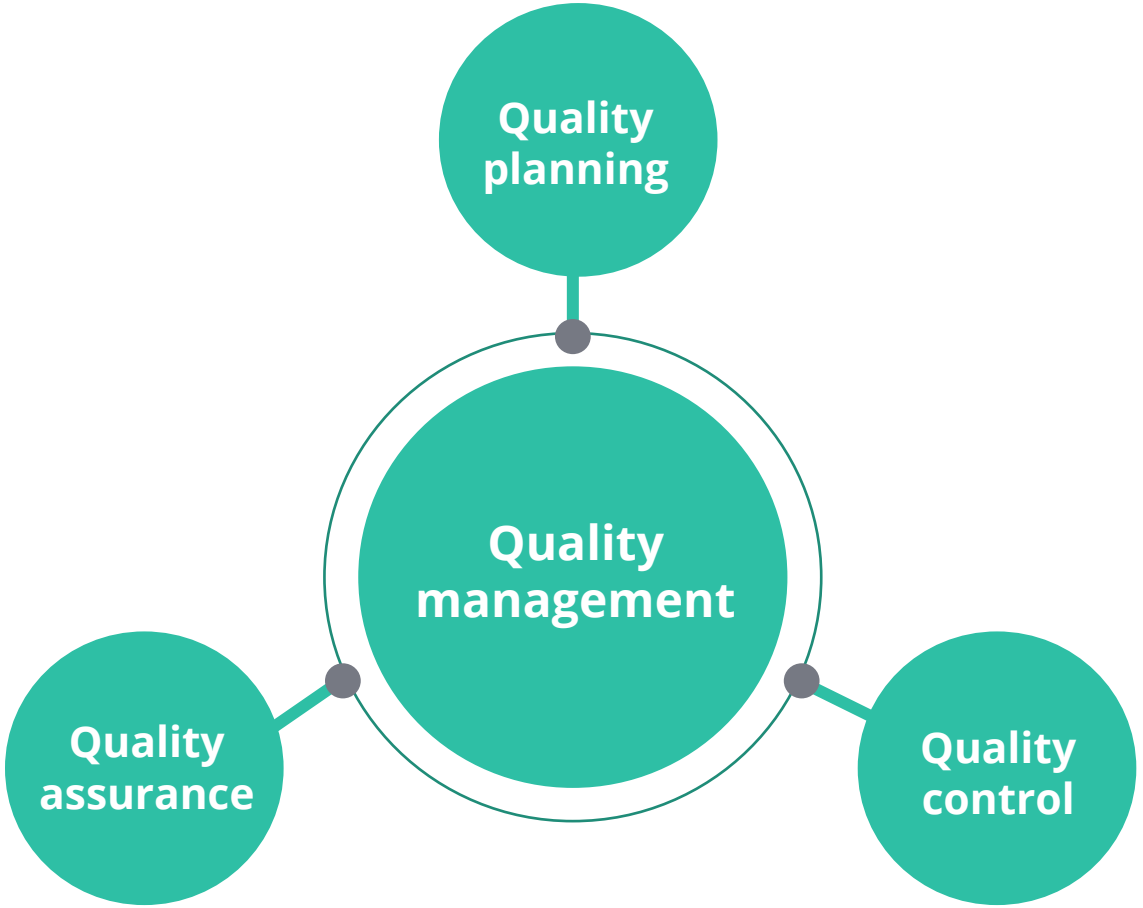

Copyright © 2025 PeopleCert International Limited.

Quality planning



The **capturing** of **quality specifications** for the project products and **generating** the associated **product descriptions** and quality management approach.

Identify major products of the project in terms of user's quality expectations and acceptance criteria.

Elicit user requirements and detail them as quality specifications.

Develop the quality management approach.

Obtain project board approval.

Copyright © 2025 PeopleCert International Limited.

Quality control



The **procedures** to monitor the **specific products** of a project and their development or delivery activities to determine whether they **comply** with **relevant standards** and of identifying ways to minimize causes of unsatisfactory performance.

- **Implement quality management approach.**
- **Assess quality issues and raise exceptions, if necessary.**
- **Obtain user approval of products.**

Copyright © 2025 PeopleCert International Limited.

Quality assurance



A **planned and systematic activity** that provides **confidence** that **products** will **meet** their defined **quality specifications** when tested under quality control. Quality assurance activities are typically performed by the business, ensuring they are **independent from the project team.**

Ensures the quality control techniques are sufficient to confirm that the quality requirements can be met.

Quality assurance is not the same as project assurance.

Copyright © 2025 PeopleCert International Limited.

PRINCE2 Project Management quality management procedure

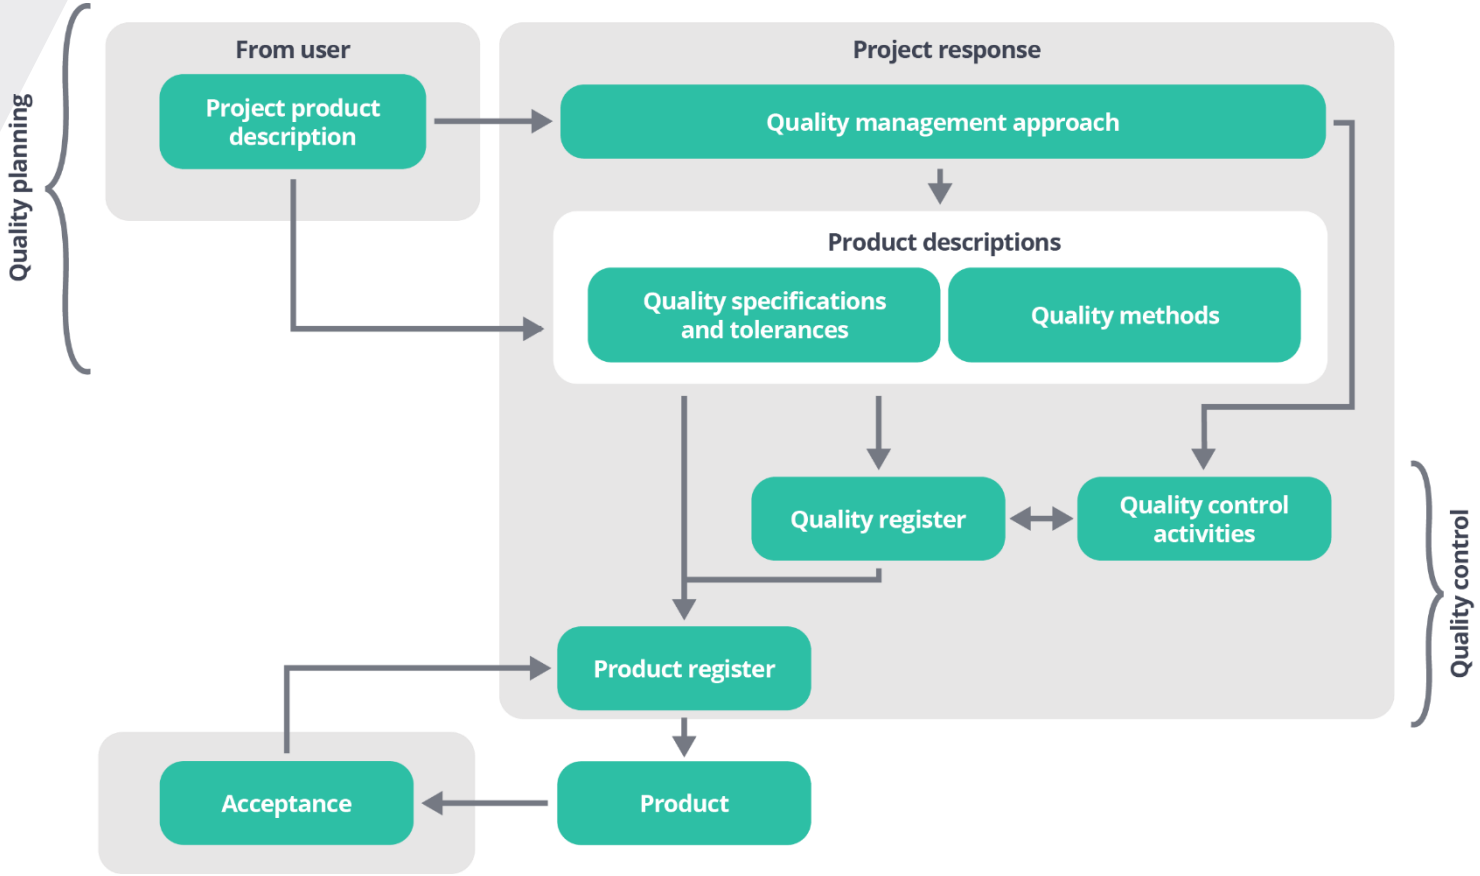


Figure 8.1 Product quality lifecycle

Copyright © 2025 PeopleCert International Limited.

Management products



Copyright © 2025 PeopleCert International Limited.

Applying the principles



Basing all quality planning and control activities on the project products

Ensure continued business justification

Focus on products

Tailor to suit the project

Manage by stages

Learn from experience

Define roles, responsibilities, and relationships

Manage by exception

Aligning quality controls and techniques with stage boundary controls

Establishing the quality tolerances approved by the project board in the project initiation documentation

Copyright © 2025 PeopleCert International Limited.


Supporting techniques for the quality practice

- Verification
- Validation
- Prototyping
- Testing
- Inspection
- Certification



Copyright © 2025 PeopleCert International Limited

Applying the quality practice

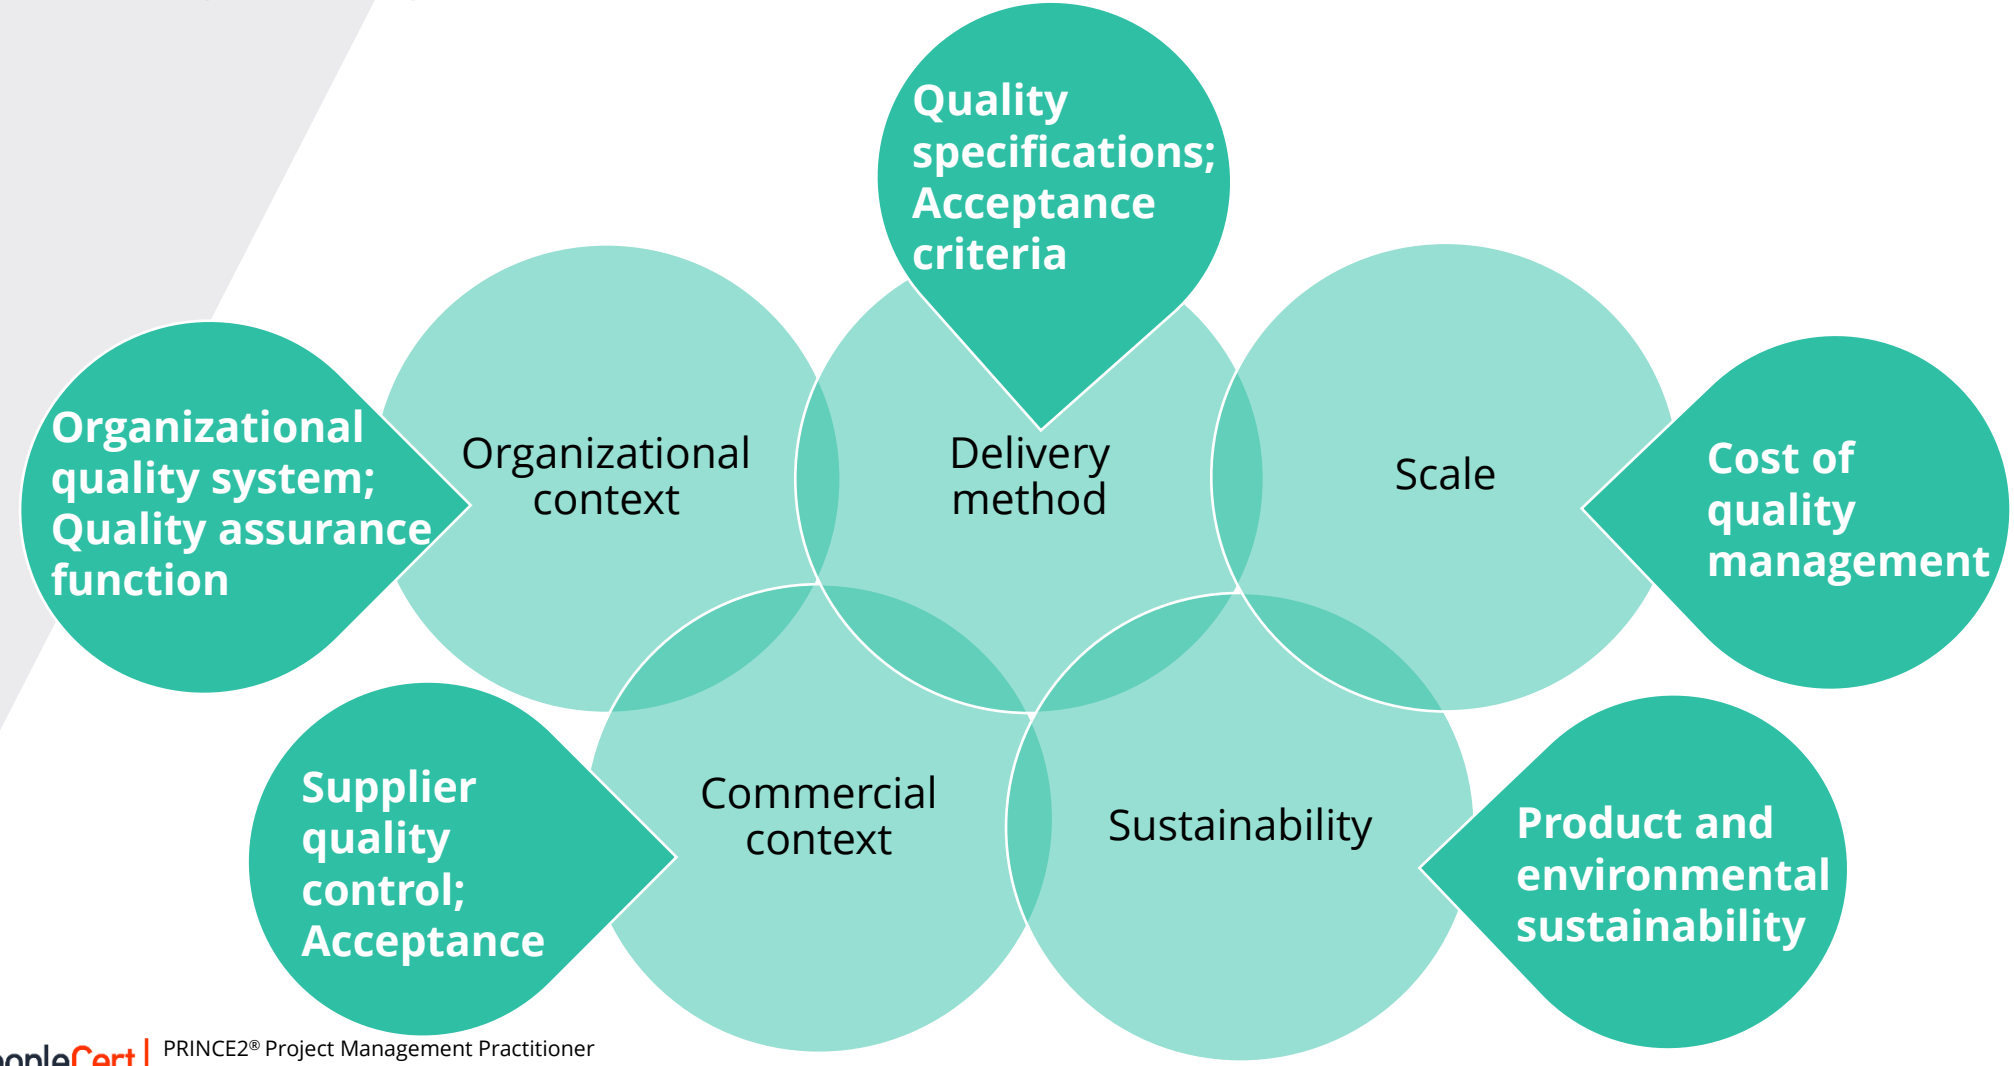

Copyright © 2025 PeopleCert International Limited

Module 8

Risk

The definition of risk



An **uncertain event** or set of events that, should they occur, will affect the achievement of objectives. A risk is measured by a combination of the **likelihood** of a perceived threat or opportunity occurring, and the magnitude of its **impact** on objectives.



Copyright © 2025 PeopleCert International Limited.

The purpose of the risk practice




The purpose of the PRINCE2 Project Management risk practice is to **identify, assess,** and **control uncertainties** and, as a result, improve the ability of the project to succeed.



Copyright © 2025 PeopleCert International Limited.

Key risk concepts

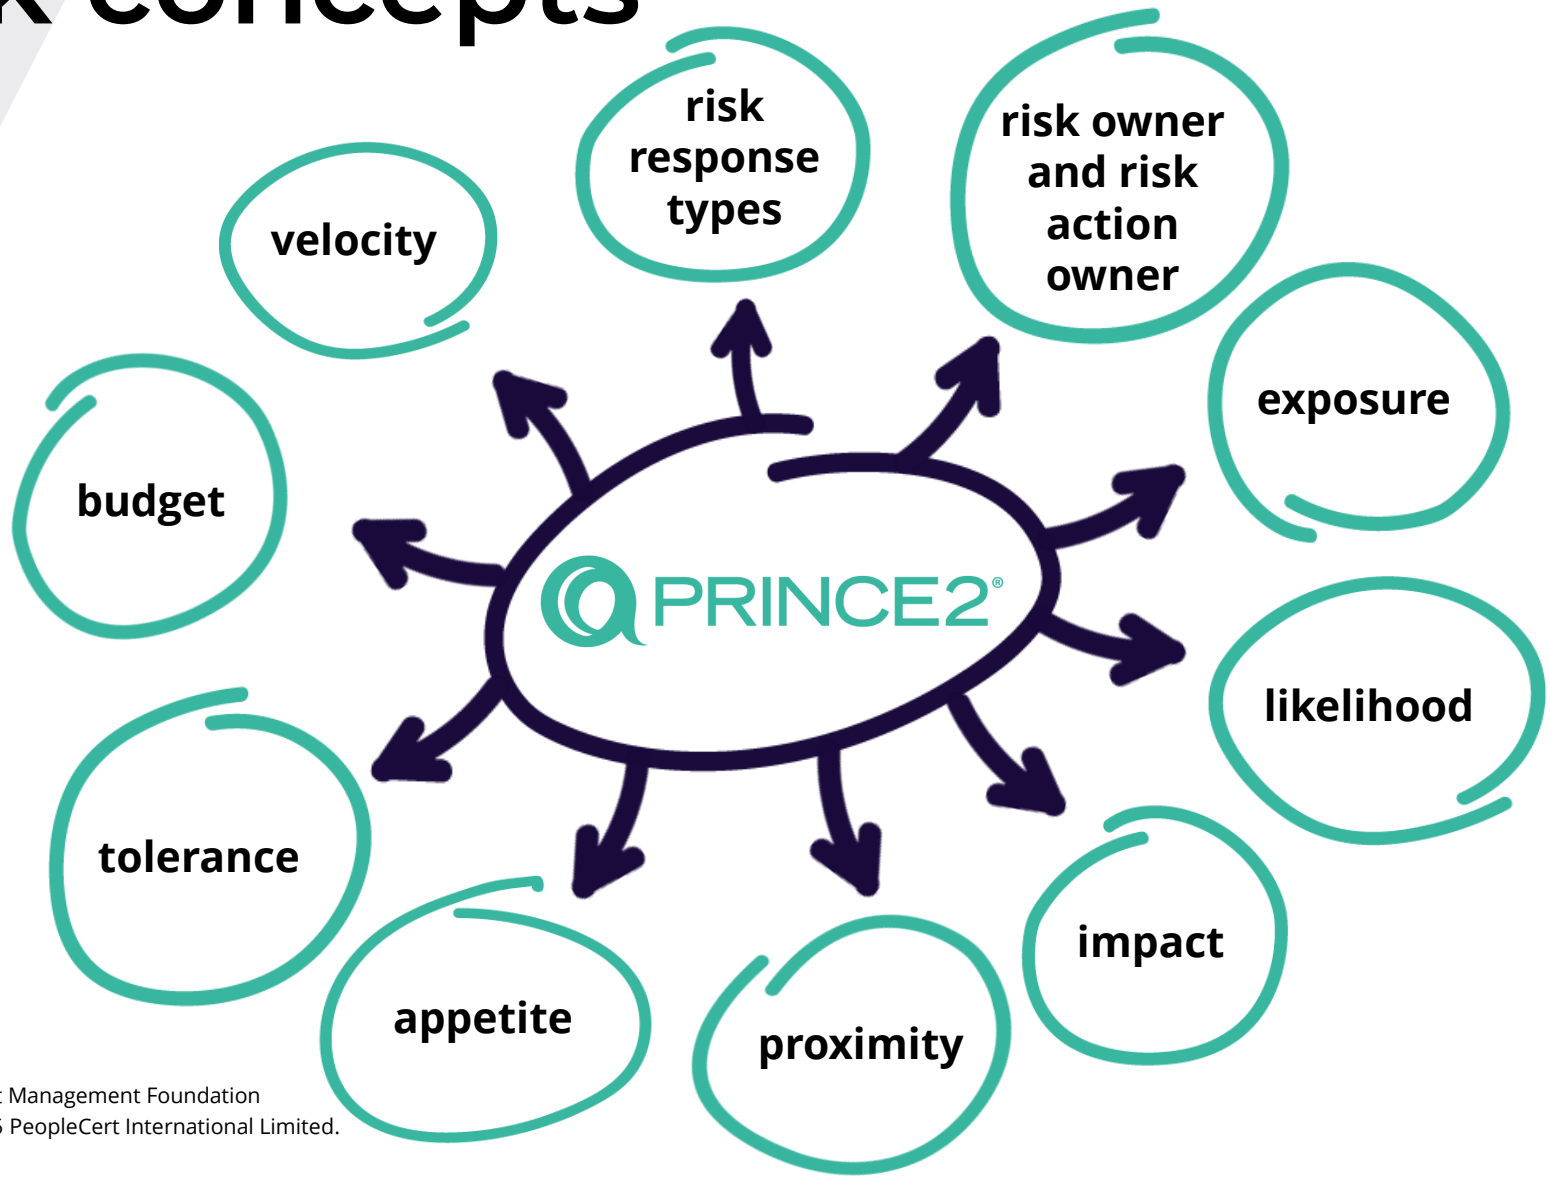

Copyright © 2025 PeopleCert International Limited.


Risk planning

Identify and prioritize risks using risk categories.



Copyright © 2025 PeopleCert International Limited.

Risk analysis

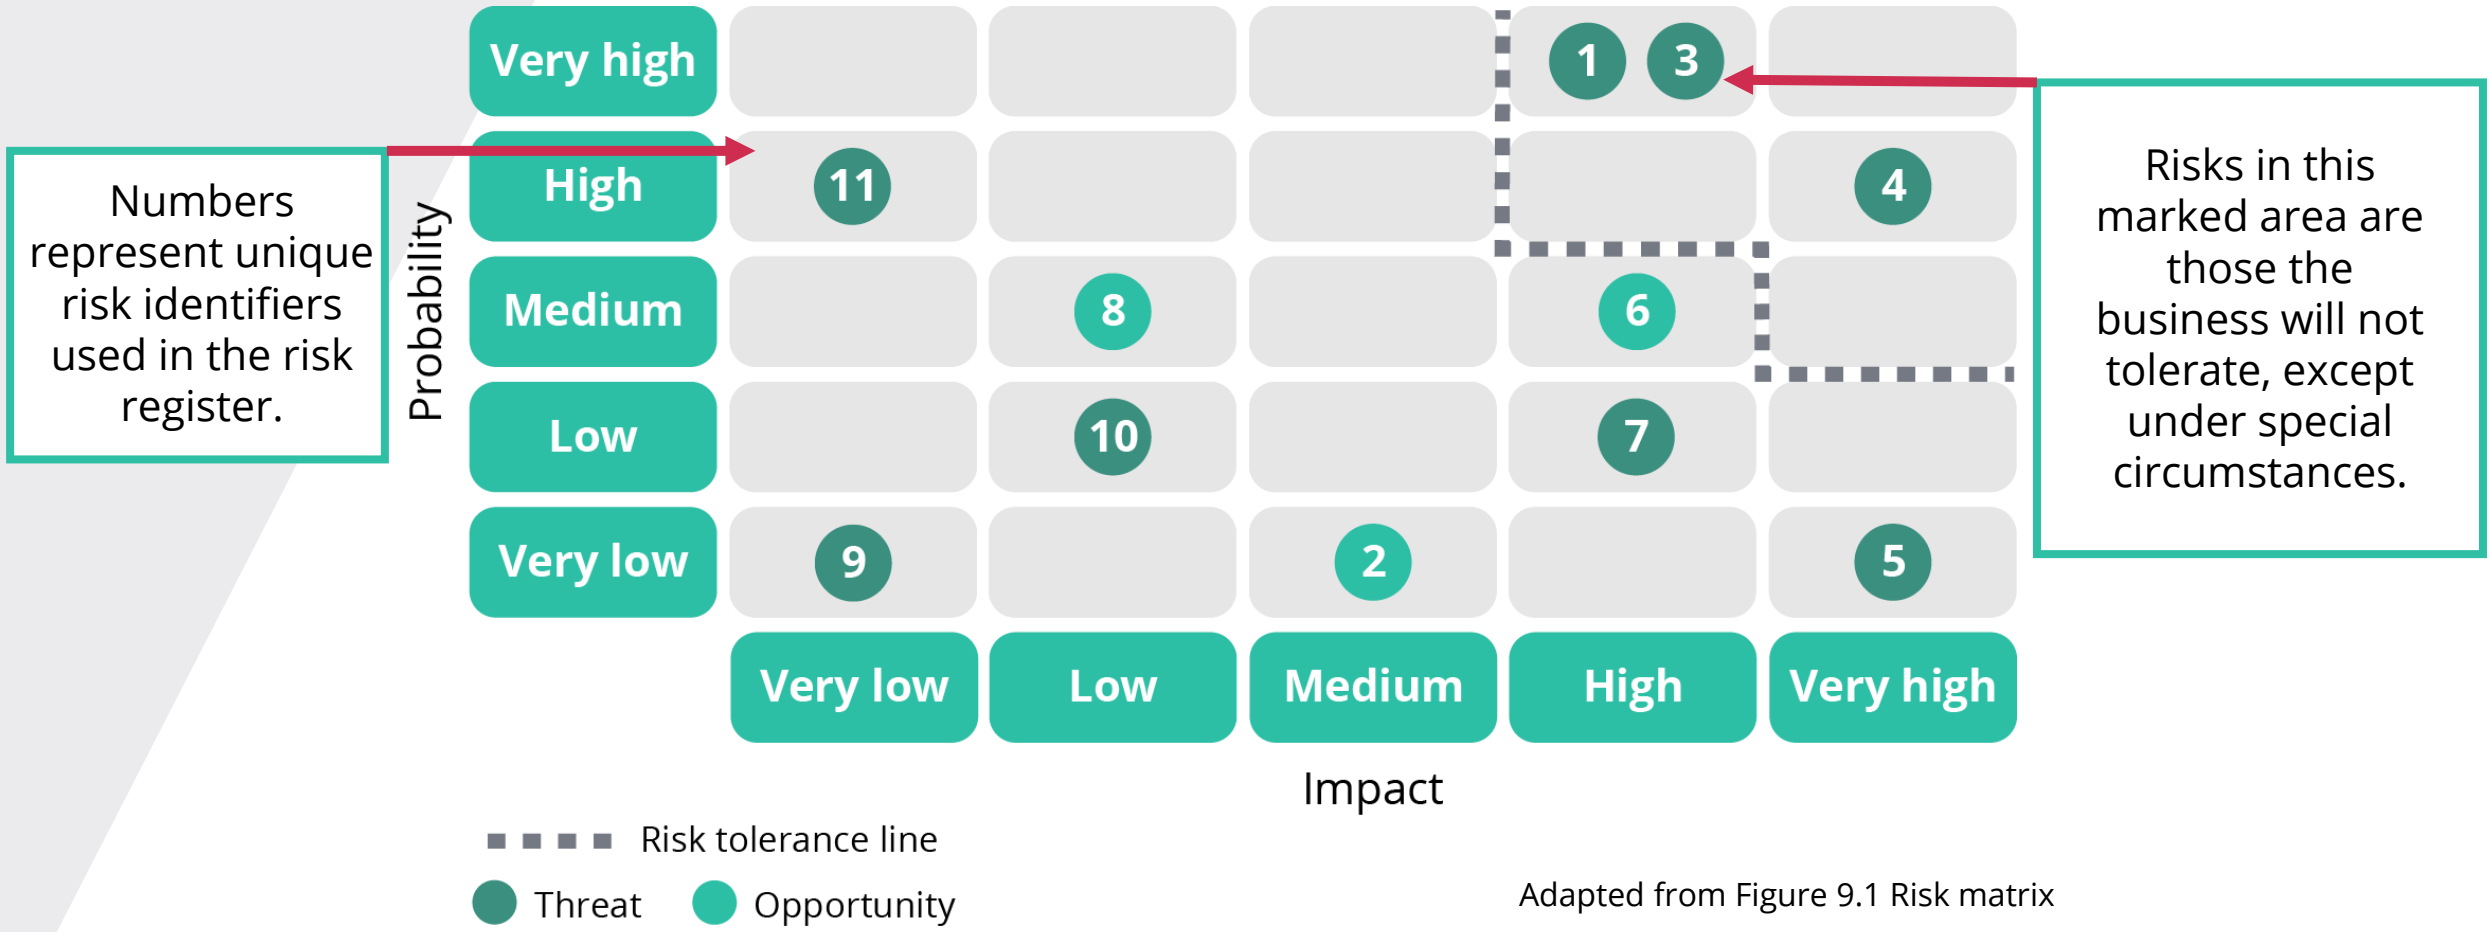

Adapted from Figure 9.1 Risk matrix

Copyright © 2025 PeopleCert International Limited.


Risk control

- **Risk response** depends on the situation and type of risk.
- It may lead to **residual** or **secondary** risks.
- **Risk owners** and **risk action owners** should be clearly identified.
- An explicit **risk budget** should be ring-fenced within the project's budget.



Copyright © 2025 PeopleCert International Limited.

Types of risk responses

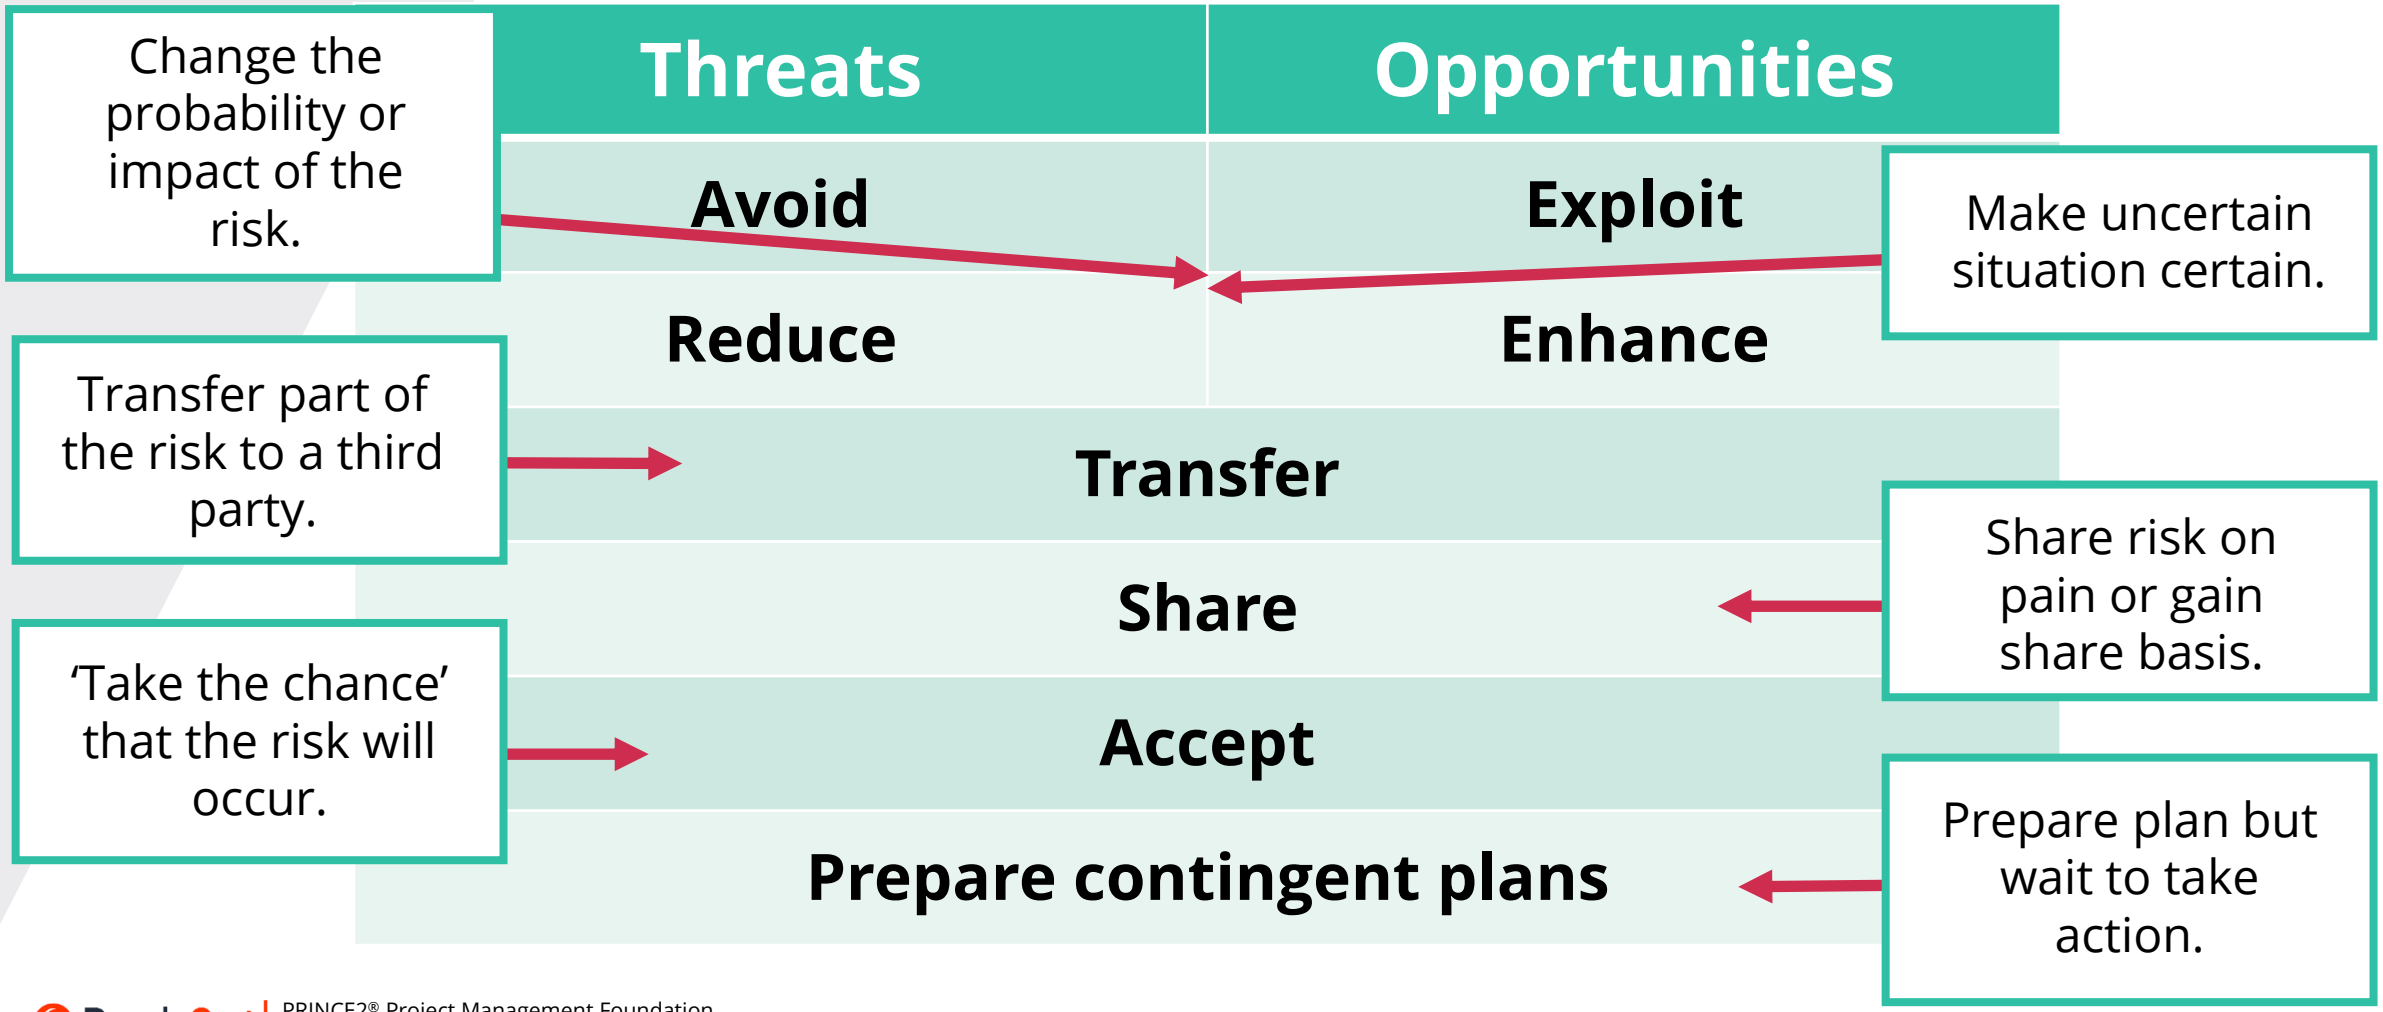

Copyright © 2025 PeopleCert International Limited.

Managing risk in NowByou (1/3)

NowByou has decided to implement some changes to their structure and to also introduce an automated fundraising app. However, none of the charity trustees has any experience of restructuring or fundraising technology. This has been identified a project risk.

Find the four possible responses in the next slide. Select the type that each one most closely represents.



Copyright © 2025 PeopleCert International Limited.

Managing risk in NowByou (2/3)


A. Reduce

B. Transfer

C. Accept

D. Contingent plan

1. Rely on the selected supplier to act in a reliable and conscientious manner to provide the support and advice that will protect the charity's interests.
2. Include a clause in the contract with the selected technology supplier stating that, if the functionality of the solution is not appropriate, the selected supplier will reduce their fees accordingly.
3. Contract a restructuring specialist to take a consulting role to provide advice to the project manager.
4. Request assistance from a consultancy with restructuring expertise, if difficulties arise in understanding what is happening.

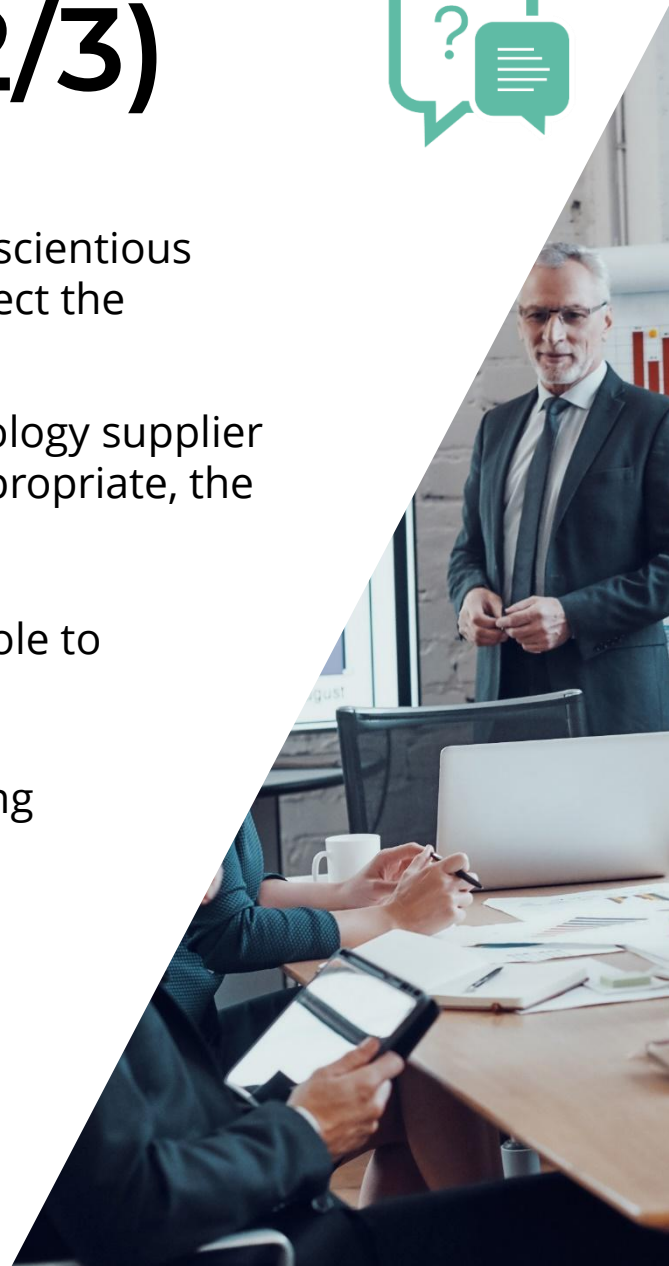

Copyright © 2025 PeopleCert International Limited.

Managing risk in NowByou (3/3)

A. Reduce

3. Contract a restructuring specialist to take a consulting role to provide advice to the project manager.

B. Transfer

2. Include a clause in the contract with the selected technology supplier stating that, if the functionality of the solution is not appropriate, the selected supplier will reduce their fees accordingly.

C. Accept

1. Rely on the selected supplier to act in a reliable and conscientious manner to provide the support and advice that will protect the charity's interests.

D. Contingent plan

4. Request assistance from a consultancy with restructuring expertise, if difficulties arise in understanding what is happening.



Copyright © 2025 PeopleCert International Limited.

Risk culture

- **The risk culture** of the business should be reflected in its risk appetite.
- Decisions and risk management can be affected by **decision bias.**





Copyright © 2025 PeopleCert International Limited.

PRINCE2 Project Management technique for risk management

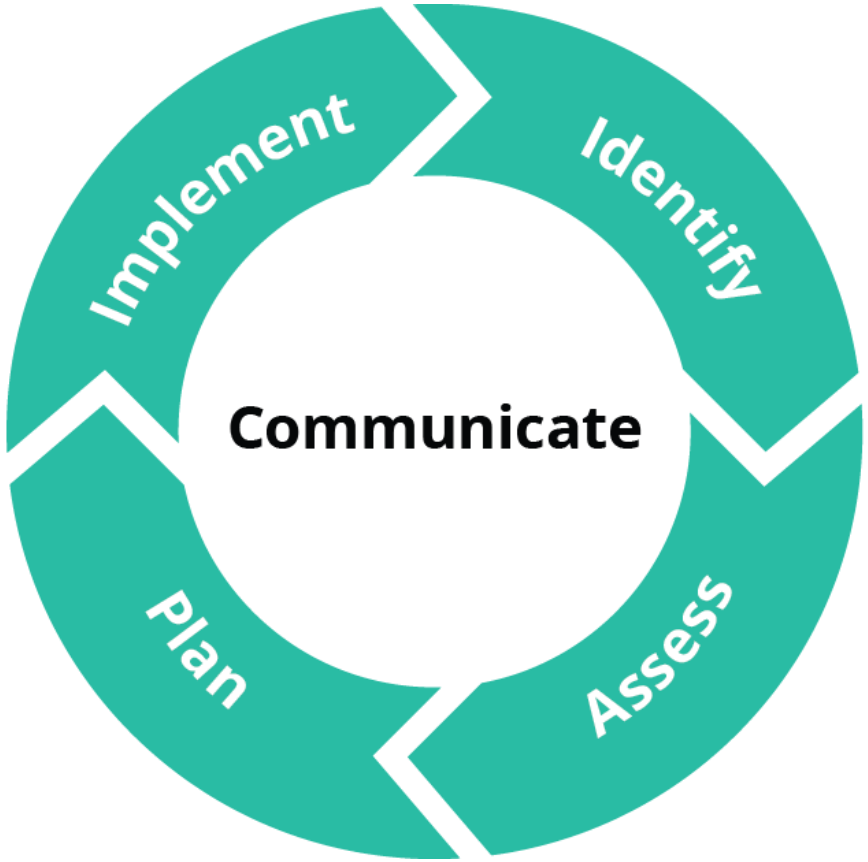


Figure 9.2 PRINCE2 Project Management technique for risk management

Copyright © 2025 PeopleCert International Limited.

Responsibilities (1/2)



1	Maintain the risk register. Ensure that project risks are being identified, assessed, and controlled throughout the project lifecycle.
2	Review risk management practices to ensure that they are performed in line with the project's risk management approach.
3	Ensure that risk management approach is appropriate. Risks associated with the business case are identified, assessed, and controlled. Escalate risks as needed to programme manager or customer.
4	Participate in the identification, assessment, and control of risks.

Copyright © 2025 PeopleCert International Limited.


Responsibilities (2/2)



Project manager	Maintain the risk register. Ensure that project risks are being identified, assessed, and controlled throughout the project lifecycle.
Project assurance	Review risk management practices to ensure that they are performed in line with the project's risk management approach.
Project executive	Ensure that risk management approach is appropriate. Risks associated with the business case are identified, assessed, and controlled. Escalate risks as needed to programme manager or customer.
Team manager	Participate in the identification, assessment, and control of risks.

Copyright © 2025 PeopleCert International Limited.


Responsibilities relevant to the risk practice

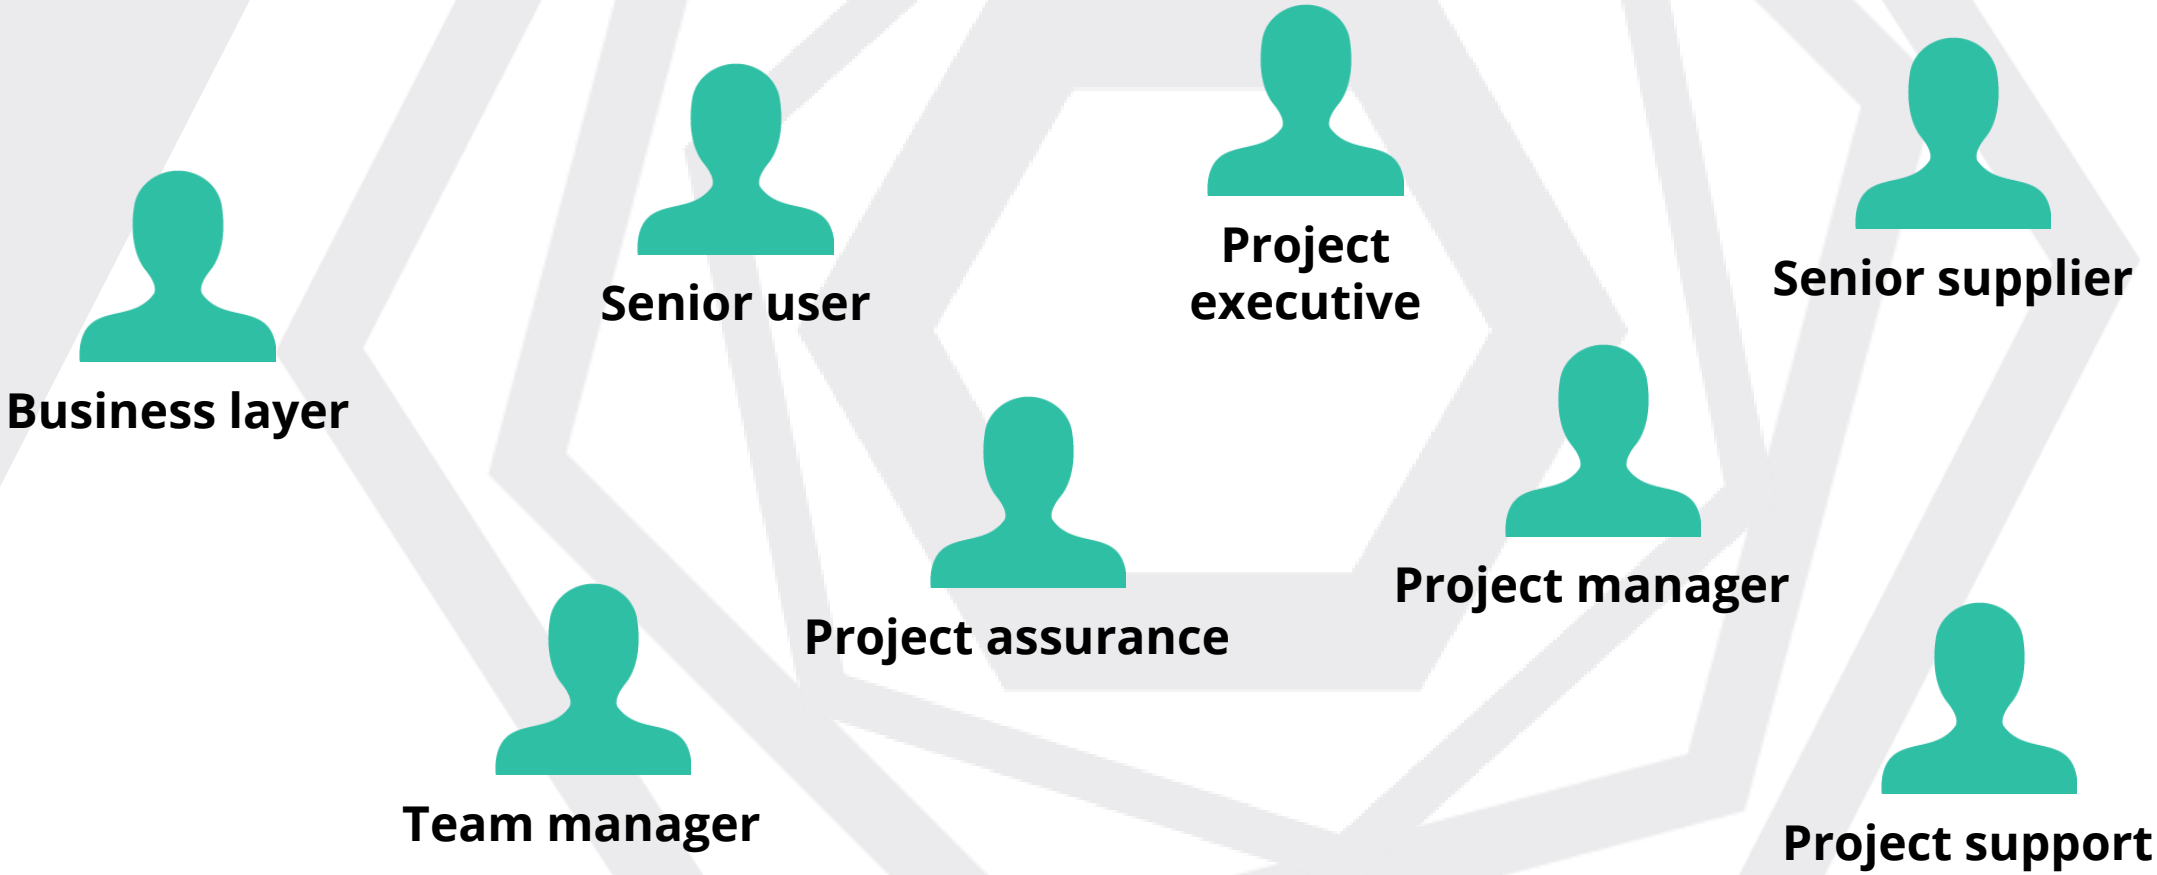

Copyright © 2025 PeopleCert International Limited.

Management products

Risk management approach
How risk will be managed on the project.

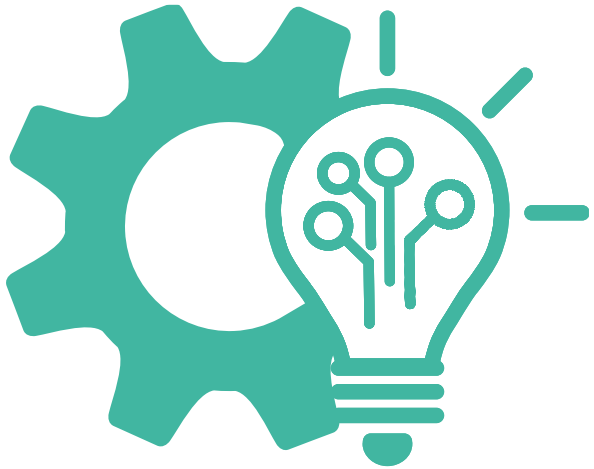


Risk register
Record of identified risks (threats and opportunities) related to the project.

Copyright © 2025 PeopleCert International Limited.

Applying the principles

Assessing whether identified risks have a material impact on the business case

Aligning the risk management approach to the project size and complexity

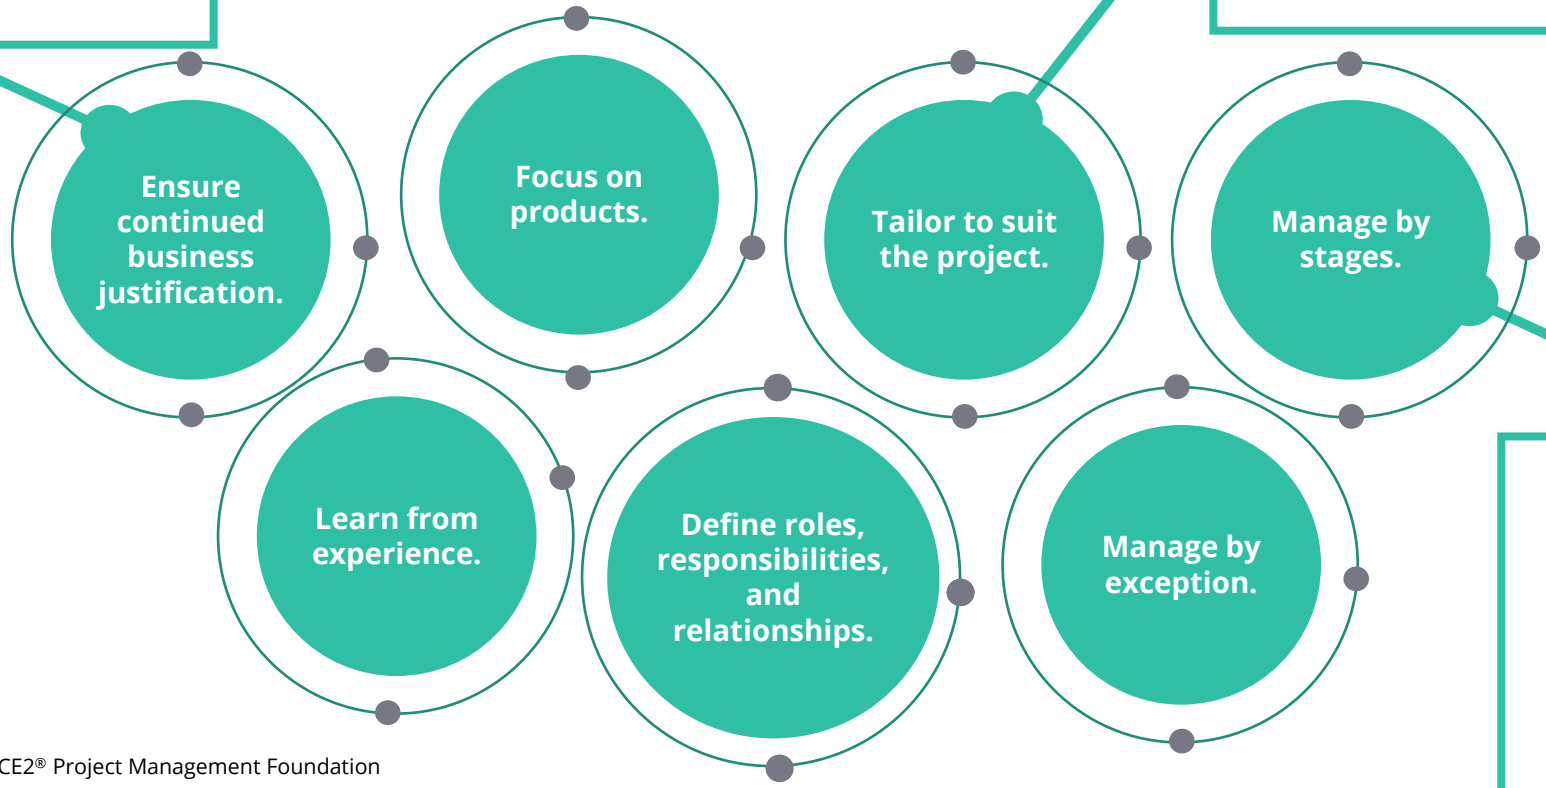

De-risking the project by having ‘stop-go’ decisions at critical points at the end of project stages

Copyright © 2025 PeopleCert International Limited.


Supporting techniques for the risk practice

- Cause and effect diagrams
- Horizon scanning
- Prompt lists
- Pre-mortem
- Swiss cheese
- Data



Copyright © 2025 PeopleCert International Limited

Applying the risk practice

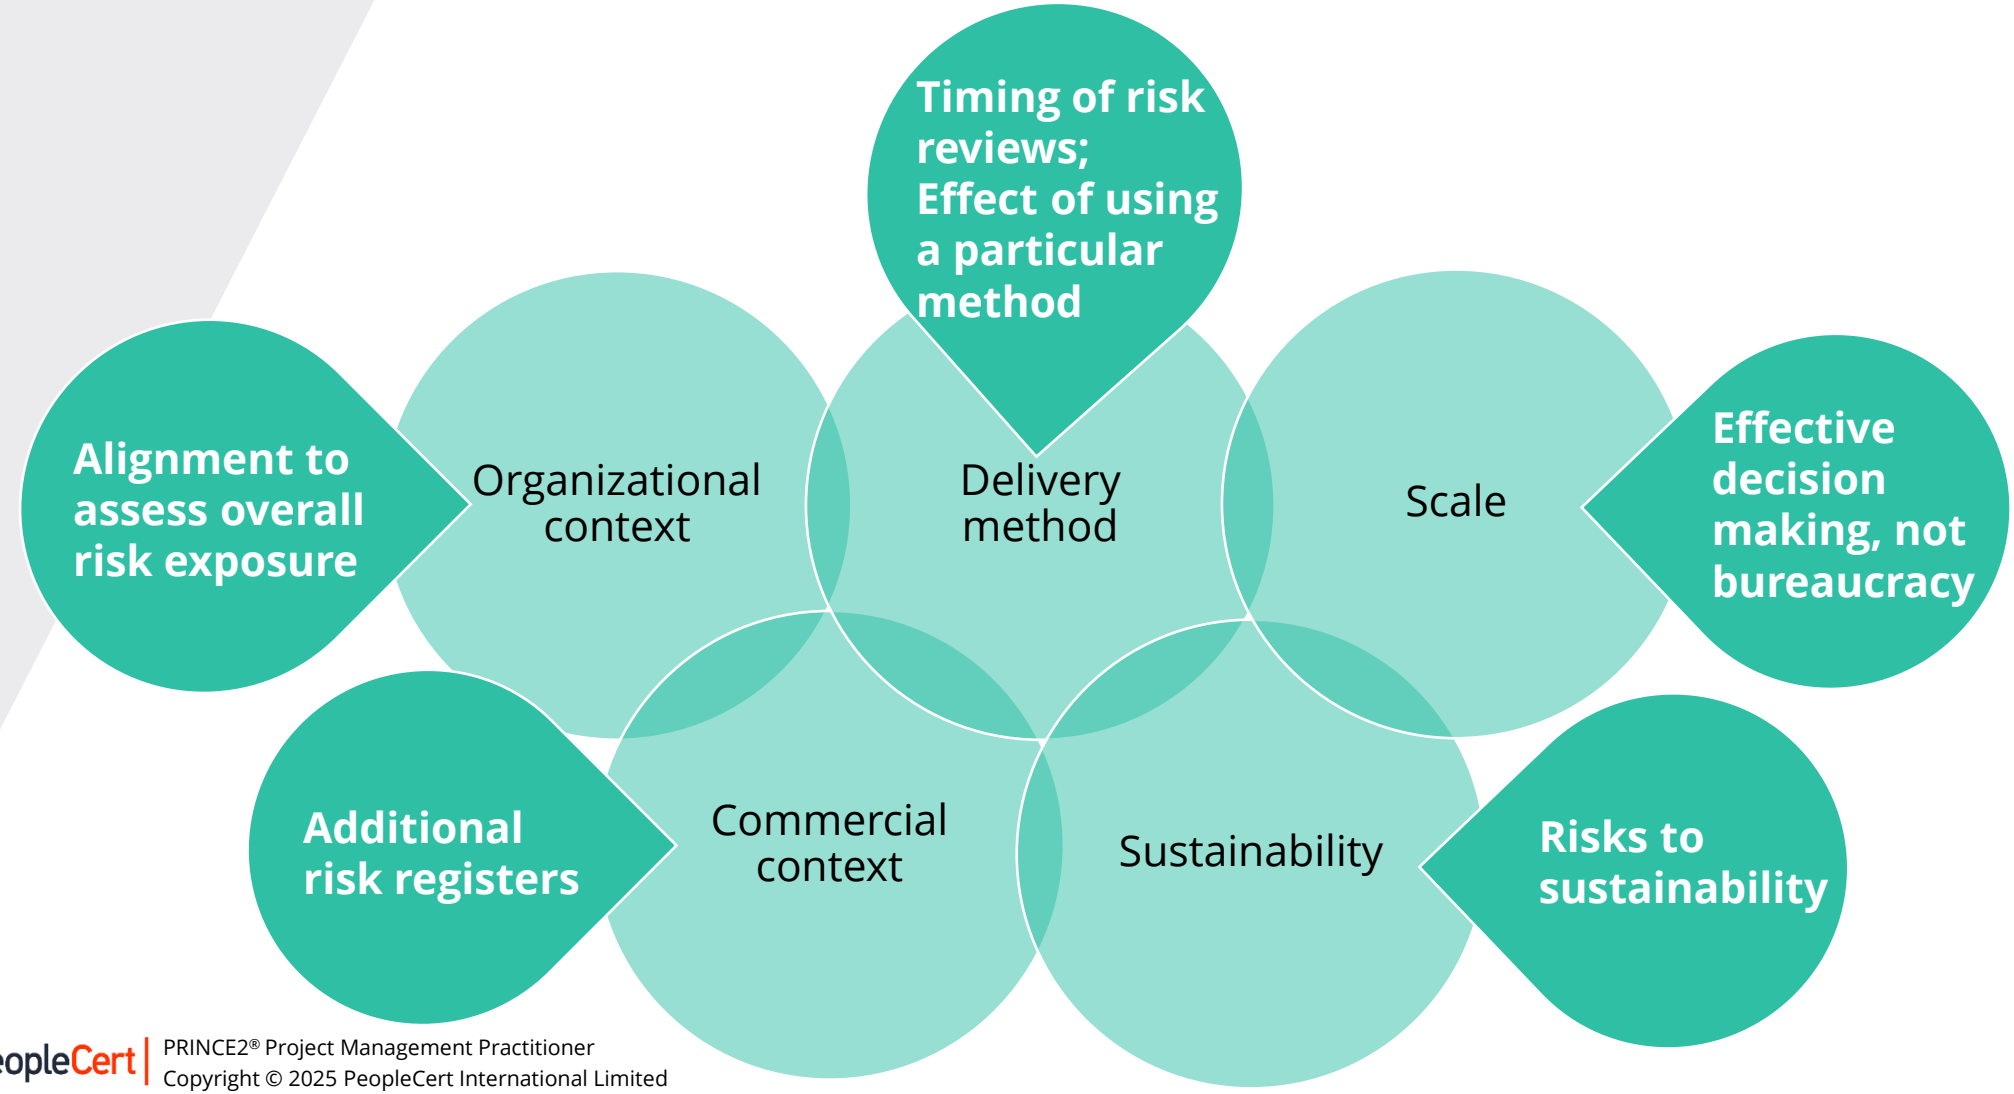

Copyright © 2025 PeopleCert International Limited


30 minutes

Risk

Activity

Identifying and analysing risks

Identify and analyse three possible risks for NowByou.

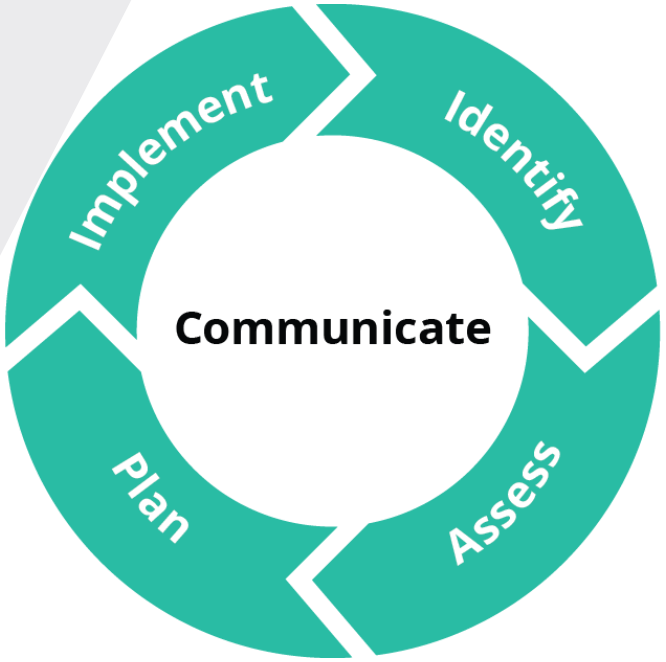



PeopleCert | PRINCE2® Project Management Foundation
Copyright © 2025 PeopleCert International Limited.

Risk analysis

Risk cause → **Risk event** → **Risk effect**

Probability (High/Medium/Low)

Impact (High/Medium/Low)



Copyright © 2025 PeopleCert International Limited.

Module 9

Controlling a stage and managing product delivery

Points of view

Controlling a stage

Views the project from the **project manager's** perspective.


Managing product delivery

Views the project from the **team manager's** perspective.



Copyright © 2025 PeopleCert International Limited.

The PRINCE2 Project Management processes

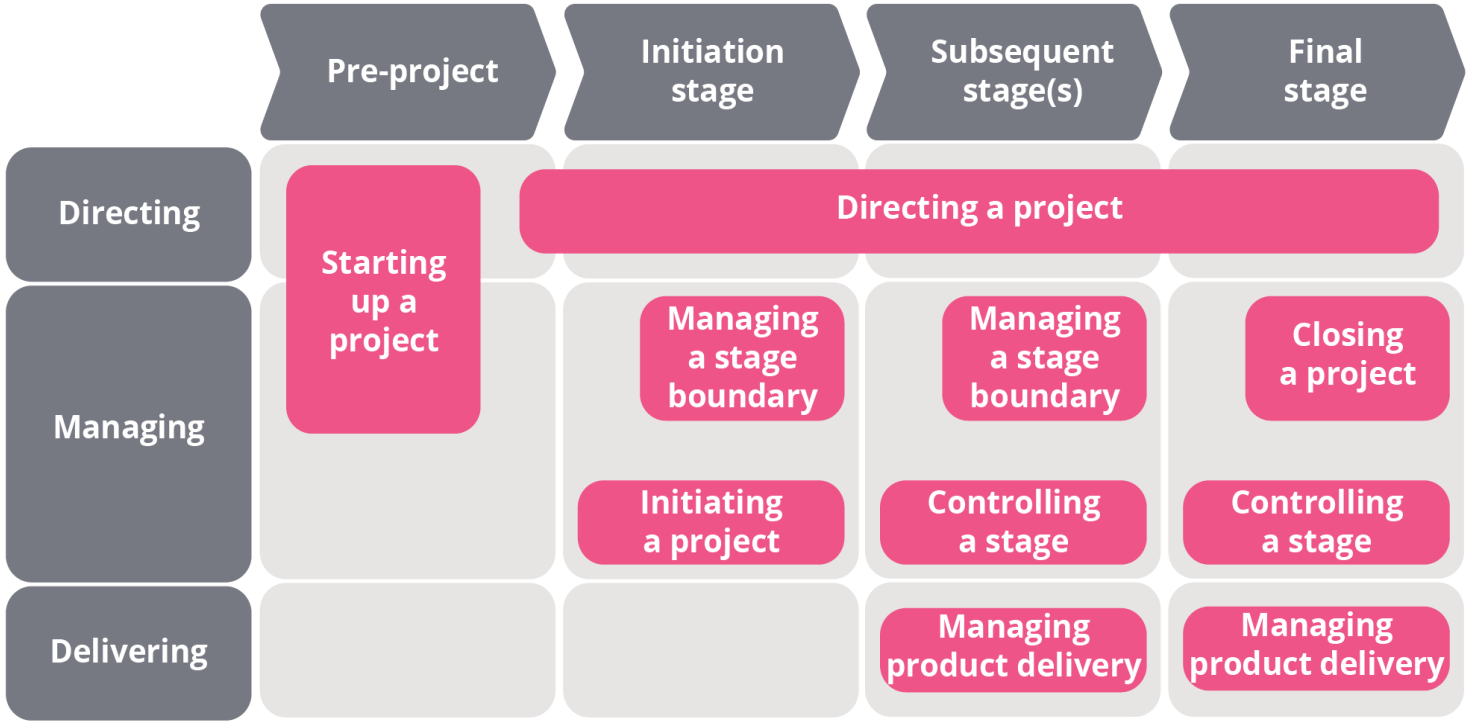

Note

- Starting up a project is used by both the directing and managing levels.
- There should be at least two stages, the first of which is the initiation stage.
- Managing a stage boundary is first used at the end of the initiation stage and repeated at the end of each subsequent stage except the final stage. It is also used to prepare exception plans, which can be done at any time including in the final stage.

Figure 12.1 The PRINCE2 Project Management processes

Copyright © 2025 PeopleCert International Limited.

Purpose of controlling a stage process

The purpose of the controlling a stage process is to:

- **assign** work to be done
- **monitor** such work
- **deal with issues**
- report **progress** to the project board
- take **corrective actions** to ensure that the management stage remains **within tolerance.**



Copyright © 2025 PeopleCert International Limited.

Objectives of controlling a stage process

The objectives of the controlling a stage process are to ensure the following:

- Attention is focused on delivery of the stage's products.
- The project management team is focused on delivery within the established tolerances.
- The business case is kept under review.
- Risks and issues are kept under control.
- The agreed products for the stage meet the agreed quality expectations and are accepted.



Copyright © 2025 PeopleCert International Limited.

Overview of ‘controlling a stage’


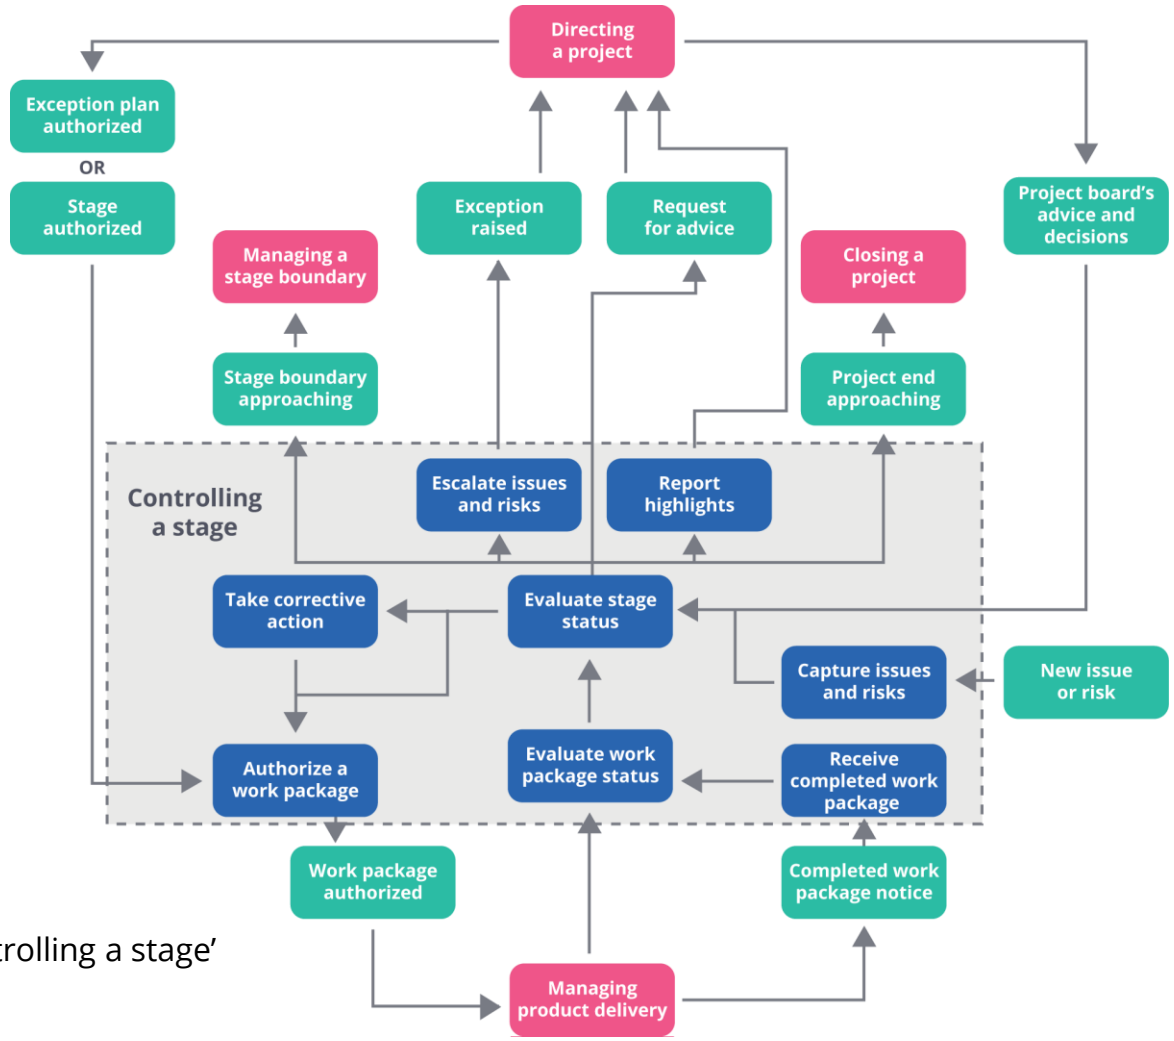


Figure 16.1 Overview of ‘controlling a stage’

Copyright © 2025 PeopleCert International Limited.

‘Controlling a stage’ activities

The activities of the **project manager** in ‘controlling a stage’ involve:

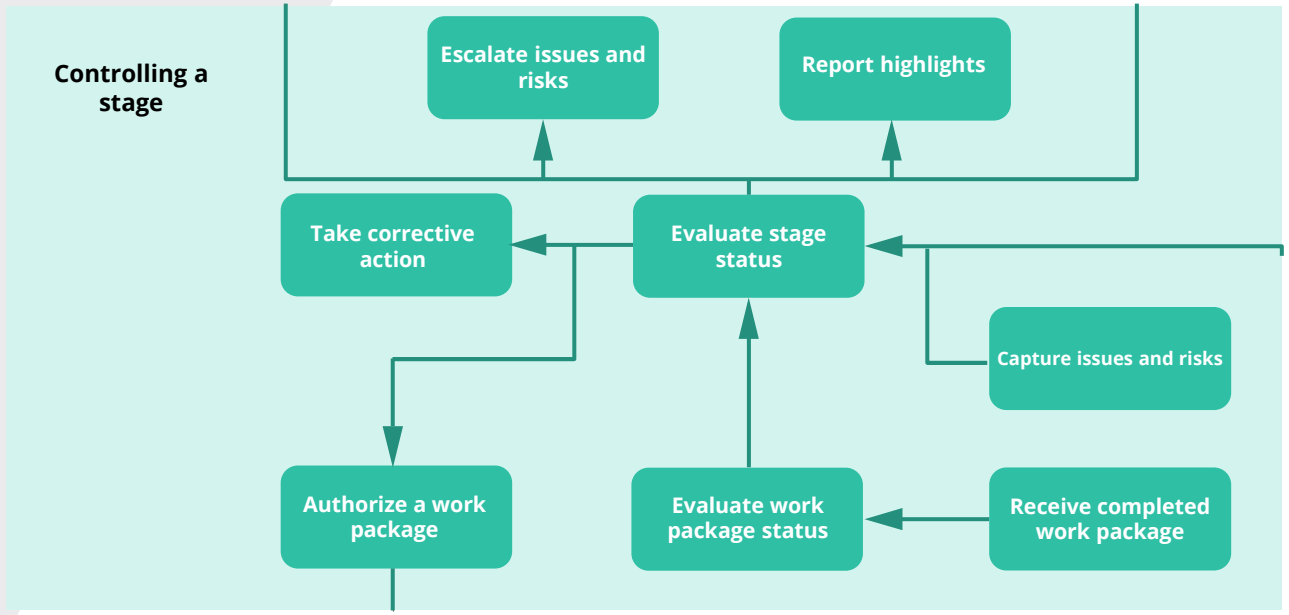

Adapted from Figure 16.1 Overview of ‘controlling a stage’

Work packages

Issues and risks

Monitoring and reporting



Copyright © 2025 PeopleCert International Limited.

‘Controlling a stage’ roles and responsibilities

Table 16.2 RACI chart for ‘controlling a stage’


Activity	Business layer	Project executive	Senior user	Senior supplier	Project manager	Team manager	Project assurance	Project support
Authorize a work package		A			R	C	C	C
Evaluate work package status		A			R	C	C	C
Receive completed work package					A	R	C	I
Evaluate stage status		A	C	C	R	C	C	C
Capture issues and risks		A			R^1	R^2	C	C
Take corrective action		A	C	C	A^1/R^3	R^4		I
Escalate issues and risks		A	C	C	R	I		I
Report highlights		A	C	C	R	C	C	C

R = Responsible, A = Accountable, C = Consulted, I = Informed
R^1: Responsible for capturing issues and risks at stage level
R^2: Responsible for capturing issues and risks at team level
A^1: Accountable for corrective actions taken by team manager
R^3: Responsible for own corrective actions
R^4: Responsible for corrective actions at team level

Copyright © 2025 PeopleCert International Limited

Managing product delivery


This process considers the project from the **team manager's** perspective.
The team manager(s) or team members execute assigned work packages.

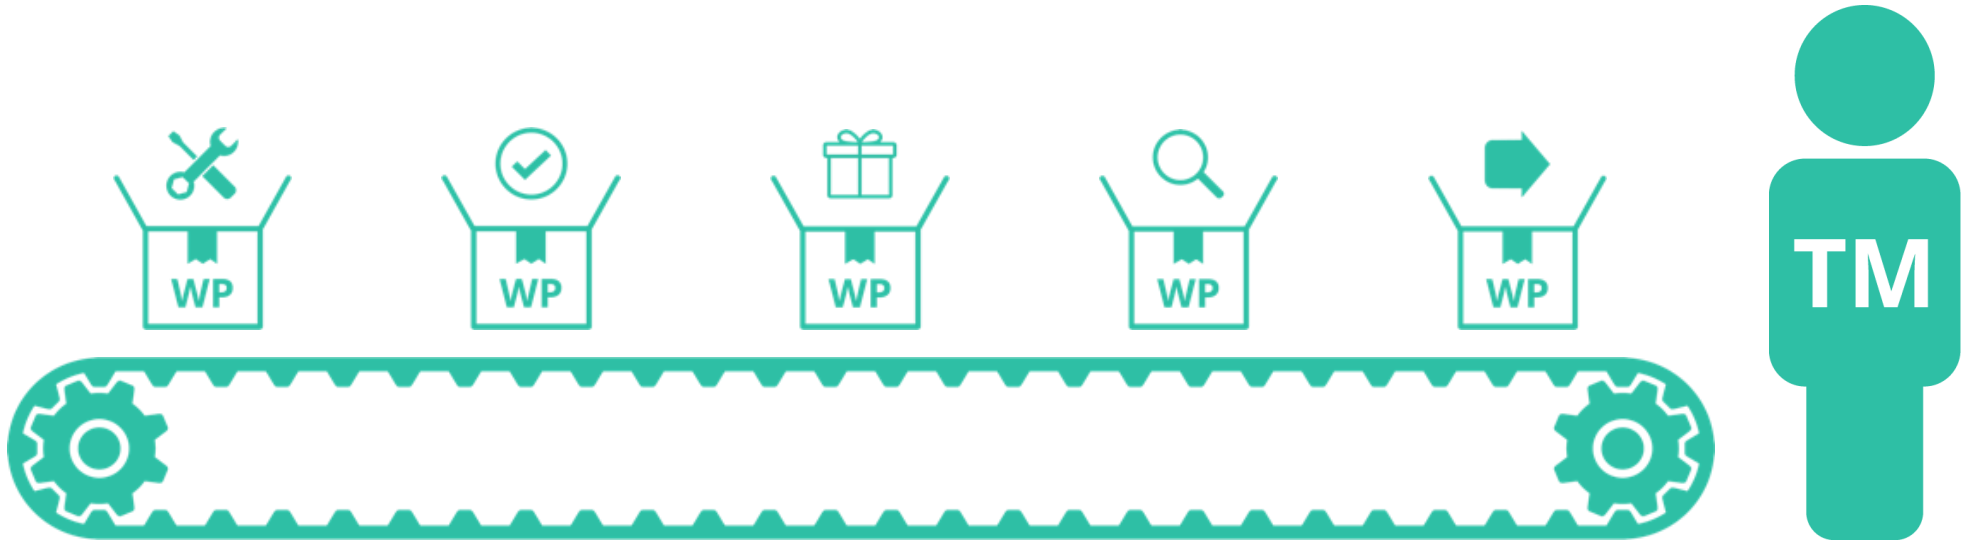

Copyright © 2025 PeopleCert International Limited.

Purpose of ‘managing product delivery’

Control the link between the project manager and the team manager by agreeing the requirements for **acceptance, execution, reporting** and **delivery** of products.

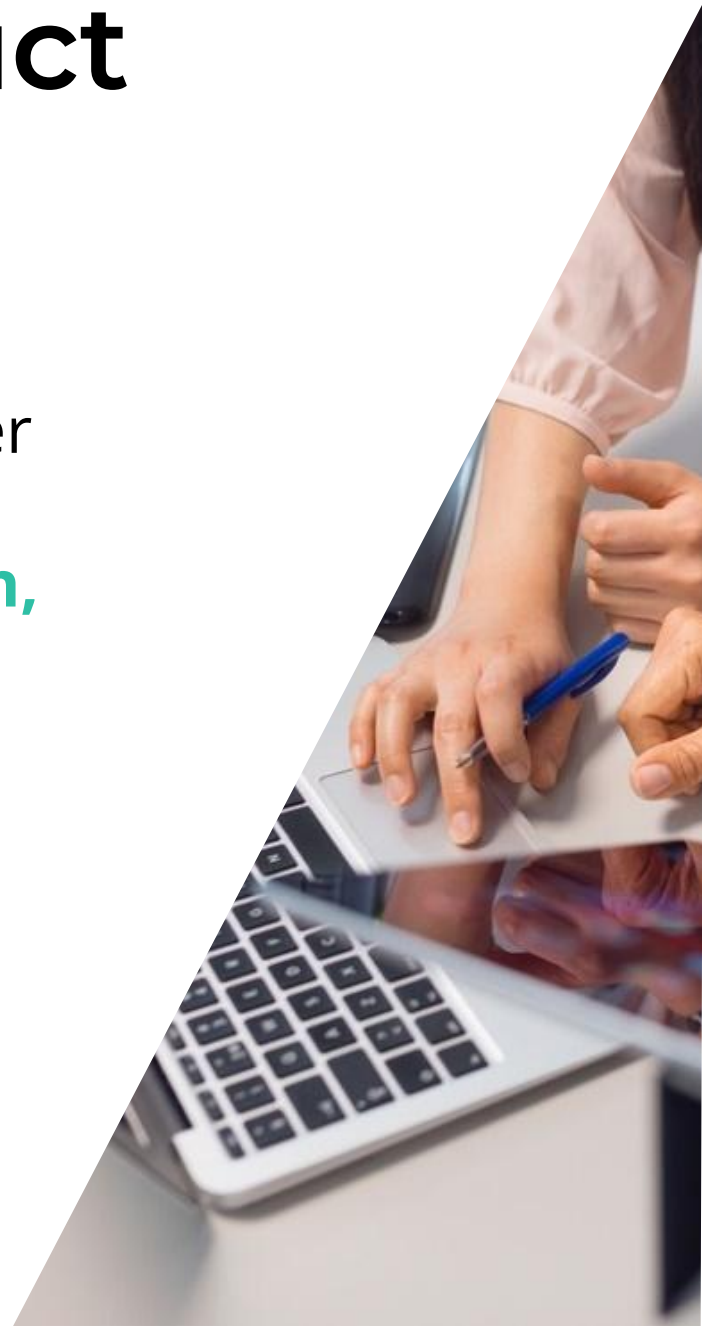

Copyright © 2025 PeopleCert International Limited.

Objectives of ‘managing product delivery’

Ensure that work on products allocated to the team is authorized and agreed.

Ensure that team managers and their teams are clear as to what is to be produced and what is the expected effort, cost, or timescales.

Ensure that the planned products are delivered to quality expectations and within tolerance.

Ensure that accurate progress information is provided to the project manager at an agreed frequency to manage expectations.



Copyright © 2025 PeopleCert International Limited.

Overview of ‘managing product delivery’

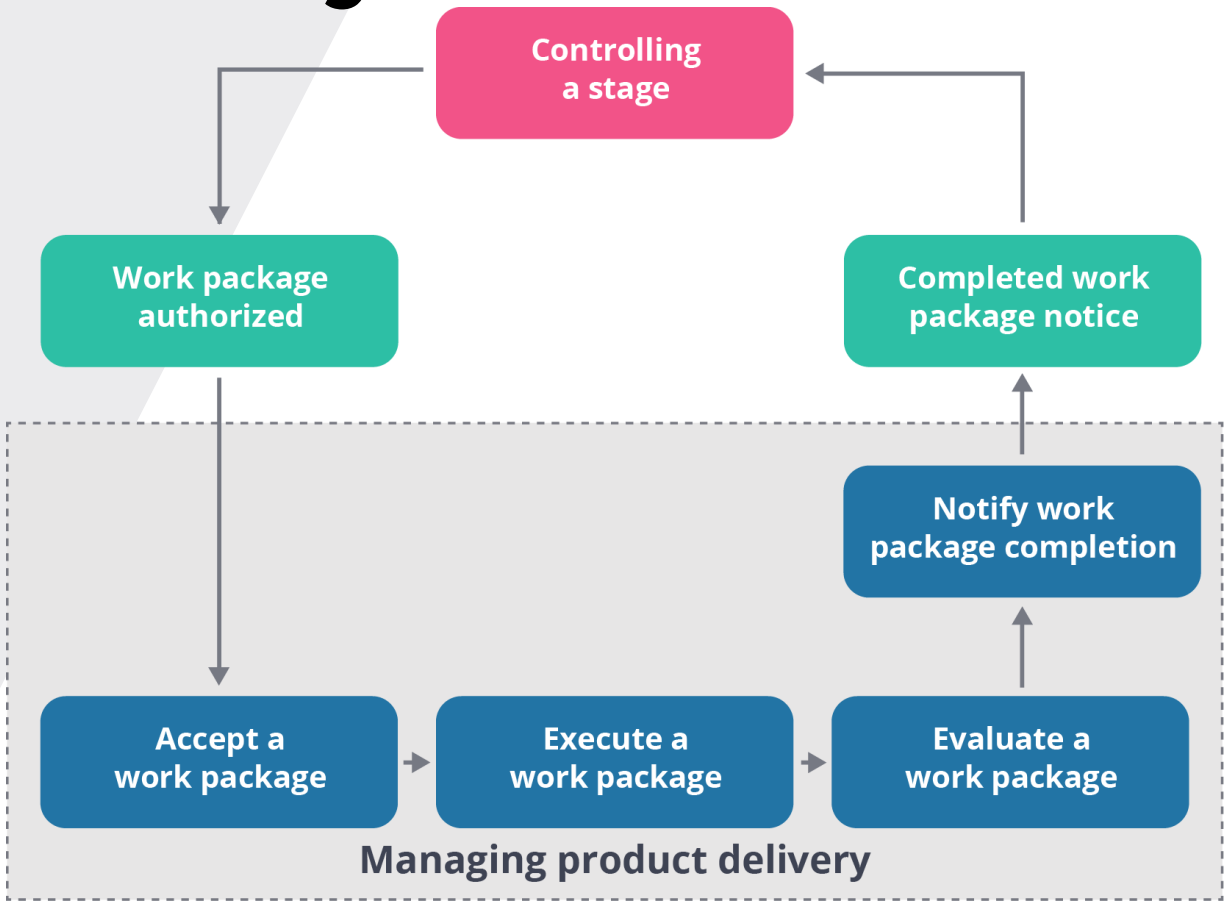


Figure 17.1 Overview of ‘managing product delivery’



Accept a work package.



Execute a work package.



Evaluate a work package.



Notify work package completion.

Copyright © 2025 PeopleCert International Limited.

Roles

The project manager



- authorizes a work package
- checks on work package progress
- receives a completed work package.


The team manager



- accepts a work package
- executes a work package
- delivers a work package.

Copyright © 2025 PeopleCert International Limited.

Work package description

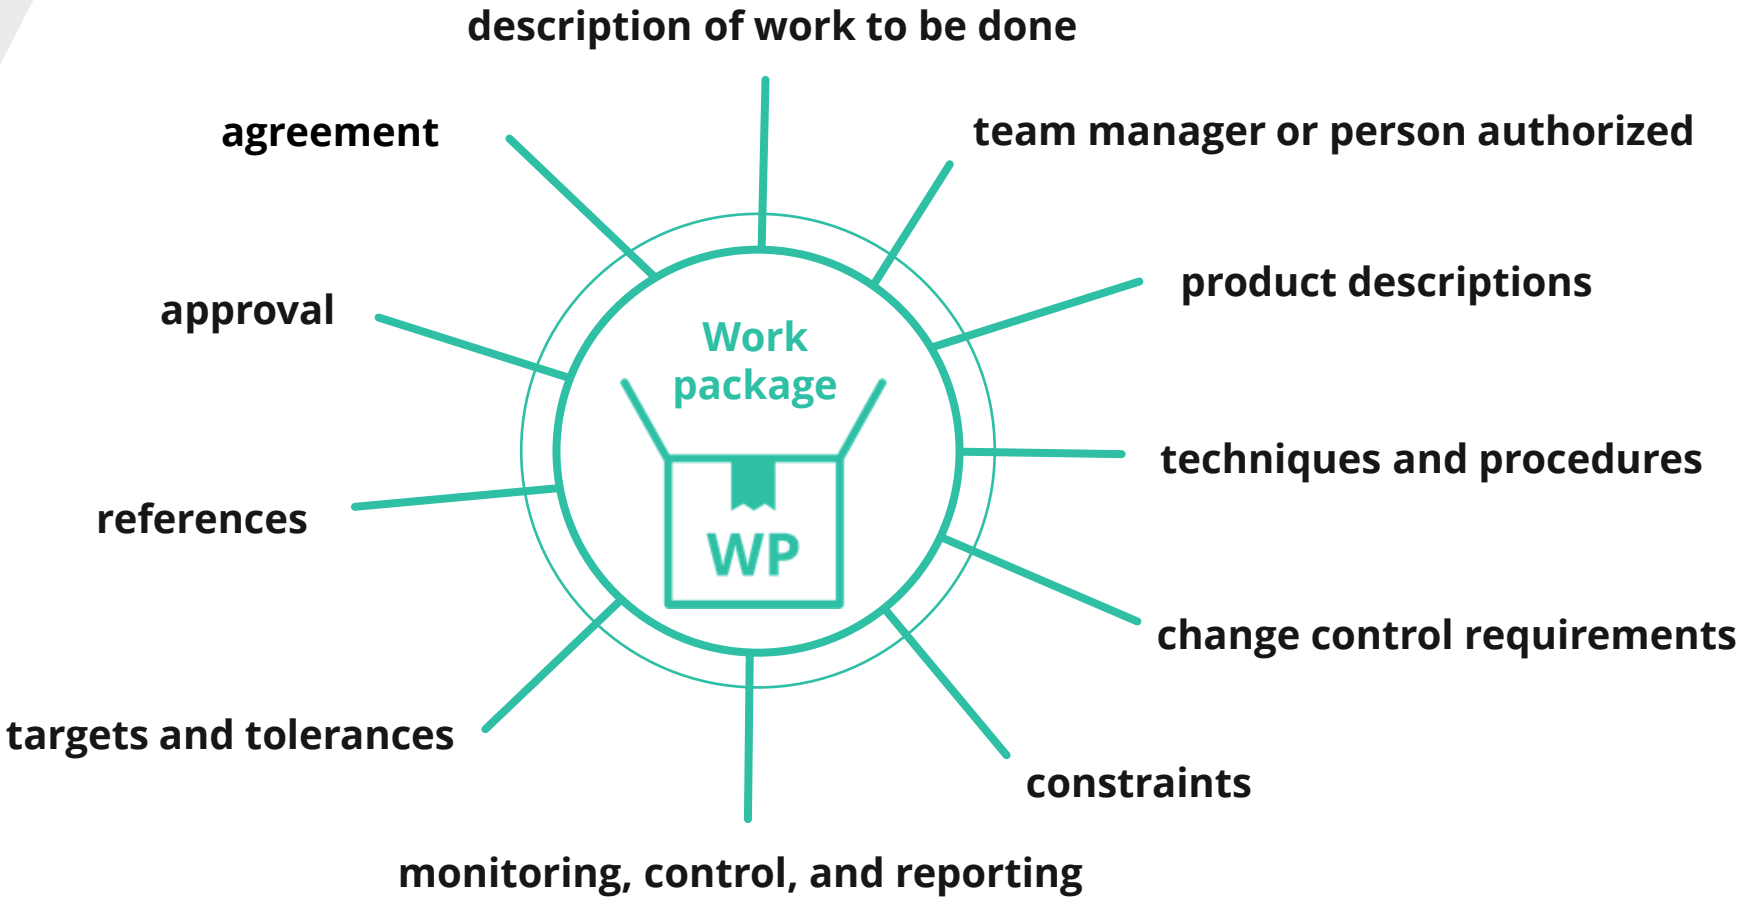

Copyright © 2025 PeopleCert International Limited.

‘Managing product delivery’ roles and responsibilities

Table 17.2 RACI chart for ‘managing product delivery’

Activity	Business layer	Project executive	Senior user	Senior supplier	Project manager	Team manager	Project assurance	Project support
Accept a work package					A	R		I
Execute a work package					A	R	C	C
Evaluate a work package					A	R	C	C
Notify work package completion					A	R	C	I

R = Responsible, A = Accountable, C = Consulted, I = Informed

Copyright © 2025 PeopleCert International Limited

Module 10

Managing a stage boundary

Purpose of ‘managing a stage boundary’

Enable the project manager to **provide** the project board with sufficient **information** in order to:

- **review** the **success** of the current management stage
- **approve** the next stage plan
- **review** the updated **project plan**
- confirm **continued business justification** and **acceptability** of the **risks.**



Copyright © 2025 PeopleCert International Limited.

Objectives of ‘managing a stage boundary’

- Assure project board.
- Prepare stage or exception plan.
- Review and update the PID.
- Provide information to assess viability.
- Record information to help later stages or projects.
- Request authorization to start the next stage.



Copyright © 2025 PeopleCert International Limited.

Context

All projects must ensure that the products created will deliver the benefits sought.

- **Business justification should be reconfirmed at the end of each stage.**
- **The project can be redirected or stopped, if necessary.**
- **Provides a means for implementing an exception procedure.**



Copyright © 2025 PeopleCert International Limited.

Overview of ‘managing a stage boundary’

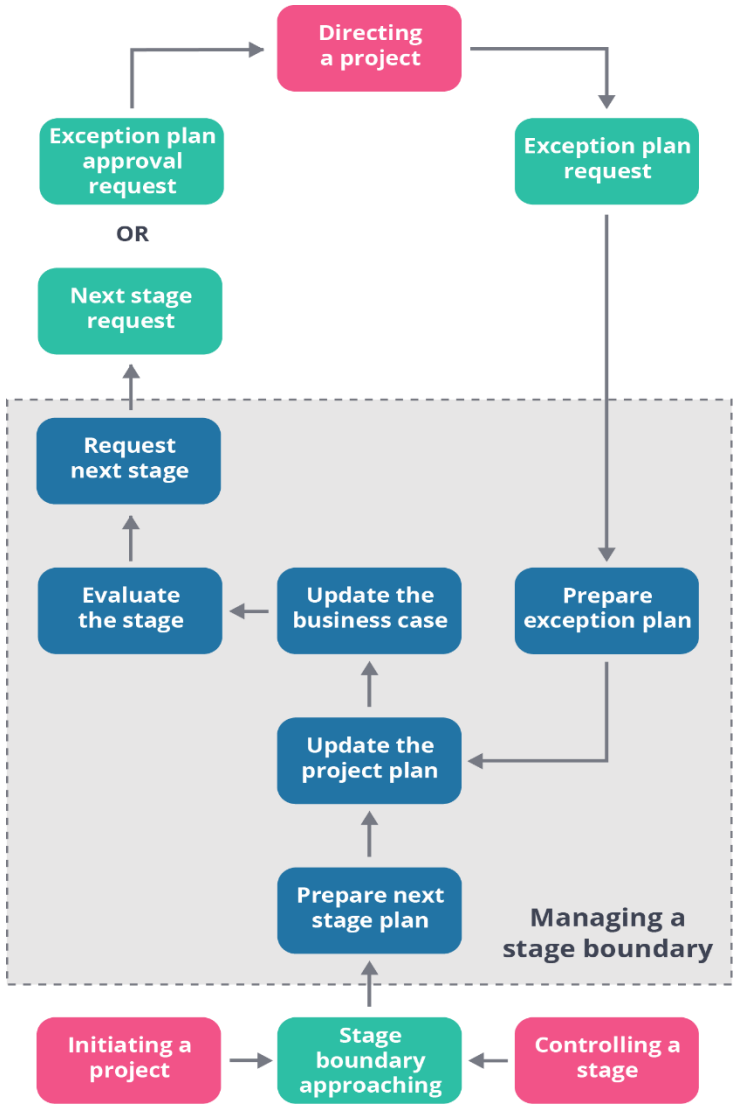


Figure 18.1 Overview of ‘managing a stage boundary’



Copyright © 2025 PeopleCert International Limited.

‘Managing a stage boundary’ roles and responsibilities

Table 18.2 RACI chart for ‘managing a stage boundary’

Activity	Business layer	Project executive	Senior user	Senior supplier	Project manager	Team manager	Project assurance	Project support
Prepare the next stage plan		A	C	C	R	C	C	C
Prepare the exception plan (if required)		A	C	C	R	C	C	C
Update the project plan		A	C	C	R	C	C	C
Update the business case		A	C	C	R	C	C	C
Evaluate the stage		A	C	C	R	C	C	C
Request the next stage		A	C	C	R	I	C	I

R = Responsible, A = Accountable, C = Consulted, I = Informed

Copyright © 2025 PeopleCert International Limited

25 minutes



Managing a stage boundary

Activity

Create a checklist (1/2)

Objective: understand the management products that are relevant to this process.

Task: which management reports and plans should (or may) be updated or created during the managing a stage boundary process?



Copyright © 2025 PeopleCert International Limited.

Create a checklist (2/2)

- Exception plan
- Project plan
- Business case
- Quality register
- PID
- Stage plan
- Risk register
- Issue register



Copyright © 2025 PeopleCert International Limited.

Module 11

Issues

Purpose of the issues practice

To **collect** and **assess issues** and **control changes** to the project's baseline.



Copyright © 2025 PeopleCert International Limited.

Definition and types of issues

An **issue** is an event relevant to the project that requires project management consideration.

Event external to project

Request for change

Business opportunity

Problem or concern

Off-specification



Copyright © 2025 PeopleCert International Limited.

Change

A change is defined as a modification to any of the approved products that constitute the project baseline.

The project baseline is the current approved versions of the management products and specialist products that are subject to change control.



Copyright © 2025 PeopleCert International Limited.

Issue resolution

They are often presented informally.

Categorize by issue type.

Apply judgement.

Identify issues early.


Monitor the external environment.



Copyright © 2025 PeopleCert International Limited.

Change control

The process by which changes that may affect the project baseline are identified, assessed, and then approved, rejected, or deferred.

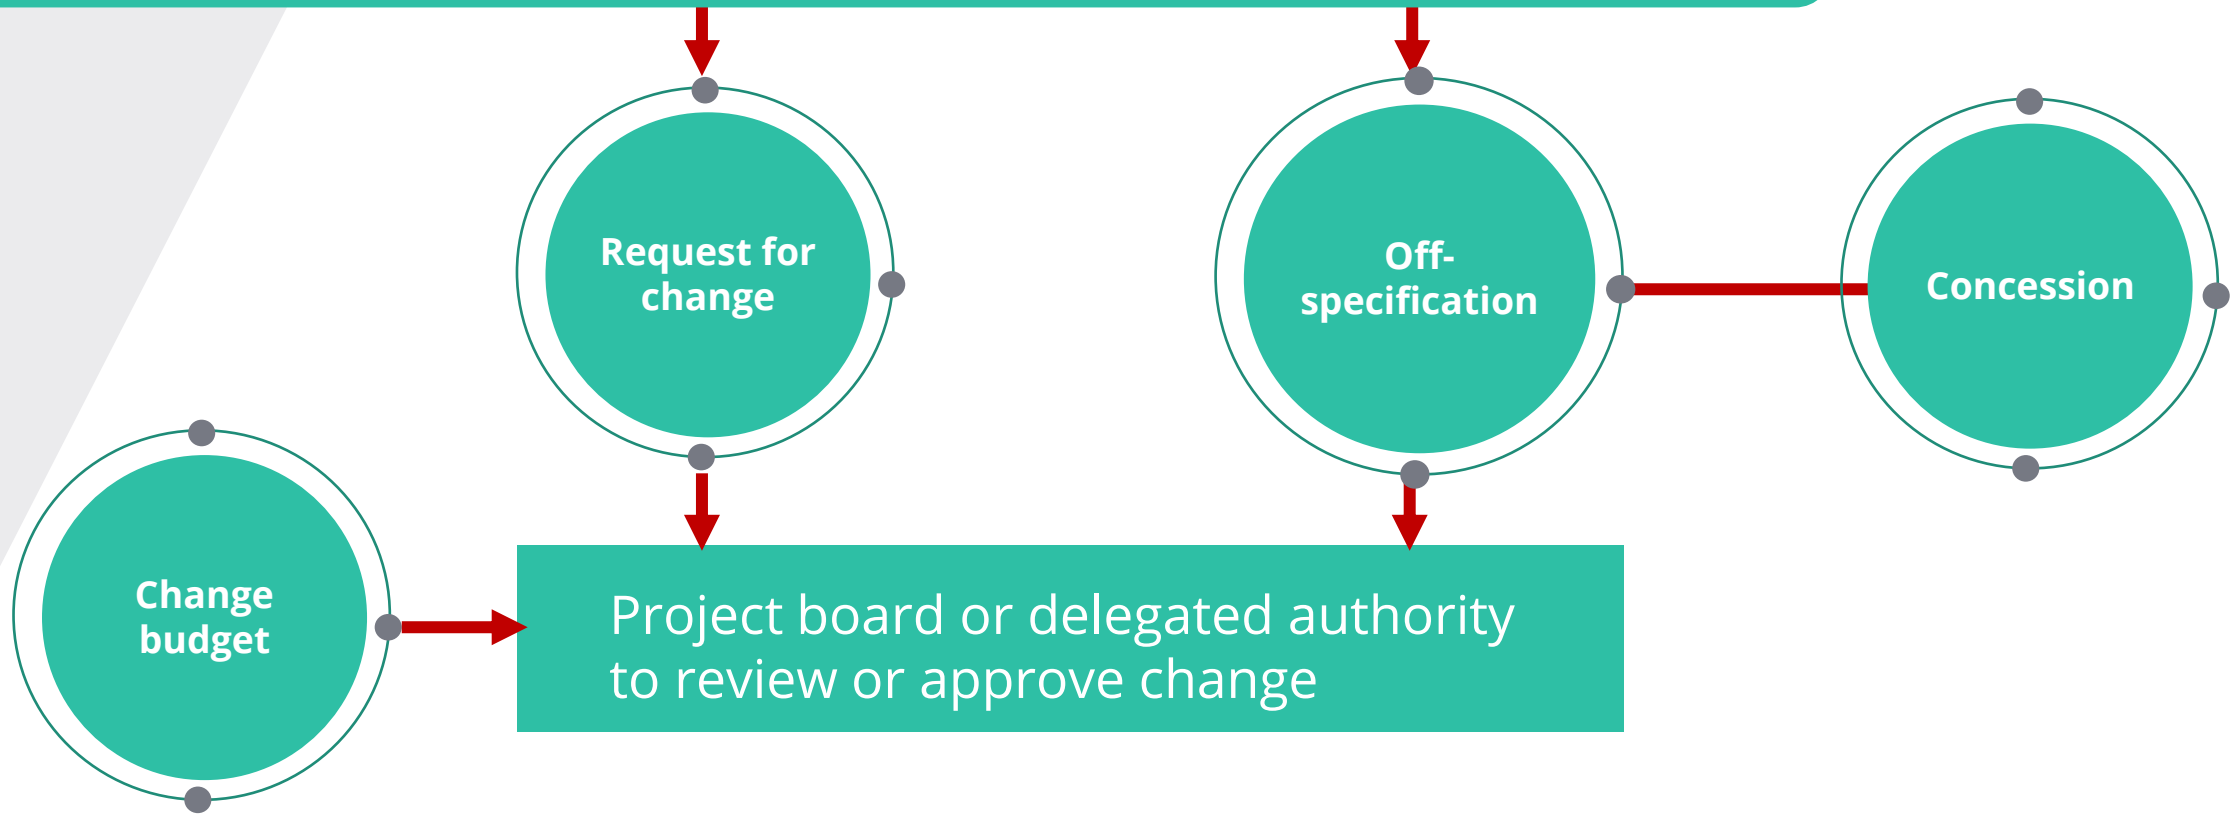

Copyright © 2025 PeopleCert International Limited.

PRINCE2 Project Management technique for issue management


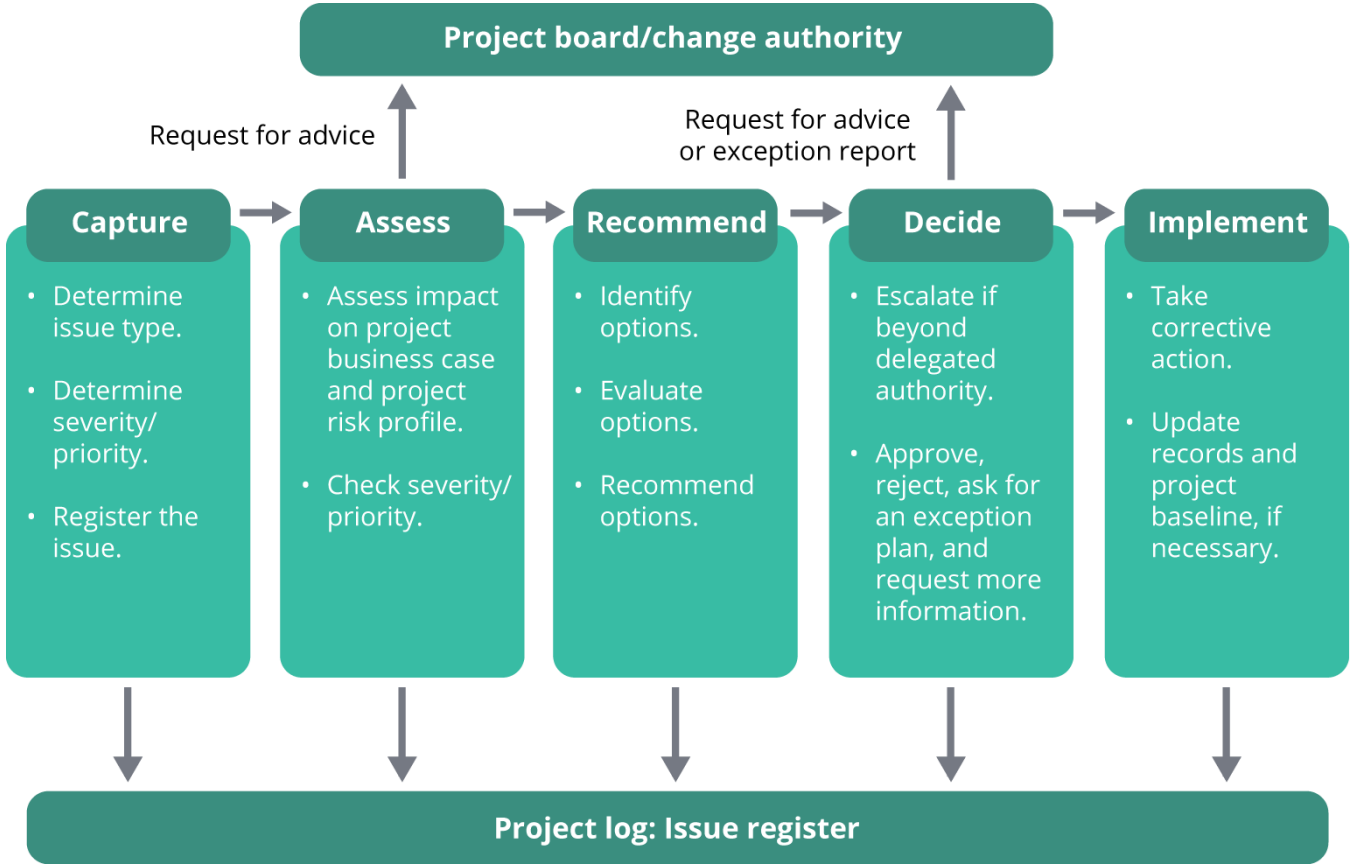


Figure 10.1 PRINCE2 Project Management technique for issue management

Copyright © 2025 PeopleCert International Limited.

Key management products



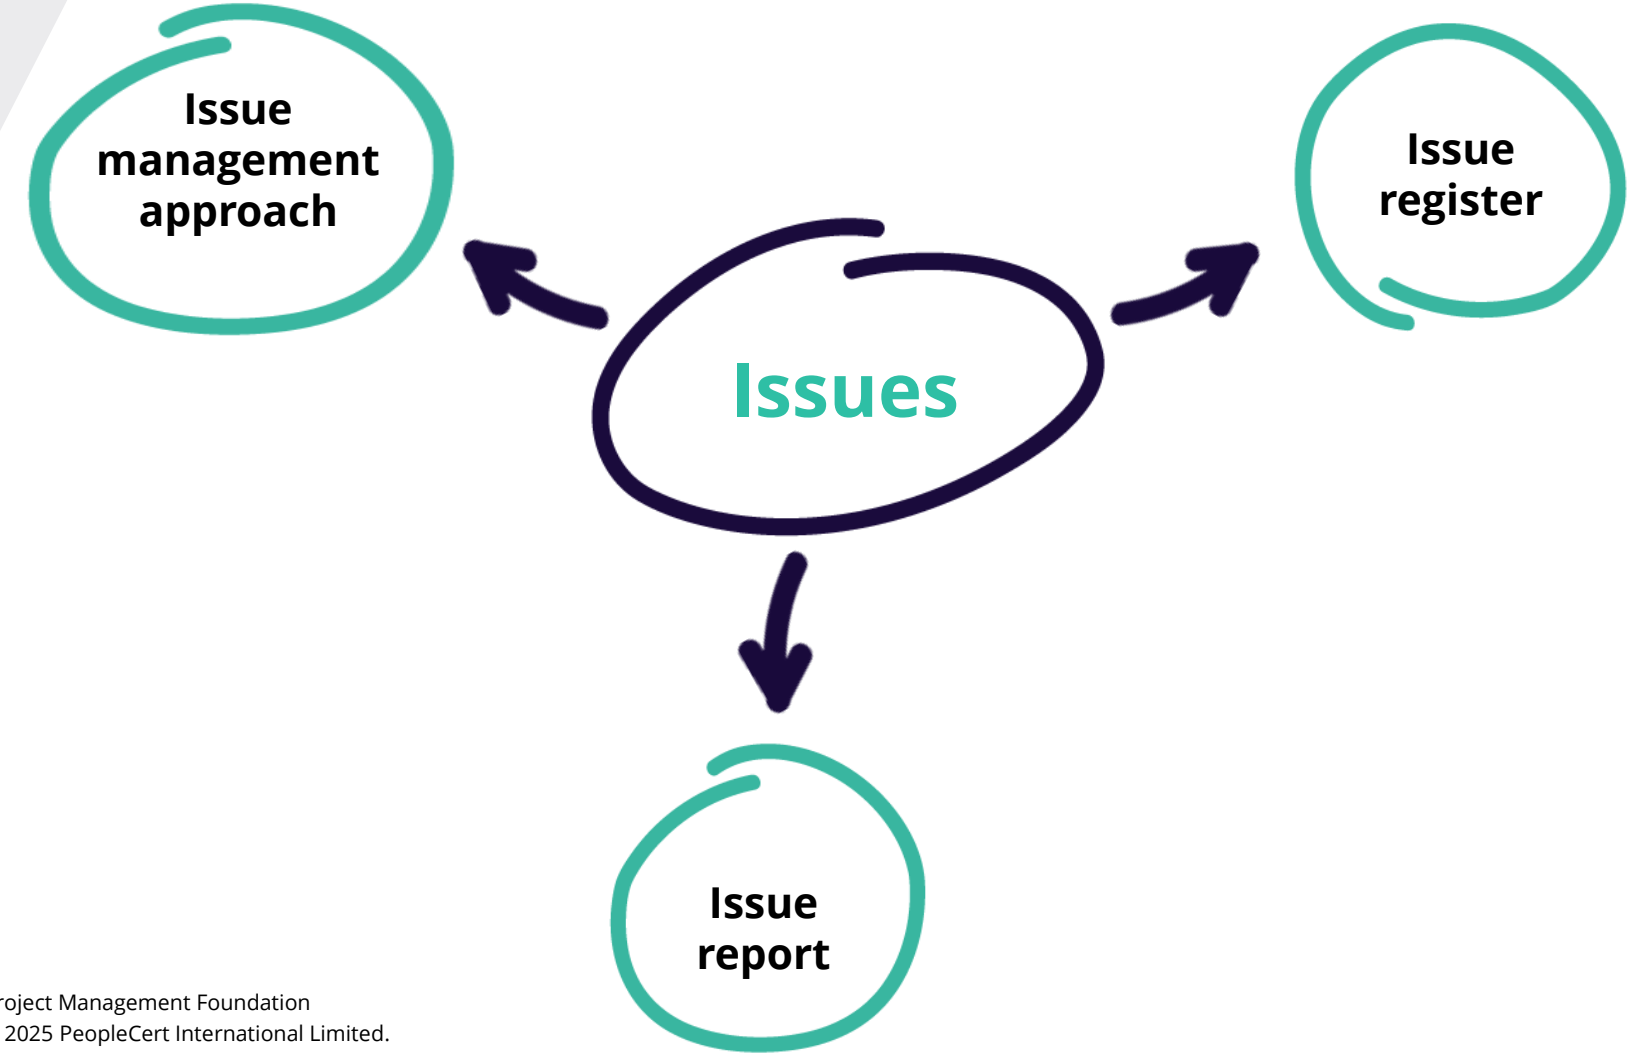

Copyright © 2025 PeopleCert International Limited.


Supporting techniques for the issues practice

- Root cause
- Pareto
- Cause and effect
- Failure mode
- 5 whys



Copyright © 2025 PeopleCert International Limited

Applying the issues practice

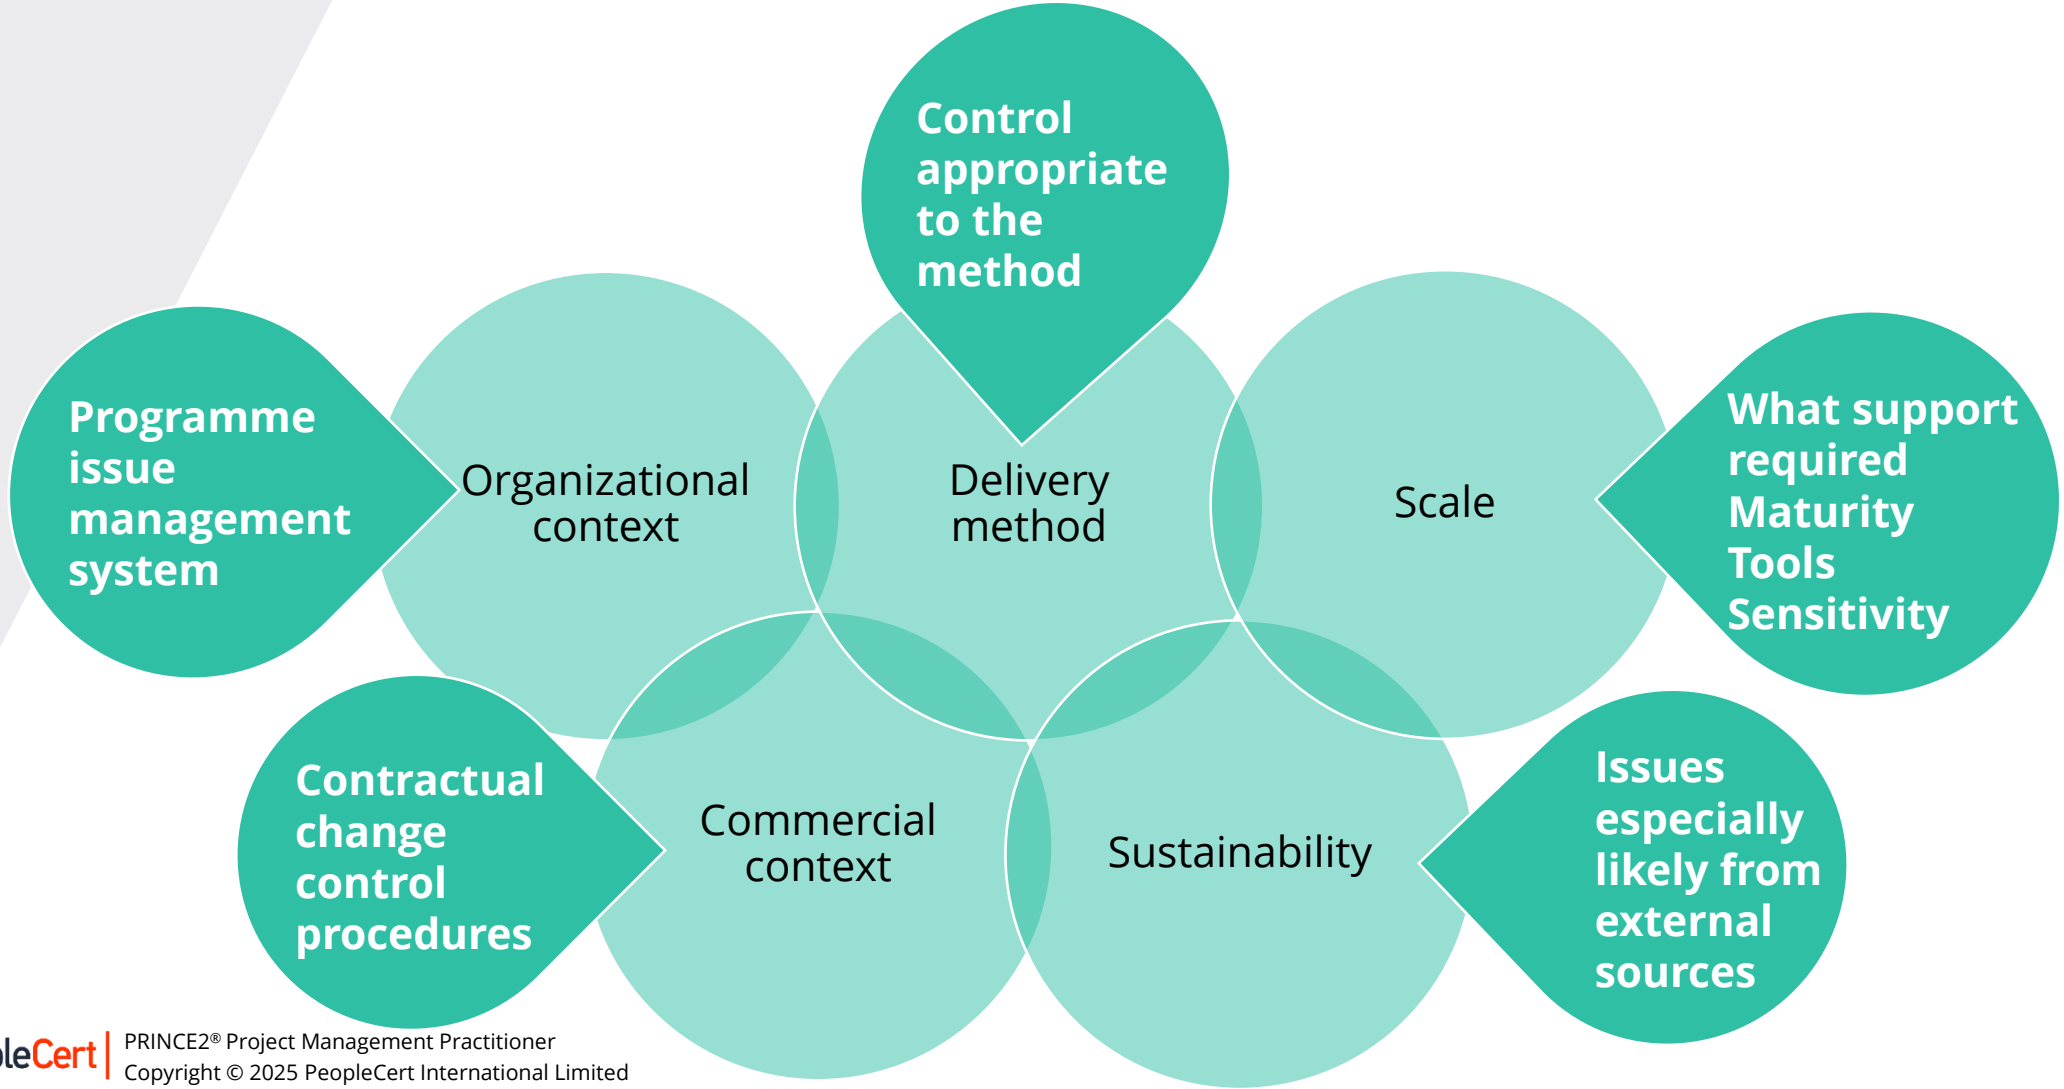

Copyright © 2025 PeopleCert International Limited

Module 12

Progress

The purpose of the progress practice


The purpose of the progress practice is to:

- establish mechanisms to monitor and compare actual achievements against those planned
- control any unacceptable deviations
- provide a forecast for the project's objectives and continued viability



Copyright © 2025 PeopleCert International Limited.

Definitions



Progress
The measure of the achievement of the objectives of a plan.

Forecast
A prediction made by studying historical data and past patterns.

Exception
A situation where it can be forecast that there will be a deviation beyond the tolerance levels agreed between the project manager and the project board (or between the project board and business layer).



Copyright © 2025 PeopleCert International Limited.

Effective progress management

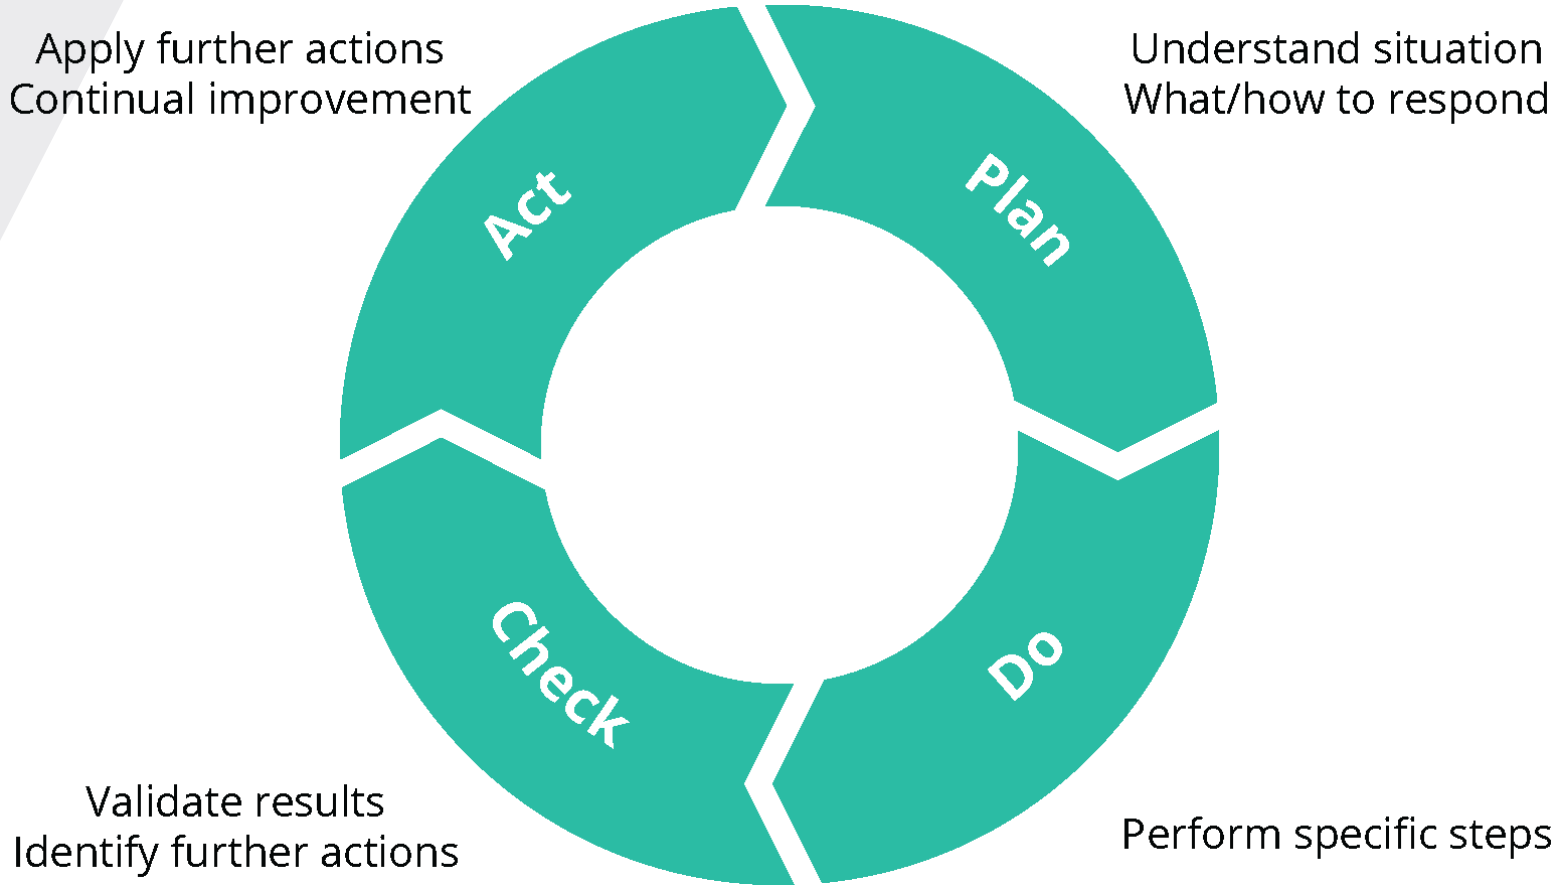


Figure 11.1 Plan-do-check-act cycle



Copyright © 2025 PeopleCert International Limited.

The seven types of tolerances



Benefits



Time



Cost



Risk



Sustainability



Scope



Quality



Copyright © 2025 PeopleCert International Limited.

Delegating tolerances and reporting progress


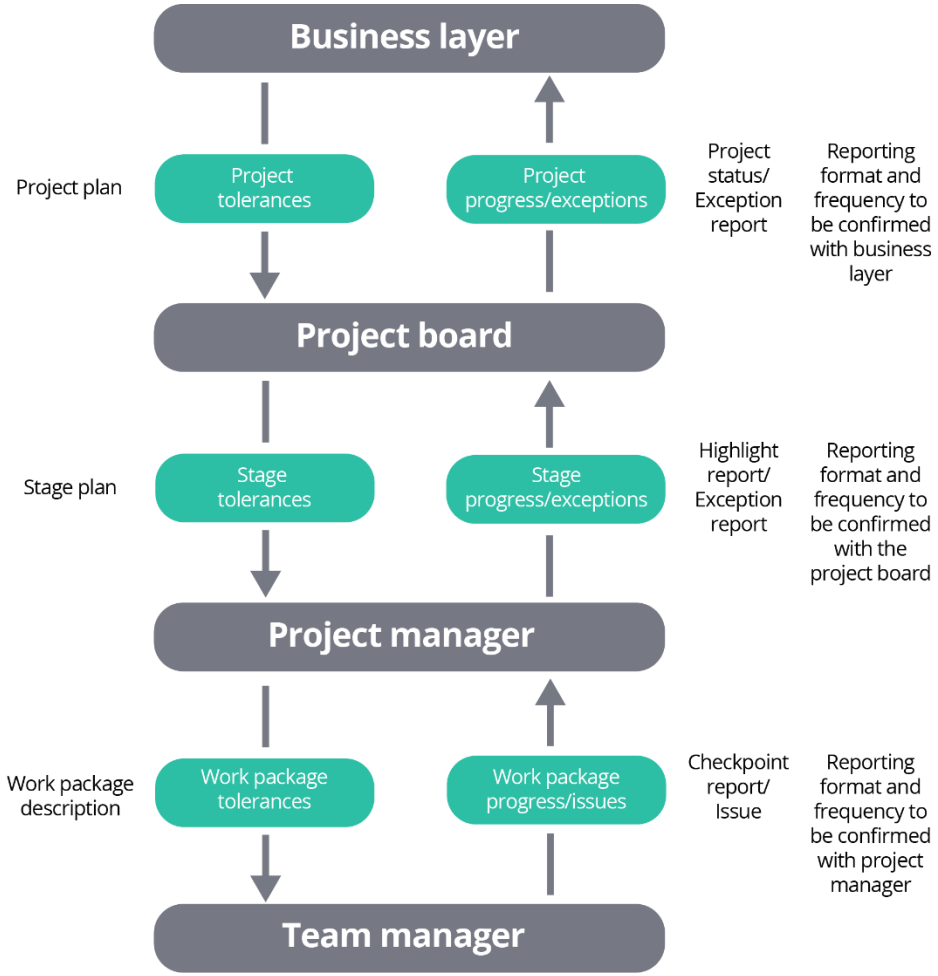


Figure 11.2 Delegating tolerance and reporting actual and forecast progress

Copyright © 2025 PeopleCert International Limited.

Escalating

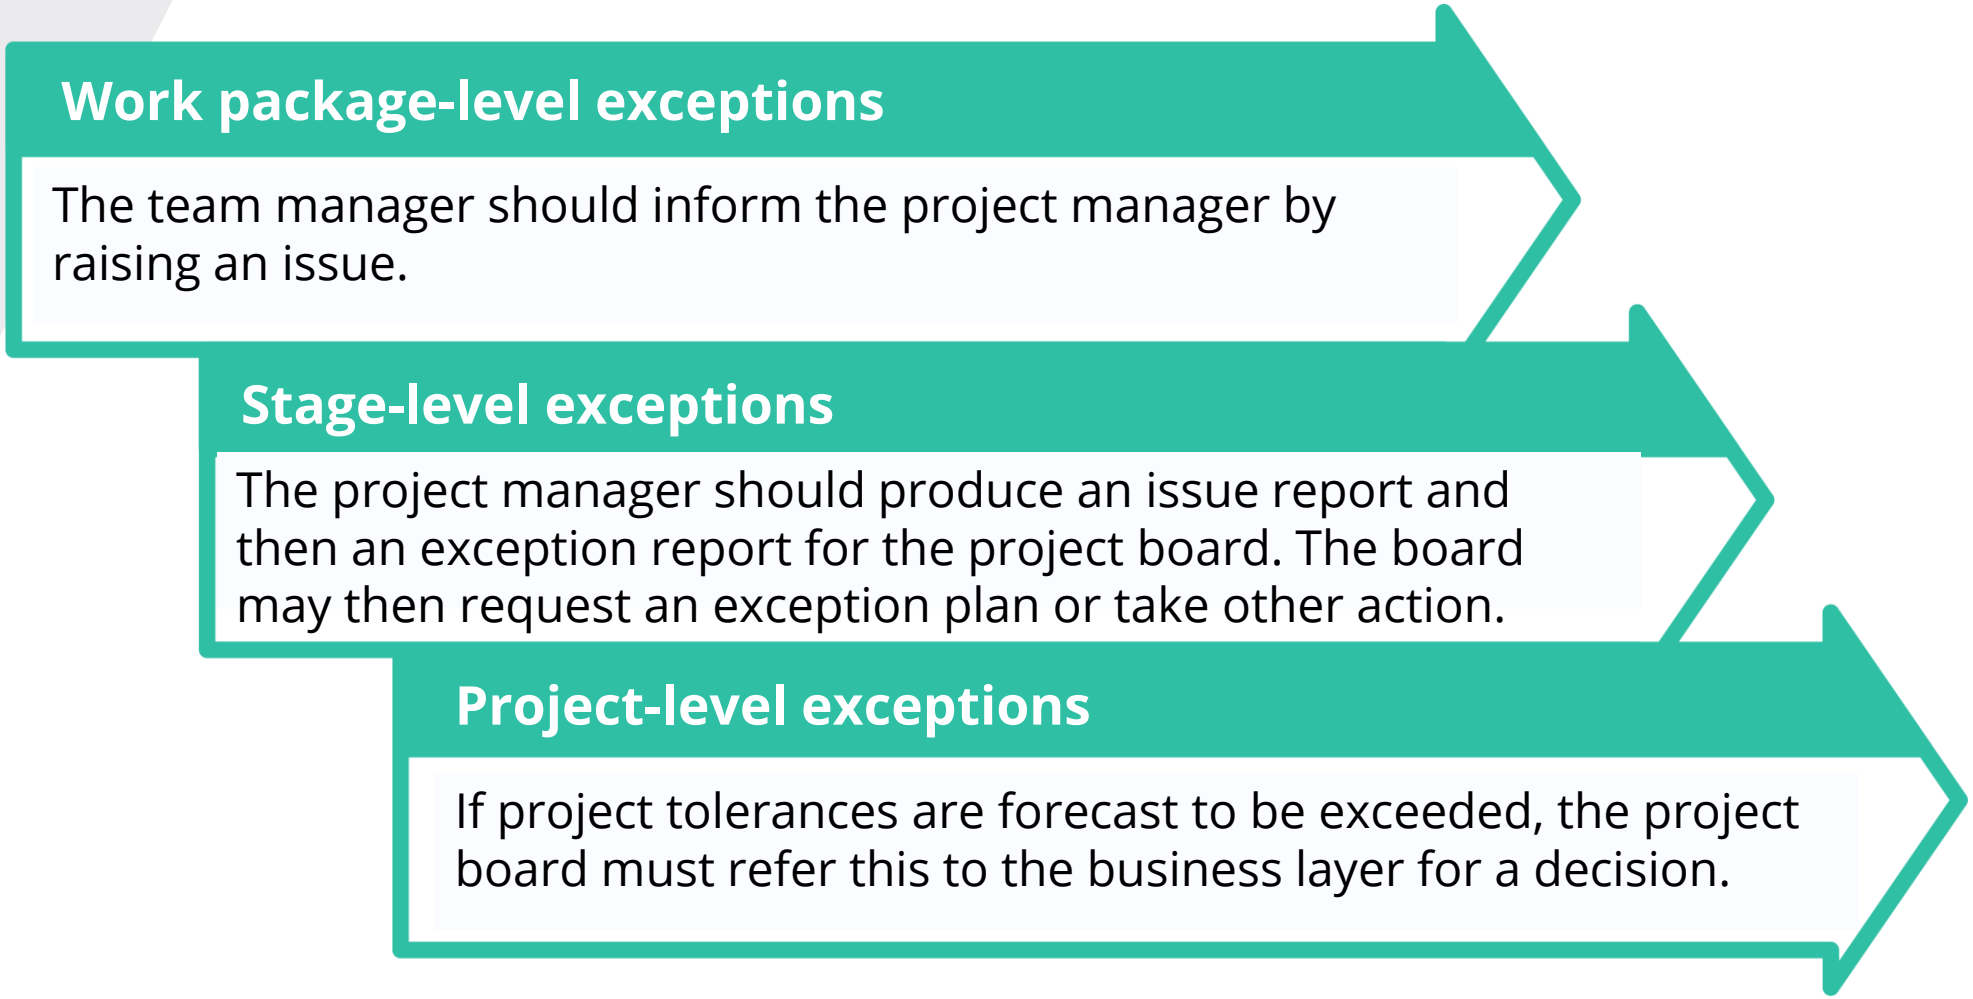

Copyright © 2025 PeopleCert International Limited.

PRINCE2 Project Management technique for exception management

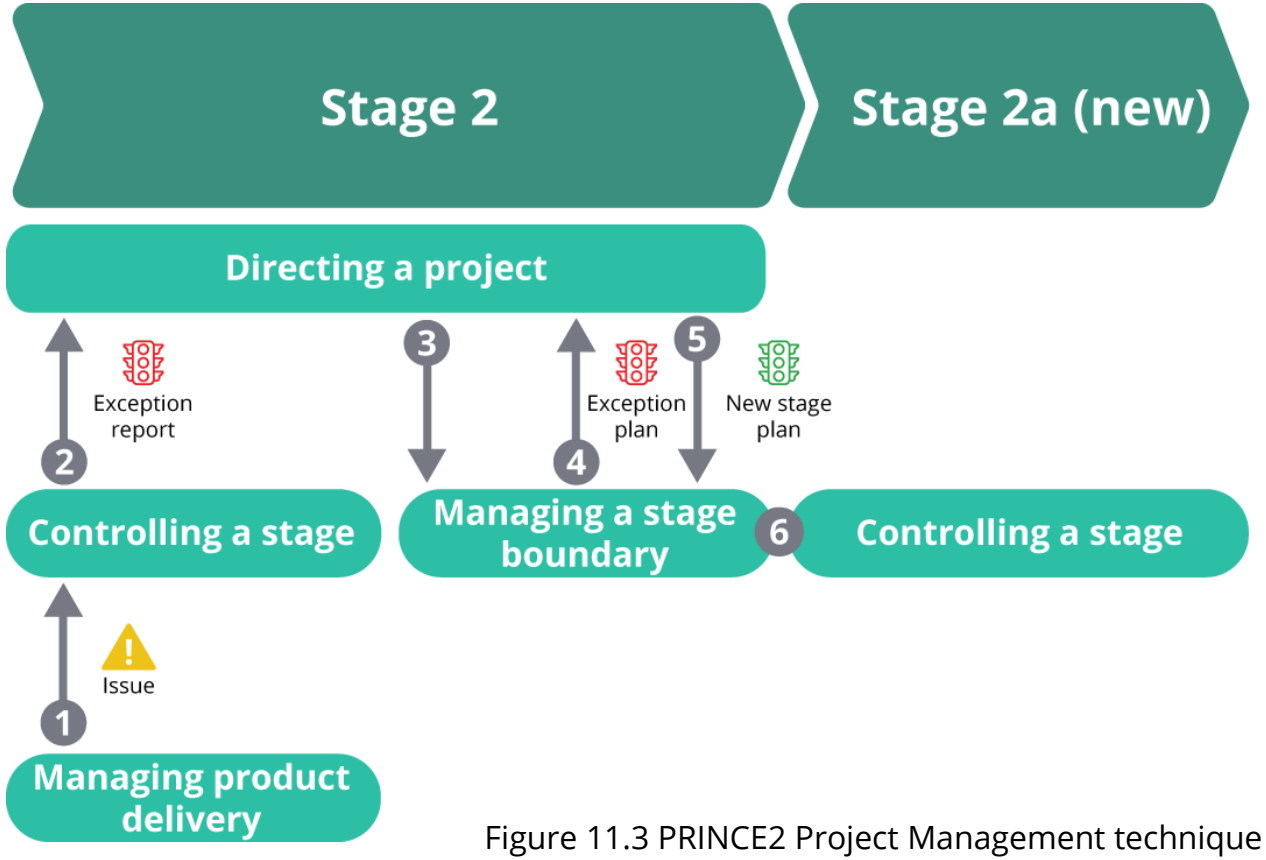


Figure 11.3 PRINCE2 Project Management technique for exception management

Copyright © 2025 PeopleCert International Limited.

Forecasting

What role does forecasting play in progress and exception management?



Copyright © 2025 PeopleCert International Limited.

Types of control

Event-driven controls

Control (decision-making) is an event-based activity.

Time-driven controls

Monitoring and reporting requires a time-based approach.



Copyright © 2025 PeopleCert International Limited.

Reports in PRINCE2 Project Management

Frequency of reporting should reflect required level of control.



PRINCE2 Project Management does not define report composition, format, or presentation.



Copyright © 2025 PeopleCert International Limited.

Lessons

A lesson is **information** to **facilitate the future** of the project or other projects and actively promote **learning from experience.** The experience may be **positive,** as in a successful test or outcome, or **negative,** as in a mishap or failure.

What did we expect to occur?

What actually happened?

What worked well and why?

What did not work well and why?

What needs to be done differently or be repeated?



Copyright © 2025 PeopleCert International Limited.

Logs and reports mini quiz

Complete the sentences using log or report:

1. A _____ may be a single document or a collection of separate logs.

2. A _____ provides a snapshot of certain aspects of the project.

3. How many logs does PRINCE2 Project Management have?



Copyright © 2025 PeopleCert International Limited.

Answers

Complete the sentences using log or report:

1. A **project log** may be a single document or a collection of separate logs.

2. A **report** provides a snapshot of certain aspects of the project.

3. How many logs does PRINCE2 Project Management have?

   Three.



Copyright © 2025 PeopleCert International Limited.

Use of data and systems

How do data and systems support progress management? What factors need to be considered?

- Allows for greater accuracy.
- Data analytics supports decision-making.
- Digital systems support work across multiple locations.
- Digital technology has supported data collection.
- Automation allows a professional focus on value-adding activities.
- Solutions must fit requirements and business maturity.

Copyright © 2025 PeopleCert International Limited.


Management products to support the progress practice

- Digital & Data management approach
- Daily log
- Lessons log
- Checkpoint report
- Highlight report
- Lessons report
- Exception report
- End stage report
- End project report




Copyright © 2025 PeopleCert International Limited

Applying the principles

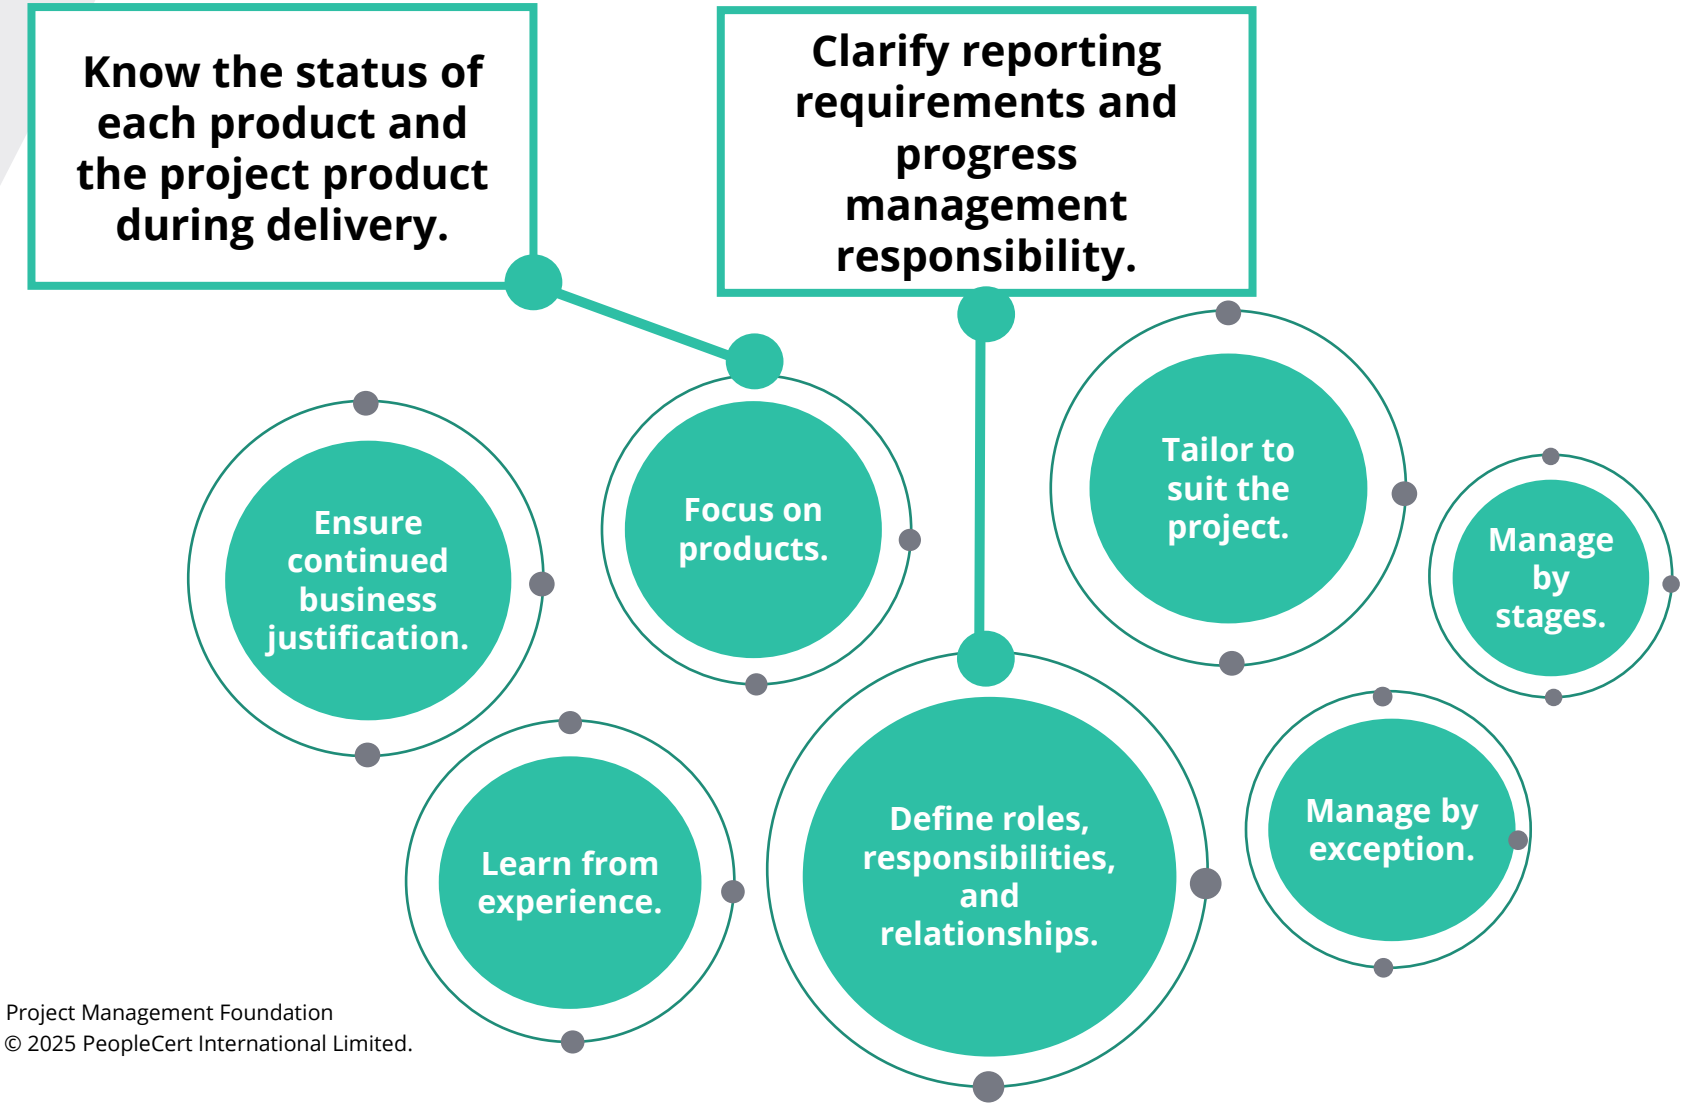

Copyright © 2025 PeopleCert International Limited.

Applying the progress practice

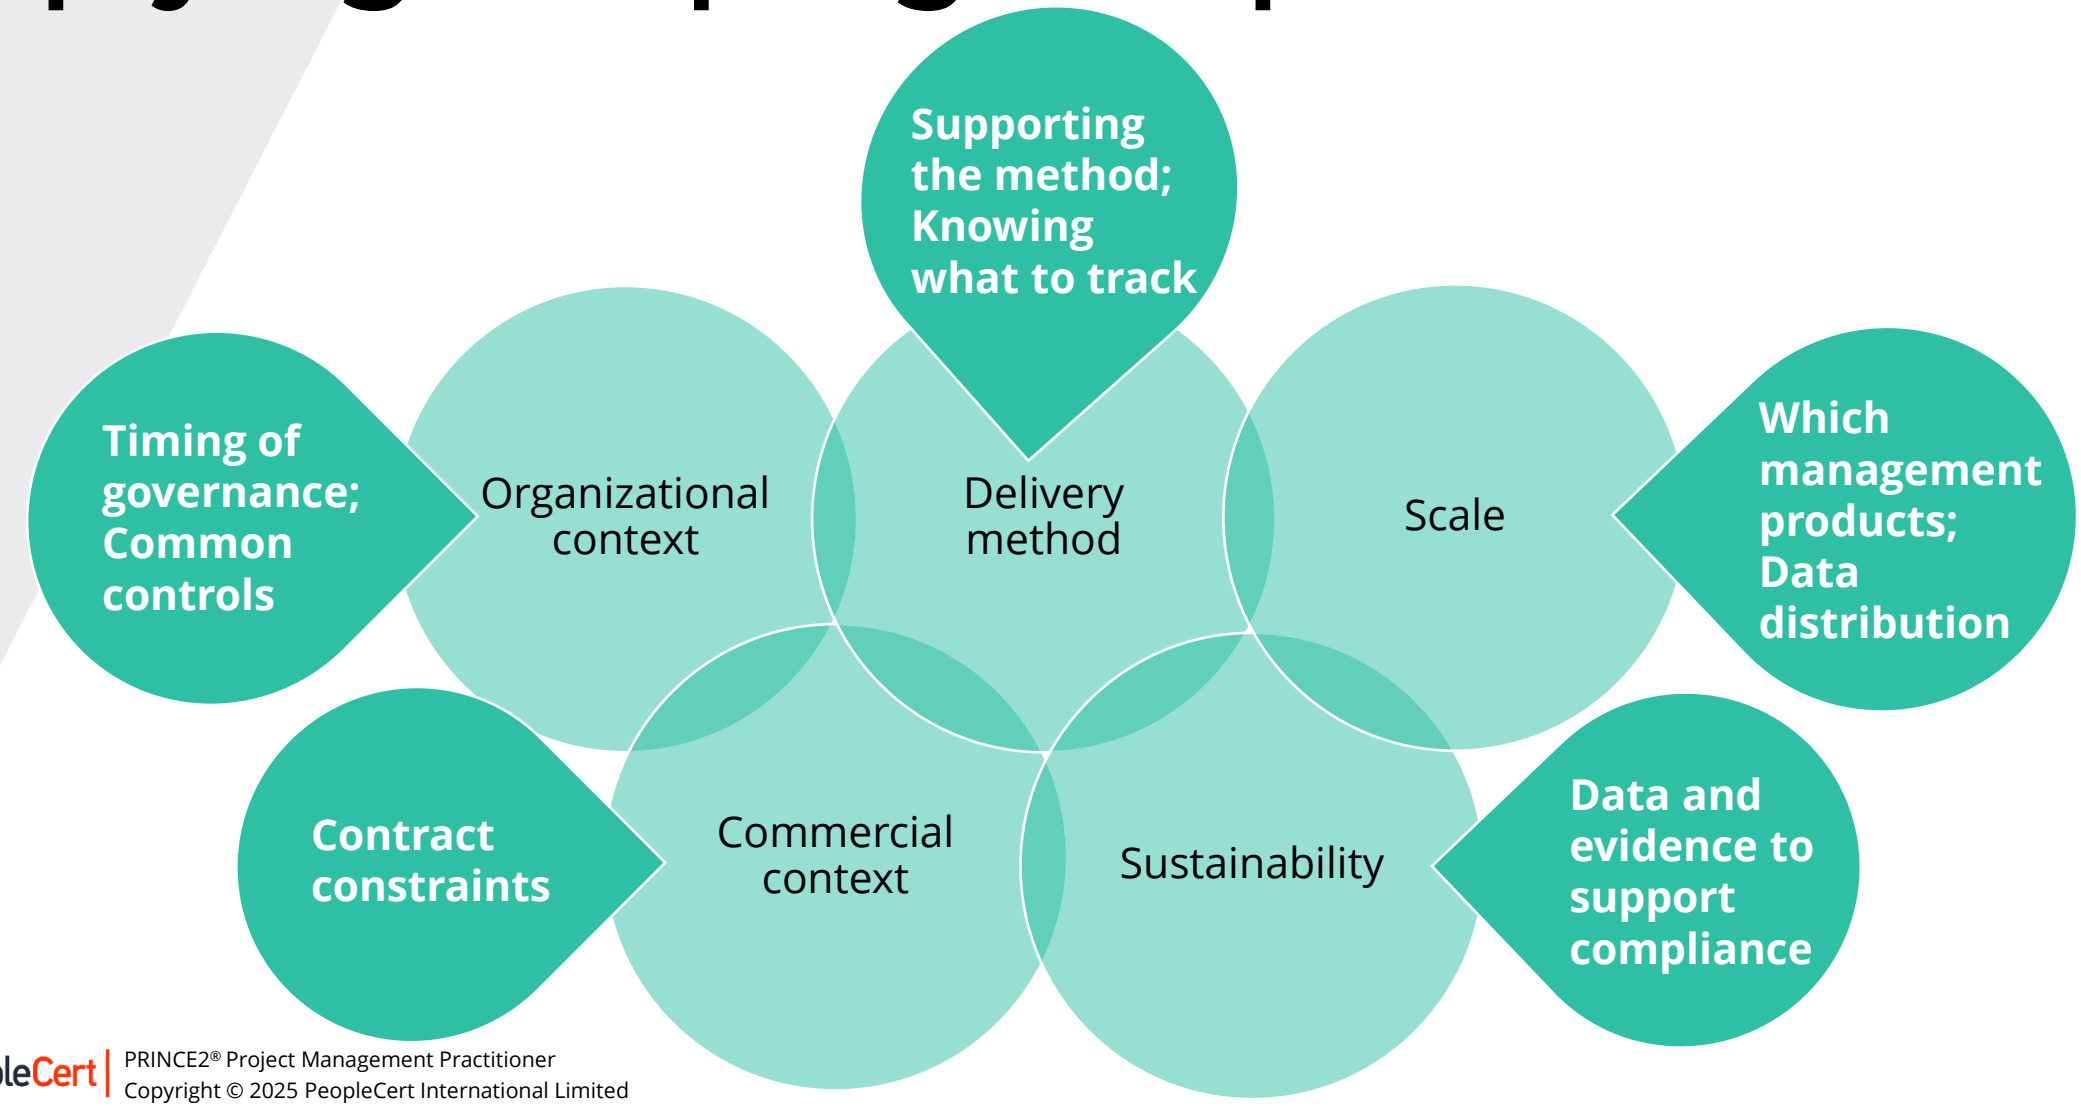

Copyright © 2025 PeopleCert International Limited

10 minutes



Progress

Activity 1

Matching terms (1/2)

Use the worksheet in your Learner Workbook.

Definition	Term
A Responsible for setting work package tolerances	**6** Project manager
B The result of change normally affecting real-world behaviour and/or circumstances	**5** Outcome
C To list all the products required of a plan and the status of those products	**9** Product register
D To provide a full and firm foundation for the initiation of the project	**10** Project Brief
E The process that controls the link between the project manager and the team manager	**3** Managing product delivery
F To report where tolerances have or are forecast to be breached	**8** Exception report
G Doing the minimum necessary to decide whether it is worthwhile to initiate the project	**1** Starting up a project
H Accountable for the quality of the products delivered	**7** Senior supplier
I The measurable improvement resulting from an outcome, perceived as an advantage by the investing organization	**2** Benefit
J A guiding obligation that ensures effective application and tailoring of PRINCE2 Project Management to any project	**4** Principle

Copyright © 2025 PeopleCert International Limited.

Matching terms (2/2)

Use the worksheet in your Learner Workbook.

Definition	Term
K Maintains information on all the identified threats and opportunities	**15** Risk register
L A problem, concern, change request, or off-specification	**18** Issue
M Any individual or group that can affect or be affected by the project	**20** Stakeholder
N The process that covers the activities of the project board	**17** Directing a project
O A diagram showing the sequence of production of products and interdependencies	**12** Product flow diagram
P The single point of accountability for the project	**14** Project executive
Q People from across the project ecosystem working together to achieve the project's objectives	**19** Collaboration
R The section of a project that the project manager is managing on behalf of the project board at any one time	**11** Stage
S To provide a progress and status update of the stage/project at pre-determined intervals	**16** Highlight report
T Providing services such as administration, planning support, and guidance on project tools	**13** Project support

Copyright © 2025 PeopleCert International Limited.

Module 13

Closing a project

Purpose of ‘closing a project’

The purpose of the process is to:

- provide a **fixed point** at which **acceptance** of the project product is **confirmed**
- recognize that **objectives** set out (or approved changes) have been **achieved**
- close the project in an **orderly way** where there is cause for a **premature close.**



Copyright © 2025 PeopleCert International Limited.

Objectives of ‘closing a project’

- Check user acceptance.
- Ensure that business is able to support the products.
- Review performance of the project.
- Assess any benefits.
- All open issues and risks are addressed.
- Ensure project is closed in an orderly way.



Copyright © 2025 PeopleCert International Limited.

Overview of ‘closing a project’

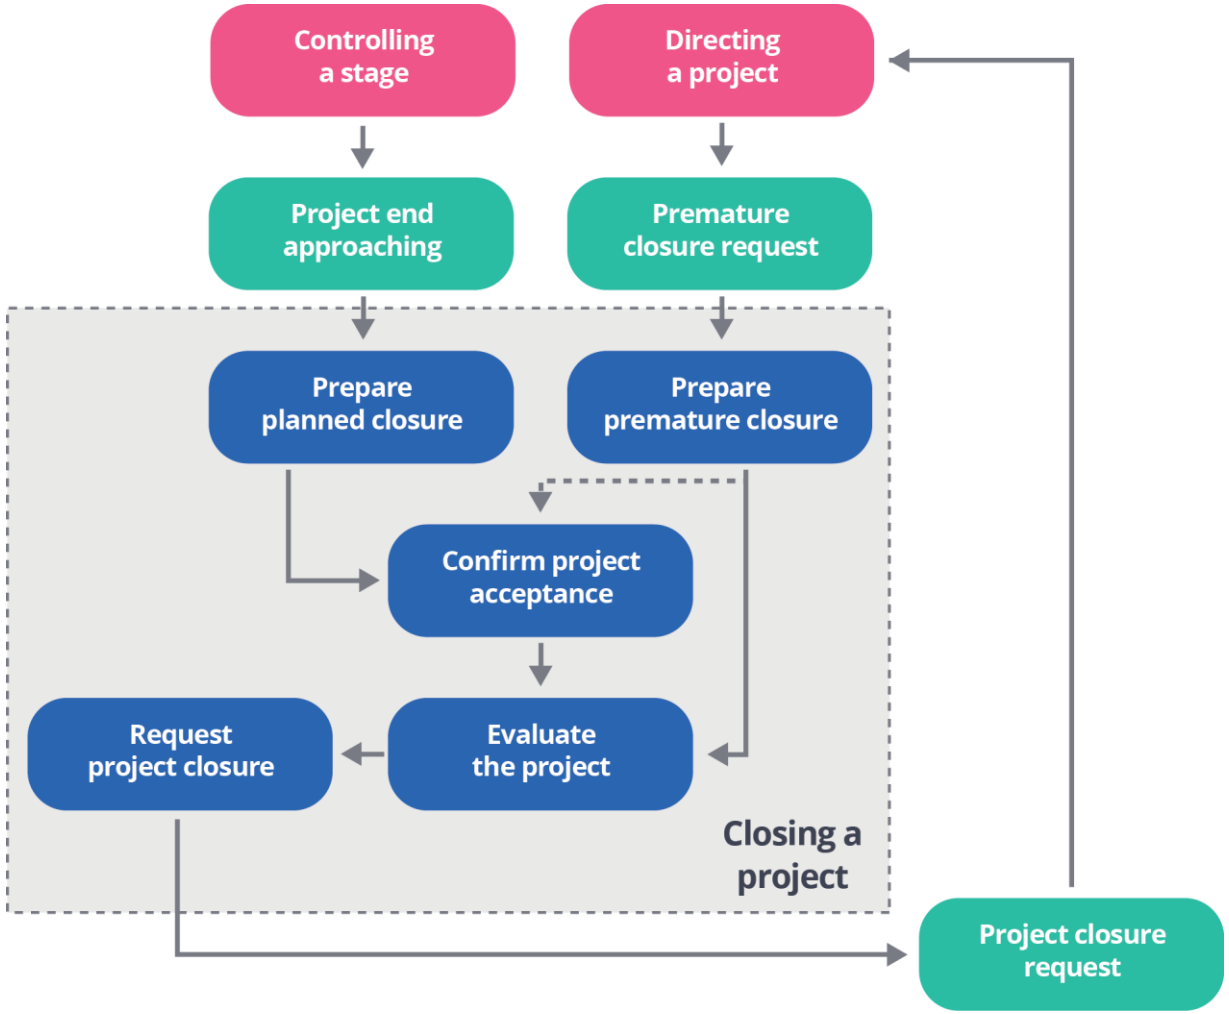


Figure 19.1 Overview of ‘closing a project’

Copyright © 2025 PeopleCert International Limited.

‘Closing a project’ roles and responsibilities

Table 19.2 RACI chart for ‘closing a project’

Activity	Business	Project executive	Senior user	Senior supplier	Project manager	Team manager	Project assurance	Project support
Prepare planned closure		A	C	C	R	C	C	C
Prepare premature closure		A	C	C	R	C	C	C
Confirm project acceptance		A	C	C	R	I	I	I
Evaluate the project		A	C	C	R	C	C	C
Request project closure	I	A	C	C	R	I	C	I

R = Responsible, A = Accountable, C = Consulted, I = Informed

Copyright © 2025 PeopleCert International Limited

Module 14

Directing a project

Purpose of ‘directing a project’

The purpose of the process of directing a project is to enable the **project board** to **be accountable** for the project’s **success,** by making key decisions and exercising overall control while **delegating day-to-day management** of the project to the **project manager.**



Copyright © 2025 PeopleCert International Limited.

Objectives of ‘directing a project’

Ensure authority to initiate the project and deliver the project product.

Ensure the project remains viable.

Ensure authority to close the project.

Provide management direction and control throughout the project.

Ensure the business layer has a connection to the project.

Ensure plans for realizing the post-project benefits are managed and reviewed.



Copyright © 2025 PeopleCert International Limited.

The project board...

ensures two-way communication with the business layer

engages with the business layer

provides unified direction and support to the project manager

manages by exception



ensures continued business justification



Informal advice and guidance

Copyright © 2025 PeopleCert International Limited.

Overview of ‘directing a project’ (1/2)


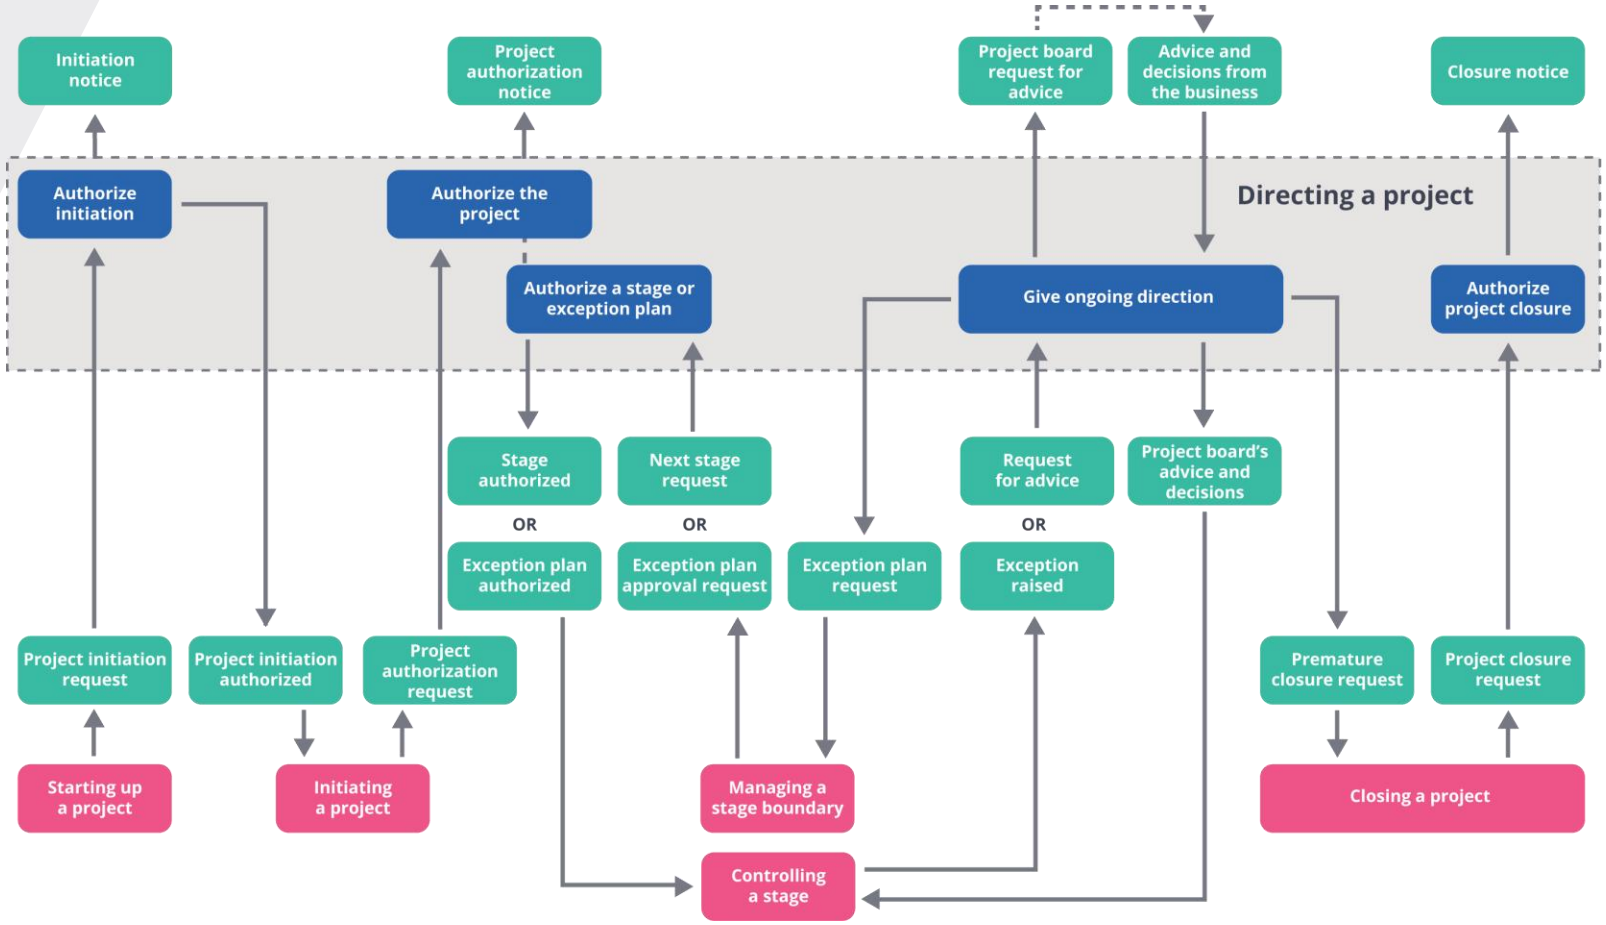


Figure 14.1 Overview of ‘directing a project’

Copyright © 2025 PeopleCert International Limited.

Overview of ‘directing a project’ (2/2)

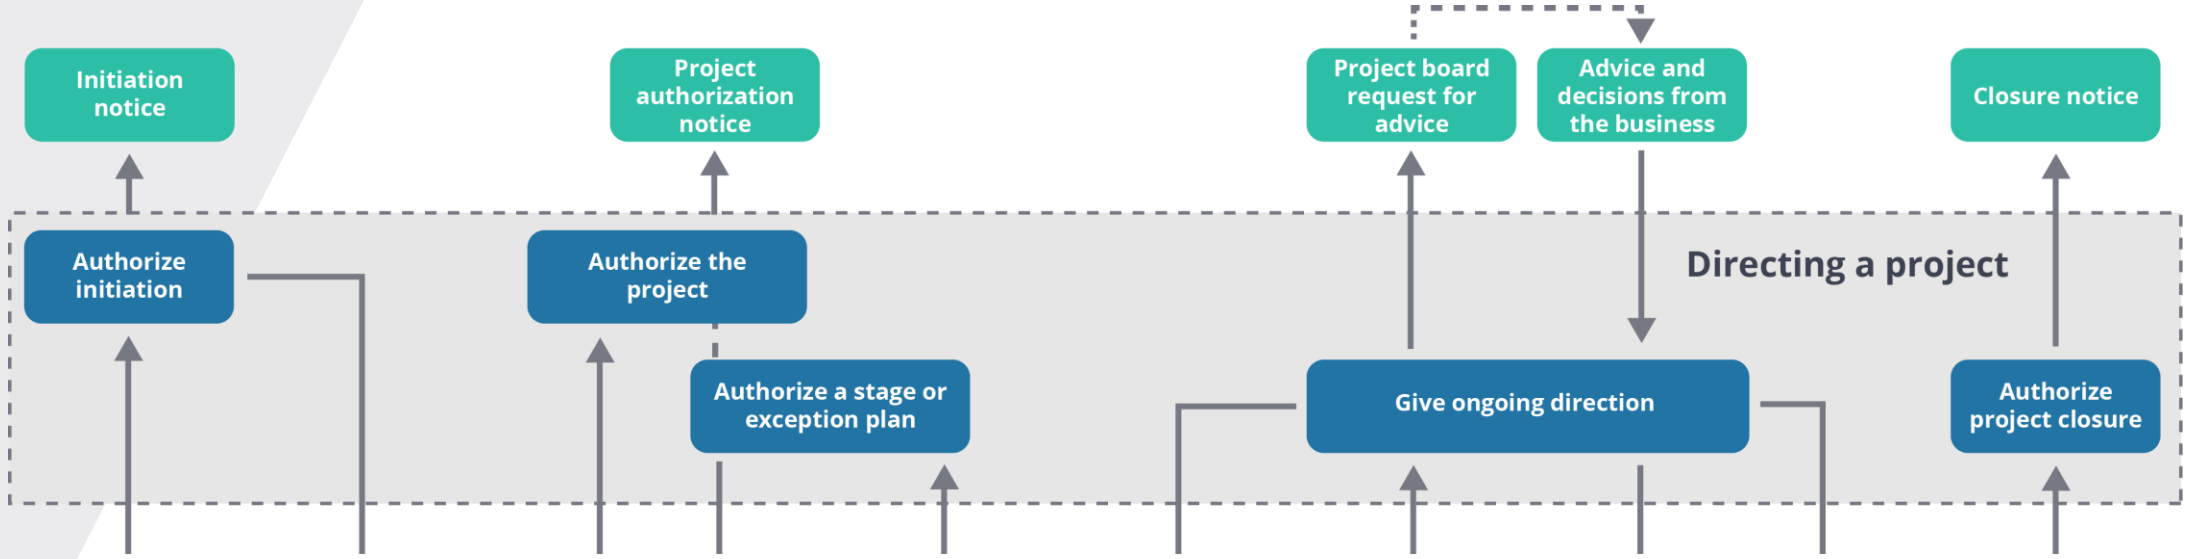

Adapted from Figure 14.1 Overview of ‘directing a project’

Copyright © 2025 PeopleCert International Limited.

‘Directing a project’ roles and responsibilities

Table 14.2 RACI chart for ‘directing a project’

Activity	Business layer	Project executive	Senior user	Senior supplier	Project manager	Team manager	Project assurance	Project support
Authorize initiation	I	A/R						
Authorize the project	I	A/R	C	C	I	I	C	I
Give ongoing direction	C	A/R[1]	R[2]	R[3]	C/I	I	C	I
Authorize a stage or exception plan	I	A/R	C	C	I	I	C	I
Authorize project closure	I	A/R	C	C	I	I	C	I

R = Responsible, A = Accountable, C = Consulted, I = Informed
R[1]: Business related; R[2]: User related; R[3]: Supplier related

Copyright © 2025 PeopleCert International Limited

20 minutes



Directing a project

Activity 1

Processes and activities

Make notes in your Learner Workbook.

Activity	Process
1. Establish project controls.	Initiating a project
2. Execute a work package.	Managing product delivery
3. Authorize project closure.	Directing a project
4. Assemble the project brief.	Starting up a project
5. Report highlights.	Controlling a stage
6. Prepare exception plan.	Managing a stage boundary
7. Evaluate stage status.	Controlling a stage
8. Evaluate the project.	Closing a project
9. Prepare the outline business case.	Starting up a project
10. Request next stage.	Managing a stage boundary
11. Prepare the project plan.	Initiating a project
12. Prepare premature closure.	Closing a project
13. Agree tailoring requirements.	Initiating a project
14. Authorize the project.	Directing a project
15. Authorize a work package.	Controlling a stage

Copyright © 2025 PeopleCert International Limited.

Any questions?



Copyright © 2025 PeopleCert International Limited.

PRINCE2®

PRINCE2® Project Management Practitioner

PeopleCert


Official Training Materials

What will be tested?

PRINCE2 Project Management Foundation



Analyse





Apply

PRINCE2 Project Management Practitioner



Copyright © 2025 PeopleCert International Limited

Exam overview

PRINCE2® Project Management projects

2 hours 30 minutes

70 marks available

PRINCE2® Project Management Practitioner exam

Multiple-choice and matching questions

Pass = 60% (42/70)

Open-book format

2 minutes per question



Copyright © 2025 PeopleCert International Limited

The exam

Scheduling

Materials

PRINCE2® PRACTITIONER

Results

Overview



Copyright © 2025 PeopleCert International Limited

The Scenario Booklet

Instructions

Project scenario

Stages

Additional information



Copyright © 2025 PeopleCert International Limited

Common mistakes

Time management

Attention to detail

Pressure



Copyright © 2025 PeopleCert International Limited

Principles

Learning outcome 1

Apply the PRINCE2 Project Management principles in context.

Analyse the application of PRINCE2 Project Management principles in context.

- Ensure continued business justification
- Learn from experience
- Define roles, responsibilities, and relationships
- Manage by stages
- Manage by exception
- Focus on products
- Tailor to suit the project

Copyright © 2025 PeopleCert International Limited

People

Learning outcome 2 (1/2)

Apply effective people management in successful projects.

Assess whether an approach to leadership and management of **teams** within a project, and people affected by a project, is appropriate.

Assess whether an approach to leadership and management of **change** within a project, and people affected by a project, is appropriate.



Figure 3.3 People are central to the method

Copyright © 2025 PeopleCert International Limited

Learning outcome 2 (2/2)

Apply effective people management in successful projects.

Apply the approach to the following:

- communications
- people central to the method.

Apply the key management products required to support the people element of projects:

- communication management approach
- change management approach.



Figure 3.3 People are central to the method


Copyright © 2025 PeopleCert International Limited

Practices

Learning outcome 3 (1/2)

Apply and tailor relevant aspects of PRINCE2 Project Management practices in context.

Demonstrating an understanding of specific elements for each PRINCE2 Project Management practice.

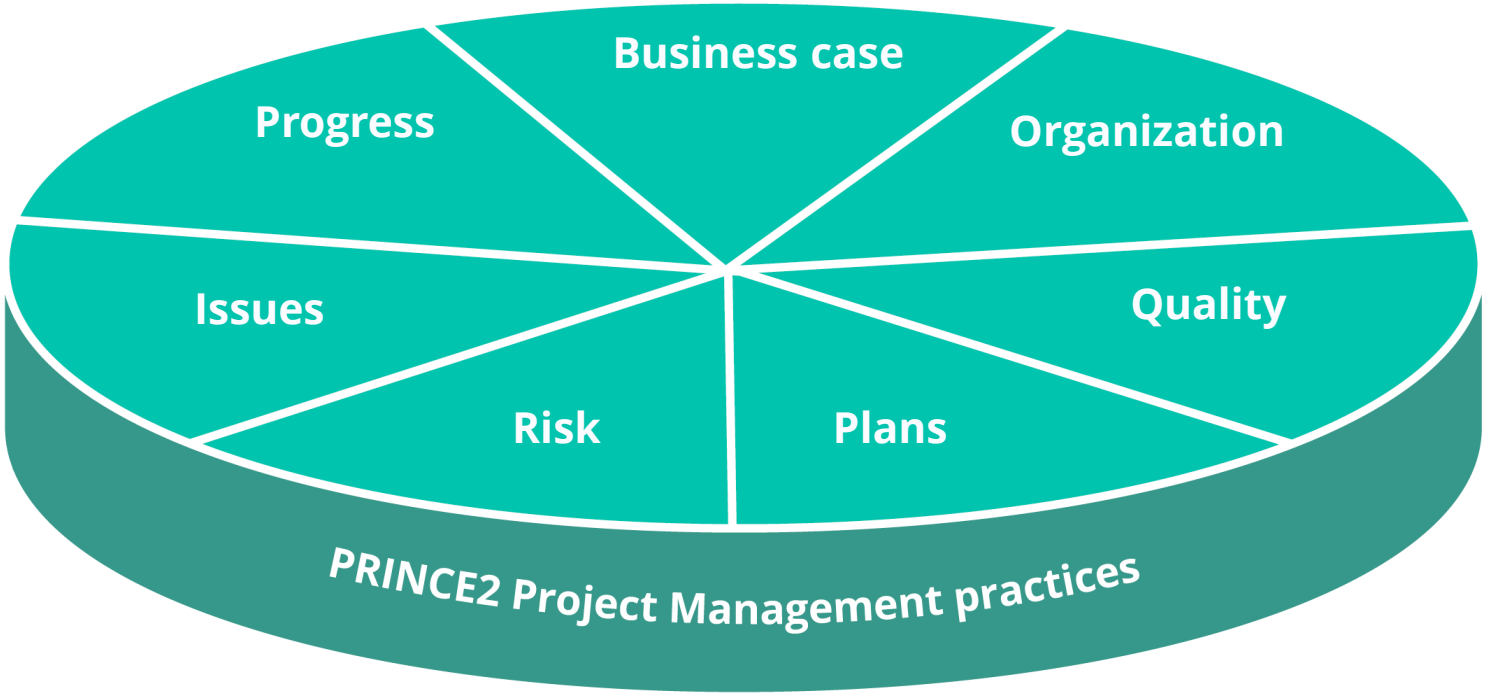


Copyright © 2025 PeopleCert International Limited

Learning outcome 3 (2/2)

Apply and tailor relevant aspects of PRINCE2 Project Management practices in context.

Assess whether an approach to applying each practice is effective and fit for purpose, taking into consideration: the PRINCE2 Project Management principles, the effective management and associated techniques of the practice, and tailoring to the project's environment/context.

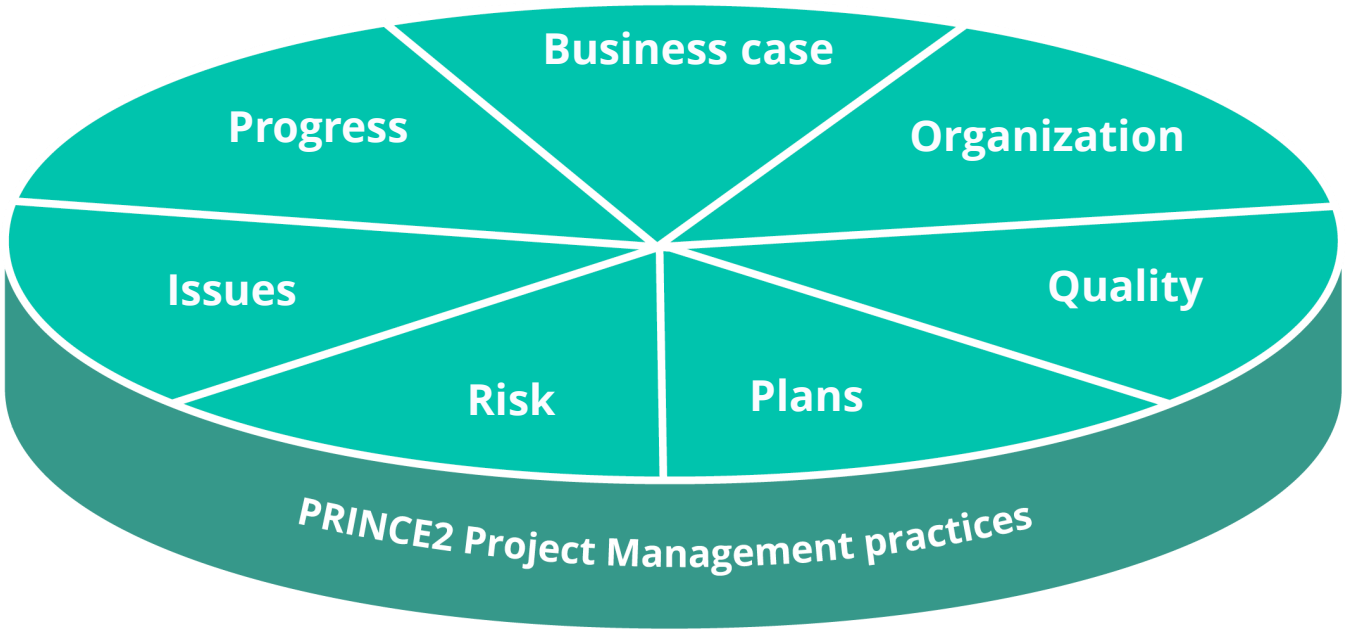

Copyright © 2025 PeopleCert International Limited

Practices: Chapter structure

- Purpose (X.1)
- Guidance (X.2)
- Techniques (X.3)
- Applying (X.4)
- Management products (X.5)
- Key roles (X.6)
- Key relationships (X.7)

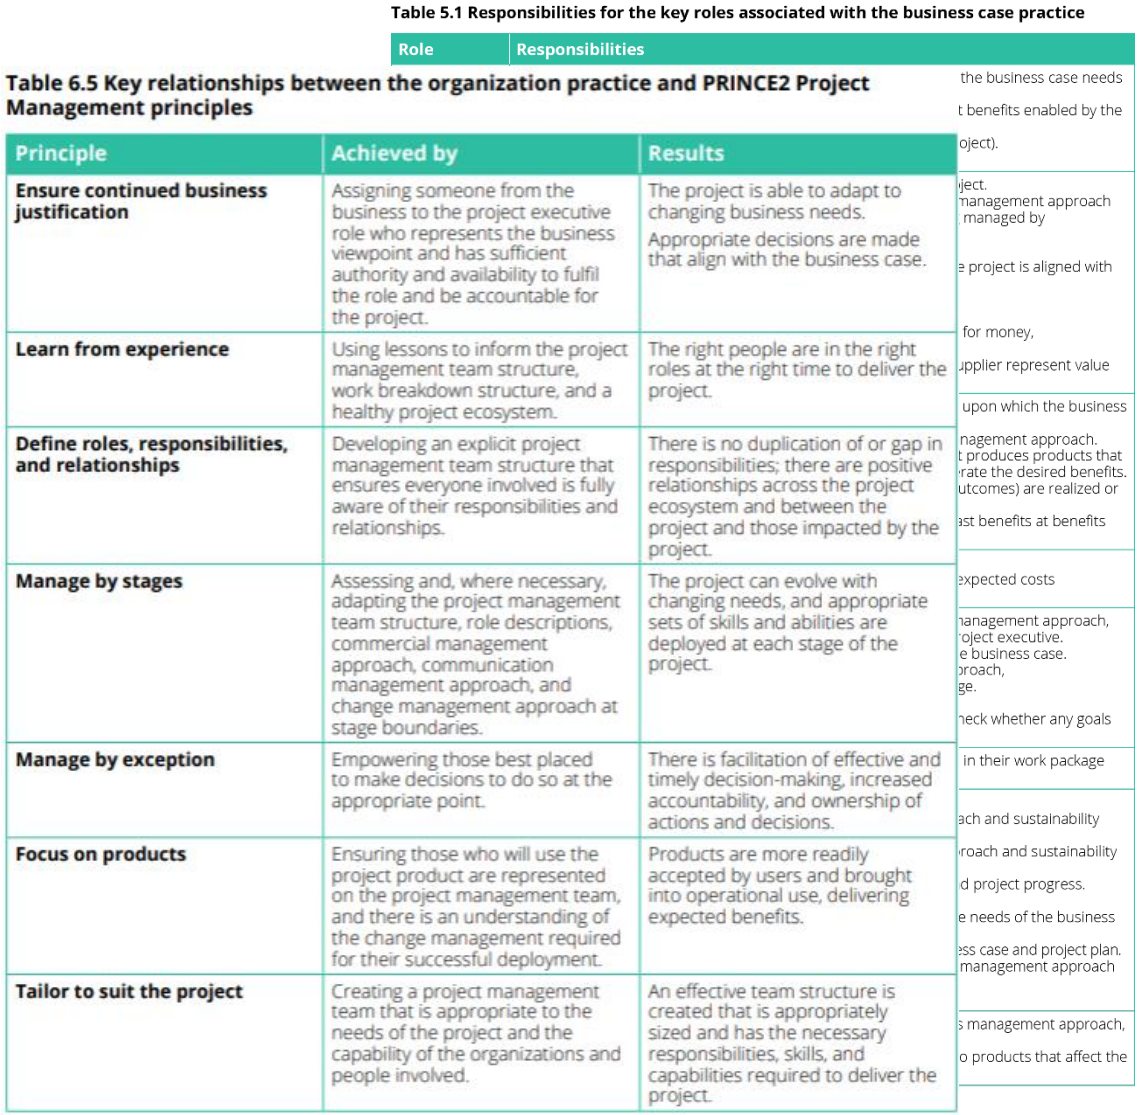


Table 5.1 Responsibilities for the key roles associated with the business case practice

Role	Responsibilities

Table 6.5 Key relationships between the organization practice and PRINCE2 Project Management principles

Principle	Achieved by	Results
Ensure continued business justification	Assigning someone from the business to the project executive role who represents the business viewpoint and has sufficient authority and availability to fulfil the role and be accountable for the project.	The project is able to adapt to changing business needs. Appropriate decisions are made that align with the business case.
Learn from experience	Using lessons to inform the project management team structure, work breakdown structure, and a healthy project ecosystem.	The right people are in the right roles at the right time to deliver the project.
Define roles, responsibilities, and relationships	Developing an explicit project management team structure that ensures everyone involved is fully aware of their responsibilities and relationships.	There is no duplication of or gap in responsibilities; there are positive relationships across the project ecosystem and between the project and those impacted by the project.
Manage by stages	Assessing and, where necessary, adapting the project management team structure, role descriptions, commercial management approach, communication management approach, and change management approach at stage boundaries.	The project can evolve with changing needs, and appropriate sets of skills and abilities are deployed at each stage of the project.
Manage by exception	Empowering those best placed to make decisions to do so at the appropriate point.	There is facilitation of effective and timely decision-making, increased accountability, and ownership of actions and decisions.
Focus on products	Ensuring those who will use the project product are represented on the project management team, and there is an understanding of the change management required for their successful deployment.	Products are more readily accepted by users and brought into operational use, delivering expected benefits.
Tailor to suit the project	Creating a project management team that is appropriate to the needs of the project and the capability of the organizations and people involved.	An effective team structure is created that is appropriately sized and has the necessary responsibilities, skills, and capabilities required to deliver the project.

Copyright © 2025 PeopleCert International Limited


Processes

Learning outcome 4 (1/2)

Apply and tailor relevant aspects of PRINCE2 Project Management processes in context.

Demonstrate an understanding of:

- the activities, inputs, and outputs
- recommended roles and responsibilities
- how the practices may be applied.

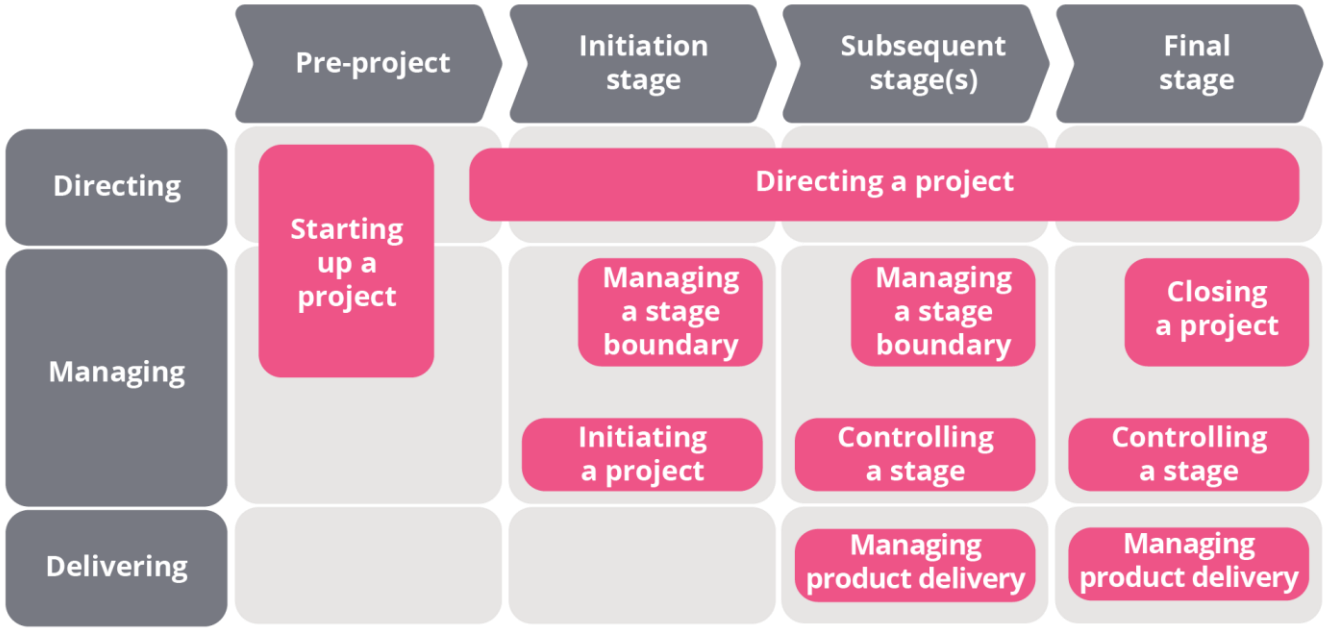

Note

- Starting up a project is used by both the directing and managing levels.
- There should be at least two stages, the first of which is the initiation stage.
- Managing a stage boundary is first used at the end of the initiation stage and repeated at the end of each subsequent stage except the final stage. It is also used to prepare exception plans, which can be done at any time including in the final stage.

Figure 12.1 The PRINCE2 Project Management processes


Copyright © 2025 PeopleCert International Limited

Learning outcome 4 (2/2)

Apply and tailor relevant aspects of PRINCE2 Project Management processes in context.

Assess whether the activities/actions, roles, and responsibilities of each process are effective and fit for purpose, taking into consideration:

- the environment/context
- the PRINCE2 Project Management practices
- the purpose and objectives of the process.

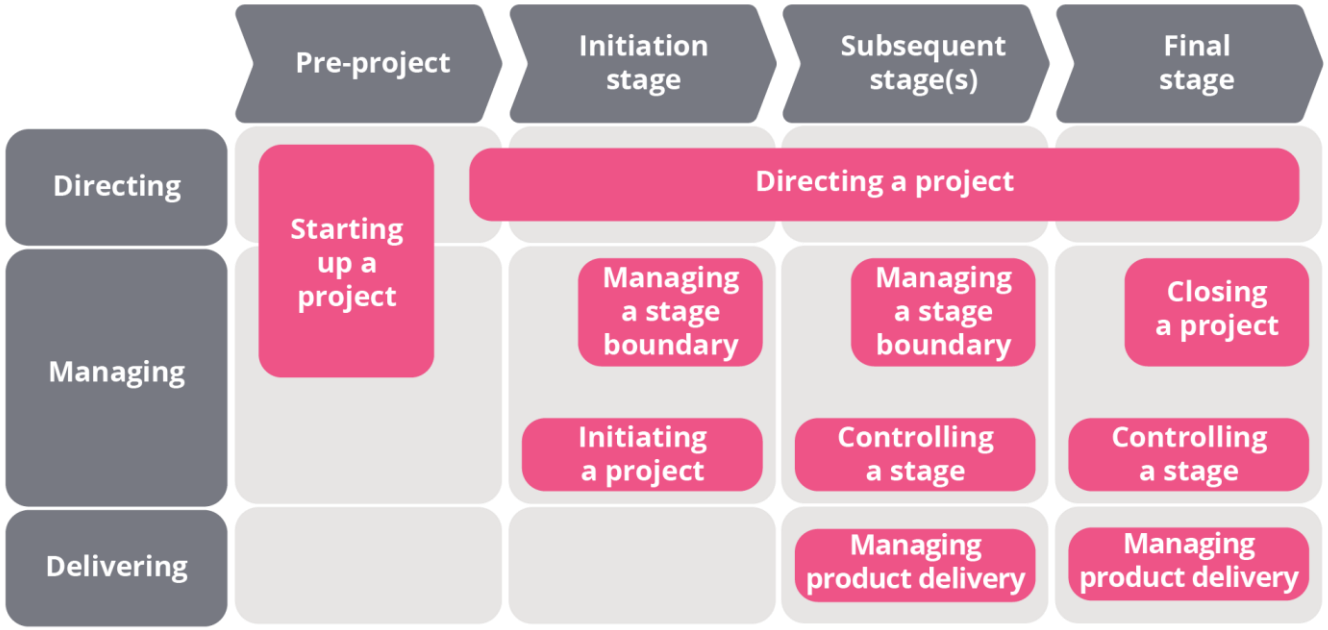

Note

- Starting up a project is used by both the directing and managing levels.
- There should be at least two stages, the first of which is the initiation stage.
- Managing a stage boundary is first used at the end of the initiation stage and repeated at the end of each subsequent stage except the final stage. It is also used to prepare exception plans, which can be done at any time including in the final stage.

Figure 12.1 The PRINCE2 Project Management processes

Copyright © 2025 PeopleCert International Limited

Processes: Chapter structure

- Purpose (X.1)
- Guidance (X.2)
- Techniques (X.3)
- Applying (X.4)
- Management products (X.5)
- Key roles (X.6)
- Key relationships (X.7)

Table 15.1 Inputs,

Input
Project initiation auth (triggers this process
Project brief (review)
Project log (check)
Project product desc (review)
Stage plan (initiation)
Outline business cas
Business case
Project brief
Project product desc
Project plan
Management approa
Project initiation doc

Table 13.2 RACI chart for 'starting up a project'

Activity	Business layer	Project executive	Senior user	Senior supplier	Project manager	Team manager	Project assurance	Project support
Appoint the project executive and project manager	A/R[1]	R						
Assess previous lessons	C	A			R			
Prepare the outline business case	C	A/R	C[3]	C[3]	R			
Appoint the project management team	A	R						
Select the project approach		A	C	C	R	C[2]	C	
Assemble the project brief		A	C	C	R		C	C
Plan the initiation stage		A	C	C	R	I[2]	C	C
Request project initiation		A	C	C	R	I[2]	C	I

R = Responsible, A = Accountable, C = Consulted, I = Informed

A/R[1]: Business is accountable for the appointment of the project executive and the project manager. They are also responsible for appointing the project executive.

C[2] / I[2] : If any team managers have been identified when designing and appointing the project management team, then it is good practice to consult them on the project approach and inform them of key details in the stage plan for the initiation stage should they be involved in that stage.

C[3] if/when appointed

Copyright © 2025 PeopleCert International Limited

Any questions?



Copyright © 2025 PeopleCert International Limited.
